METERSQUARE ERP

User Guide

Complete guide to every role, screen and process: from estimating and BOQ approval to purchasing, the M2 Store, site delivery, returns, assets, labour and payroll.

Version 14 October 2026
For all MeterSquare users

Contents

Getting Started **5**
Roles in MeterSquare 5
How the main process flows 6
Signing in 6
Finding your way around 8
Account menu 10
Profile Settings 10
Notifications 10
Support (Bug Register) 11
Ask AI (Structo) 13
Working in more than one role 13
Admin **16**
Admin Dashboard 16
User Management 17
Role Access (temporary extra roles) 20
Signature Upload 25
CC & Email Settings 26
Payroll Processing 26
Security Dashboard 27
Viewing the app as another role 28
Estimator **29**
The BOQ journey at a glance 29
Estimator Dashboard 30
Projects & BOQ Management 30
How to create a project 31
How to create a BOQ 32
How to send a BOQ to the Technical Director 35
How to send a BOQ to a Project Manager for review (optional) 35
When the TD approves or rejects 36
How to fix a BOQ the TD rejected (internal revision) 37
How to send a BOQ to the client 38

How to record the client's answer 39
How to make a client revision 39
How to cancel a BOQ (client does not proceed) 41
After the client approves 41
Viewing and downloading a BOQ 42
BOQ statuses 42
Purchase Requests (material requests needing pricing) 43
Technical Director 45
Technical Director Dashboard 45
Project Approvals 46
Purchase Orders: approving vendor selections 51
Purchase Orders: Return Approvals 52
Disposal Approvals 53
Vendor Management 54
Purchase Comparison 55
Profit Comparison 55
Role Access 56
Project Manager and MEP Supervisor 57
Dashboard 57
My Projects 58
Material Purchase (change requests) 62
Asset Requisition Approvals 68
Labour: Requisition Approvals 68
Labour: Attendance Lock 69
Site Engineer 71
Site Engineer Dashboard 71
Projects 72
Material Purchase (requesting extra materials) 73
Material Receipts (deliveries and returns) 76
Site Assets (tools and equipment) 78
Labour 81
Procurement (Buyer) 84
From request to site: the purchase flow 85

Buyer Dashboard 85
Purchase Orders 86
How to select a vendor and send for TD approval 87
How to get materials from the M2 Store 89
How to edit negotiated prices 90
How to send the LPO to the vendor 90
How to complete a purchase 91
Vendor Returns 92
Vendors 94
Store 96
Production Manager (M2 Store) 98
Material flow through the M2 Store 99
Production Dashboard 99
Main stock and backup stock 100
Materials Catalog 101
Stock In (receiving into the store) 102
Stock Out (material requests and delivery notes) 105
Receive Returns (material returns from site) 108
Repair (materials) 109
Disposal (materials) 110
Returnable Assets 110
Labour Registry 113
Assign Workers 114
Assets and Labour: End-to-End Flows 116
Asset requisition: from request to return 116
Labour: from requisition to payroll 117
Material returns from site 118
Vendor delivery problems 118
Glossary and FAQ 119
Glossary 119
Frequently asked questions 120

Getting Started

MeterSquare is the company's construction ERP. It covers the full life of a project: estimating and the Bill of Quantities (BOQ), approvals, project assignment, site material requests, purchasing from vendors, the M2 Store warehouse, deliveries to site, returns, assets, labour and payroll.

Each person signs in with a **role**. The role decides which menus, pages and approvals you see.

Screenshots in this guide show sample data and may differ slightly from your screen.

Roles in MeterSquare

Role	Main job in MeterSquare
Admin	Manages users, role access, signatures, email CC settings, security and payroll. Can view the app as any other role.
Technical Director (TD)	Approves BOQs, assigns Project Managers and MEP Supervisors to projects, approves vendors, vendor selections, disposals, returns and day extensions.
Estimator	Creates projects and BOQs, sends BOQs to the TD and to the client, handles revisions, approves purchase requests.
Project Manager (PM)	Runs assigned projects: assigns Site Engineers and BOQ items, approves material purchase requests from site, approves asset and labour requests, locks attendance.
MEP Supervisor	Same screens as the Project Manager, for MEP (mechanical, electrical, plumbing) scope on the projects they are assigned to.
Site Engineer (SE)	Works on site: views assigned items, requests materials, confirms deliveries, returns unused materials, requests labour and assets, records attendance.
Procurement (Buyer)	Buys materials: selects vendors, sends purchase orders (LPO), completes purchases, manages vendors and store items, handles vendor returns.
Production Manager	Runs the M2 Store: materials catalog, stock in/out, delivery notes to site, returns, repair and disposal, returnable assets, labour registry.

How the main process flows

The core project flow, from estimate to site:

1	**Estimator**	Creates the project and the BOQ, then sends it to the Technical Director
2	**Technical Director**	Approves the BOQ (or sends it back with a reason)
3	**Estimator**	Sends the approved BOQ to the client and records the client's decision
4	**Technical Director**	Assigns a Project Manager (and MEP Supervisor if needed)
5	**Project Manager**	Assigns Site Engineers and allocates BOQ items to them
6	**Site Engineer**	Requests extra materials when site needs them (Material Purchase)
7	**Project Manager**	Approves the request (the Estimator prices any new materials)
8	**Procurement**	Selects a vendor; the Technical Director approves the vendor
9	**Procurement**	Sends the purchase order (LPO) and completes the purchase
10	**Production Manager**	Inspects the delivery at the M2 Store and dispatches it to site
11	**Site Engineer**	Confirms delivery, and returns unused material to the store

Each step is described in detail in the chapter for that role.

Signing in

There are no passwords. You sign in with a one-time code (OTP) sent to your email.

How to sign in with email

1. Open MeterSquare. The page shows **Welcome to MeterSquare**.
2. In **Select Your Role**, choose your role (Admin, Technical Director, Estimator, Project Manager, Production Manager, MEP Supervisor, Site Engineer or Procurement).
3. Type your email in **Email Address**.
4. Click **Send OTP**. You will see **OTP Sent Successfully!**. Check your email.
5. On the **Enter OTP** screen, type the 6-digit code. It verifies automatically when all 6 digits are entered, or click **Verify & Login**.
6. You land on your role's dashboard.

To change the email, click ← **Back to email**.

Resending the code

After sending, the screen shows **Resend OTP in 30s**. When the countdown ends, click **Resend OTP**.

Site Engineer: sign in with phone (SMS)

When you choose **Site Engineer**, a **Login Method** choice appears: **Phone (SMS)** or **Email** (Email is the default).

1. Choose **Phone (SMS)**.
2. Pick the country code (default +971 UAE) and type your phone number. The number of digits must match the country (for example 9 digits for UAE, 10 for India).
3. Click **Send OTP** and enter the code from the SMS.

OTP rules

- The code is 6 digits and expires after **5 minutes**.
- After **5 wrong codes**, the account is locked for **30 minutes**: "Account temporarily locked due to too many failed attempts".
- A sign-in lasts **10 hours**. After that you are taken back to the login page.

Sign-in messages and what they mean

Message	What to do
Please fill all fields	Choose a role and enter your email (or phone).
Invalid email / Invalid phone number	Check the format or number of digits.
Email not found / Phone not found	The email is wrong, **or the selected role is not your role**, or your account is inactive. Check the role you picked.
Invalid OTP	The code is wrong or expired. Request a new one.
Account Blocked	An administrator blocked your account. Contact your administrator.

Signing out

Open the account menu at the bottom of the sidebar and click **Sign Out**. Signing out in one browser tab signs you out of the other tabs too.

If an administrator ends your session, your next action takes you to the login page.


Finding your way around

The sidebar

- The sidebar on the left lists your role's menu. It always starts with **Dashboard**.
- Items with an arrow have sub-menus. Click to expand.
- Drag the sidebar edge to resize it; double-click the edge to reset. When it is narrow, it shows icons only and sub-menus open on hover.
- On mobile, open the sidebar with the menu button.

Your dashboard

Every role has a dashboard with counters and charts for its own work (for example pending approvals, purchase orders, deliveries or stock alerts). A clock and today's date appear at the top right of dashboard pages.

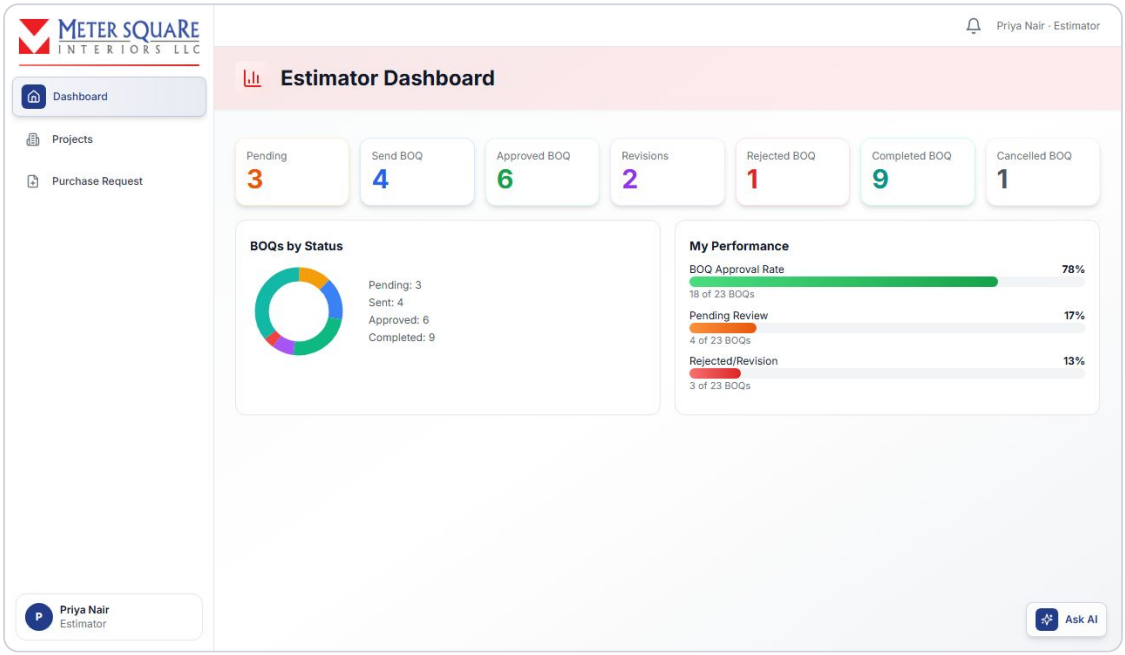

The sidebar and a dashboard (Estimator shown)

Sidebar menu by role

Role	Menu
Admin	Dashboard, User Management, Role Access, Signature Upload (Signatures, CC & Email Settings), Payroll Processing, Security Dashboard, plus "view as" role links
Technical Director	Dashboard, Project Approvals, Disposal Approvals (Material Disposal, Asset Disposal), Vendor Management, Purchase Orders (All Orders, Return Approvals), Purchase Comparison, Profit Comparison, Role Access
Estimator	Dashboard, Projects, Purchase Request
Project Manager	Dashboard, My Projects, Material Purchase, Asset Requisition Approvals, Labour (Requisition Approvals, Attendance Lock)
MEP Supervisor	Same as Project Manager
Site Engineer	Dashboard, Projects, Site Assets, Material Receipts, Material Purchase, Labour (Labour Requisition, Arrival Confirmation, Attendance Logs)
Procurement	Dashboard, Purchase Orders, Vendors, Store (Store Items, Material Transfer, Raw Materials), Vendor Returns (Rejected Deliveries, Return Requests)
Production Manager	Dashboard, Inventory Management (Materials Catalog, Stock In, Stock Out, Receive Returns, Repair, Disposal), Returnable Assets (Asset Catalog, Stock In, Stock Out, Process Returns, Repair, Disposal), Labour (Labour Registry, Assign Workers)

Account menu

Click your name at the bottom of the sidebar to open the account menu:

- **Status**: switch between **Online** and **Offline**. You are set Online automatically when you sign in and Offline when you sign out. Others see this status (for example when choosing a buyer).
- **SWITCH ROLE**: only shown if you have been given extra roles (see below).
- **Profile Settings**: your profile page.
- **Support**: report a problem or request a change.
- **Sign Out**.

Profile Settings

1. Open the account menu and click **Profile Settings**.
2. Click **Edit Profile**.
3. Update **Full Name**, **Email Address**, **Phone Number** or **Department**. Full name and email are required.
4. Click **Save Changes**.

The Profile tab also shows your role, account status and joined date.

The page has three more tabs: **Security**, **Preferences** and **Activity**.

- Sign-in uses one-time codes sent to your email (or phone), so there is no password to manage.
- **Two-Factor Authentication** on the **Security** tab shows **Not Enabled**, because every sign-in already needs a one-time code.
- You can also sign out from the **Security** tab.

Notifications

The notification bell

- The bell at the top right shows a red number for unread notifications. An orange dot means something urgent is unread.
- Click the bell to open the **Notifications** panel. Use the **All** and **Unread** tabs.
- Click a notification to mark it read and open the related page.

- Buttons: **Mark all as read**, **Clear All**, **View All** (full page).
- Each notification shows its priority (urgent, high, medium, low), time and sender.

The full Notifications page

Click **View All** in the panel to open it. You can:

- search, filter by priority and category, and sort.
- tick notifications and use **Mark as Read** or **Delete**.
- switch between the **All**, **Unread** and **Archived** (read) tabs.

Desktop notifications

- New notifications arrive instantly as a pop-up in the app, and as a desktop notification if your browser allows it.
- To turn desktop notifications on, click **Enable desktop notifications** (the bell icon in the panel) and allow it in the browser.
- High and urgent desktop notifications stay on screen until you click them.

Email

- Emails for most workflow steps (approvals, assignments, purchase orders) are sent only when you are **Offline**. If you are **Online**, you get the notification in the app only. Set your status in the account menu.
- Role access emails (access granted, paused, resumed, changed, removed or ended) are always sent.
- Some account emails are also always sent, for example when your account is activated, deactivated, blocked or unblocked.

Support (Bug Register)

Use Support to report a problem or request a new feature.

How to raise a support ticket

1. Open the account menu and click **Support**. The **Bug Register** page opens.
2. Click **New Ticket**. Your name, role and email are filled in automatically.
3. Choose a **Ticket Type**: Bug, Issue, Implementation or Feature Request.
4. Choose a **Priority**: Low, Medium, High or Critical.

5. Enter a **Title** and describe the problem in **Current Concern**.
6. Add at least one screenshot or file with **Upload Files** (required; up to 10 MB each; images, PDF, Word, Excel, text).
7. Optional: **Concern Implementation** (what you would like changed), **Implementation Files**, **Description**.
8. Click **Submit Ticket**. To finish later, click **Save as Draft** (only a title is needed).

Following up a ticket

- Tickets with new replies show **N new** and appear first.
- Open a ticket to see the development team's updates, response and resolution.
- Once a ticket is approved, use **Comments & Follow-ups** to add comments and files.
- When a ticket is **Resolved**, check that it works and click **Confirm & Close**.
- Draft tickets can be edited, submitted or deleted.

Ticket statuses

Status	Meaning
Draft	Saved, not yet submitted
Submitted	Sent to the development team
In Review	Being looked at
Approved	Accepted for work
Rejected	Not accepted (reason shown)
In Progress	Being worked on
Pending Deployment	Fix ready, waiting for release
Resolved	Fixed. Please verify and close
Closed	Finished

You are notified when your ticket is approved, rejected, resolved, put in review or in progress, or gets a comment.

Ask AI (Structo)

The **Ask AI** button sits at the bottom right of every page except **Support**. It opens **Structo**, the MeterSquare assistant. Structo answers how-to questions from this user guide, for the role you are working in. It cannot see or change your projects, BOQs or other records.

How to ask a question

1. Click **Ask AI**. The Structo panel opens.
2. Type your question, for example "How do I return unused material?", and send it.
3. Read the answer. Where it helps, the answer includes a screenshot of the screen from this guide (sample data); click it to open it full size. Use the full-screen button to make the panel larger, and the new-conversation button to start again.
4. Click the ✕ at the top of the panel to close it.

The **User guide (PDF)** link at the bottom of the panel downloads this full guide.

Hiding the button

- Click the small ✕ on the **Ask AI** button to hide it.
- A thin handle stays on the right edge of the screen. Click it to show the button again.
- Your choice is remembered.

Working in more than one role

An Admin or Technical Director can give you **temporary access to another role**, for example an Estimator who also works as a Project Manager for two weeks. Your own role never changes.

Two kinds of access

- **Fresh role**: you start as a new person in that role, with no projects. Projects are assigned to you in that role while your access is active, and you appear in that role's selection lists with a small **Granted · until** tag. Your Admin or TD may give you only some of the role's menus: you then see only those menus (and the dashboard), and the email you receive lists them.
- **Same as existing user**: you see and work on exactly what another holder of that role sees (their projects, BOQs, requests and approvals). Your actions in that role are recorded under that person's name.

How to sign in with a granted role

On the login page, choose the granted role in **Select Your Role**, enter your usual email and complete the code.

If your granted role is **Site Engineer**, sign in with your own role and then switch roles from the account menu (the Site Engineer sign-in only accepts people whose own role is Site Engineer).

How to switch roles while signed in

1. Open the account menu at the bottom of the sidebar.
2. Under **SWITCH ROLE** you see **Your role** and each granted role with its end date (for example "Granted · until 13 Oct"). The current one has a tick.
3. Click the role you want. You will see **Switching to …**, then that role's dashboard opens.

While you work in a granted role

- An amber banner at the top says **You're working as** and when it ends.
- Click **Switch back to** in the banner to return to your own role at any time.

When access ends

- Access ends automatically at **11:59 PM on the end date** (company time), or earlier if an Admin/TD revokes it.
- If you are using it at that moment, your next action shows **Your role access has ended. Returning to your role…** and you are moved back to your own role.

- The role disappears from the login role list and from **SWITCH ROLE**.

When access is paused

An Admin or TD can **pause** your access for a while instead of ending it.

- A paused role disappears from the login role list and from **SWITCH ROLE** until it is resumed.
- If you are using it when it is paused, you are moved back to your own role on your next action.
- The dates do not change. When the access is resumed, the role comes back.
- If the end date passes while it is paused, the access ends.

Role access notifications you may receive

- **New access** (or **access scheduled** if it starts later)
- **access is now active** (on the start day of a scheduled access)
- **access ends tomorrow**: finish or hand over open work
- **access paused**
- **access resumed**
- **access extended**, **access end date changed** or **access updated** (the Admin or TD changed it)
- **access removed** (revoked)
- **access has ended**

Notifications about a granted role have no link. Switch to that role to act on them.


Admin

The Admin manages people and system settings. Admin menu: **Dashboard**, **User Management**, **Role Access**, **Signature Upload** (Signatures, CC & Email Settings), **Payroll Processing**, **Security Dashboard**, and the "view as" role links.

Admin Dashboard

The **Admin Dashboard** gives a company-wide overview.

- **Period selector**: Last 7, 14, 30 (default), 60 or 90 days, plus **Refresh**.
- **System Health**: an overall percentage with low-stock alerts and pending change requests.
- **KPI cards**: Total Users, Total Projects, Total BOQs (approved / pending), Change Requests (completed / pending), Vendors, Materials (stock value / low stock).
- **Financial cards**: Total CR Costs, Inventory Value, Purchase Transactions, Transport Costs.
- **Charts**: User Distribution, User Registration Trend, Change Request Activity, Daily Cost Trend, Project Status, Delivery Stats, Material Requests.
- **Lists**: Top Project Managers, Top Site Engineers, Login Activity (Email OTP vs SMS OTP) and Pending CR Approvals by stage.

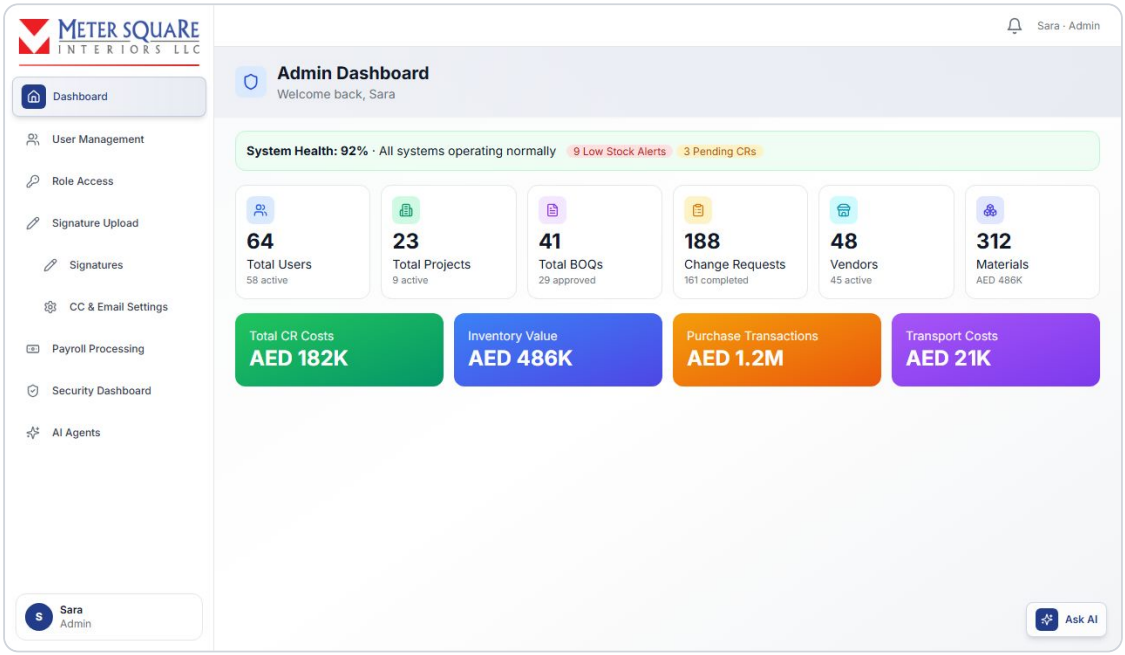

Admin Dashboard


User Management

Open **User Management** to see all users.

- Search with **Search users...**, filter by **All Roles** (with user counts) and **All Status** (Active / Inactive). Active filters show as chips; click **Clear all** to remove them.
- The table shows User (with a red **Blocked** tag if blocked), Email, Role, Department, Status and Last Login.
- 20 users per page.

How to create a user

1. Click **Add User**.
2. Fill in **Email** (must not already exist), **Full Name**, **Role**, and optionally **Phone** and **Department** (if left blank, the department is set to the role name).
3. Click **Create**. You see **User created successfully**. The user is created as Active.
4. A one-time sign-in code (OTP) is emailed to the user straight away.
5. The user signs in by choosing their role and entering their email. There is no password. If the first code has expired, they click **Send OTP** for a new one.

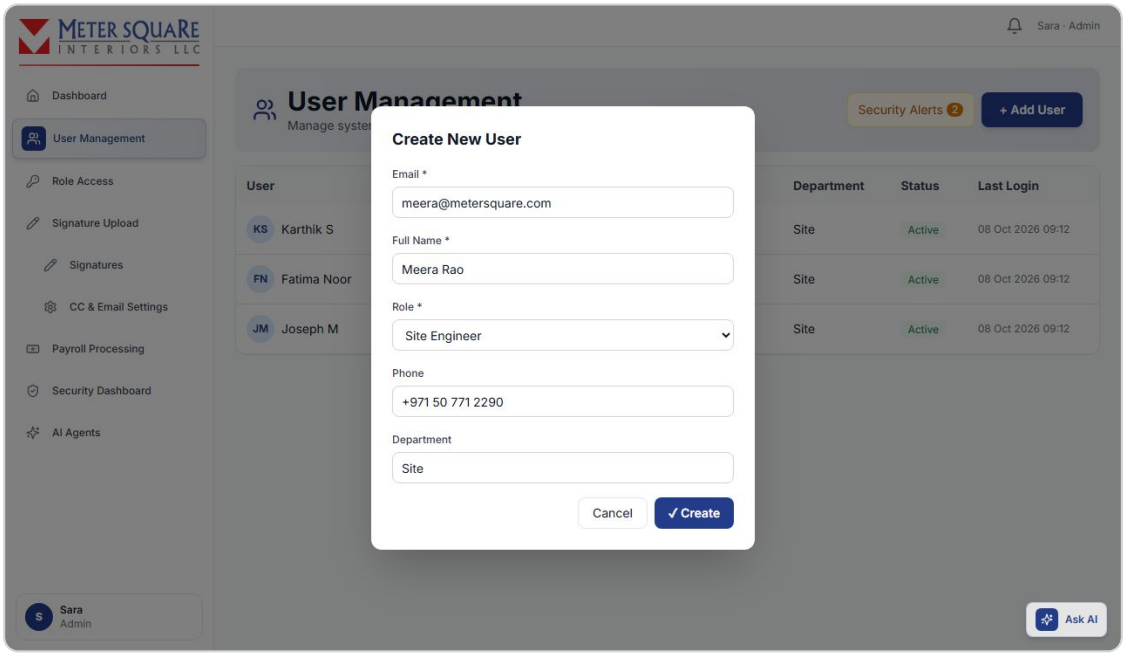

Create New User

How to activate or deactivate a user

1. Click the user's **Active** / **Inactive** status pill. The change is immediate.
2. The user is emailed about the change.

A deactivated user cannot sign in ("Email not found") and any open session stops working. You cannot deactivate yourself.

How to block or unblock a user

1. In the **Last Login** column, click the orange shield (**Block user**).
2. Enter a reason (default "Blocked by administrator") and click OK.
3. The user is signed out, set Offline and emailed with the reason. When they try to sign in they see **Account Blocked**.

To unblock, click the green shield (**Unblock user**) and confirm. The user is emailed and can sign in again.

Block or deactivate? Deactivate makes the account inactive. Block keeps the account but refuses access and marks it **Blocked** with a reason.

You cannot block yourself.

Login history

Click a user's **Last Login** to open **Login History**. Each sign-in shows:

- date and time, device (desktop, mobile or tablet), browser, operating system and IP address;
- the method (**Email OTP** or **SMS OTP**);
- a status: **Active** (session in use), **Logged Out** (signed out normally) or **Expired** (ended by a force logout, a block or the time limit).

Online status and force logout

1. Click **Online Status** to see who is online (device, browser, IP, since when) and who is offline (last seen).
2. To end someone's session, click the red log-out icon (**Force logout**) next to an online user and confirm.
3. Their session ends immediately. On their next action they return to the login page with "Your session was ended by an administrator".

You cannot force-log-out yourself.

Security Alerts

Click **Security Alerts** (the badge shows unresolved alerts). Alerts are raised automatically at sign-in:

- **multiple ips** (high): sign-ins from 3 or more different IP addresses within 24 hours.
- **unusual hours** (medium): a sign-in between 00:00 and 05:59 UTC.
- **rapid logins** (high): 5 or more sign-ins within 5 minutes.

Review an alert and click the green tick (**Mark as resolved**). Use **Show All** to include resolved alerts.

Editing user details

User Management does not have an edit button for name, phone, role or department. Users can update their own name, email, phone and department from **Profile Settings**. To give someone another role temporarily, use **Role Access**.

Role Access (temporary extra roles)

Role Access lets an Admin or Technical Director give a user temporary access to another role. The user keeps their own role and signs in with the same email.

The page shows:

- **Cards**: Active now, Ending within 3 days, Scheduled, Expired or revoked.
- **Tabs**: Active, Scheduled, Paused, Expired, Revoked, All.
- **Table columns**: User (own role), Granted role, Access type, Period, Status, Granted by, and the row actions.

Row actions

Action	Shown for
Extend	Active
Edit	Active, Scheduled, Paused
Pause	Active, Scheduled
Resume	Paused
Renew	Expired, Revoked
Revoke	Active, Scheduled, Paused

Only people whose **own** role is Admin or Technical Director can manage Role Access. Someone working in a granted Admin or TD role cannot.

Status badges


Badge	Meaning
Active · N days left	Access is in use
Ends in N days / Ends today	Active, 3 days or fewer left
Starts	Scheduled to start later
Paused	Stopped for now by Admin or TD. The row shows who paused it.
Expired	The end date has passed
Revoked	Removed early by Admin or TD

How to grant role access

Click **Grant role access**. A step-by-step wizard opens. The step bar at the top shows your progress: click a completed step to go back, use **Back** and **Next** to move between steps.

1. **User**: search by name or email and select the person. You cannot select yourself.
2. **Role**: choose the role to give. Grantable roles: Admin, Technical Director, Estimator, Project Manager, Production Manager, MEP Supervisor, Site Engineer, Procurement. The person's own role is also listed, with an **Own role** tag. You can choose it only to share another holder's work with them (**Same as existing user**), for example when one Site Engineer covers for another.
3. **Access type**:
   - **Fresh role**: starts empty as a new holder of that role. Nothing is copied from anyone. Projects are assigned to them later, and they appear in that role's selection lists while access is active. Not available when you chose the person's own role. Below it, choose the menus to give:
     - **All menus** (default): the whole role.
     - **Only selected menus**: tick the menus they may use, grouped as in that role's sidebar (for example only **Purchase Orders** and **Store › Raw Materials** for Procurement). Use **Select all** or **Clear**. Tick at least one. The dashboard is always included.
   - **Same as existing user**: they get the same projects and data as an existing holder of the role. Pick that person in the list that appears below. Each person shows their number of active projects. While using this access, the person's actions are recorded under the chosen user's name. This type always gives the whole role.
4. **Period**: choose **Start date** and **End date**, or use a quick pick (**1 day**, **1 week**, **2 weeks**, **1 month**). Access ends at 11:59 PM on the end date. A future start date makes it **Scheduled**. The maximum period is 366 days.
5. **Review**: check the summary, including **Menus** for a Fresh role, and click **Grant access**.
6. The screen shows **Access granted** (or **Access scheduled**). Click **Grant another** or **Done**.

With **Only selected menus**, the other menus are hidden from the person's sidebar, their pages open the dashboard instead, and their actions are refused. The list shows "Only N menus" under **Fresh role**. To change the menus later, click **Edit**; on access already in use, menu changes apply straight away.

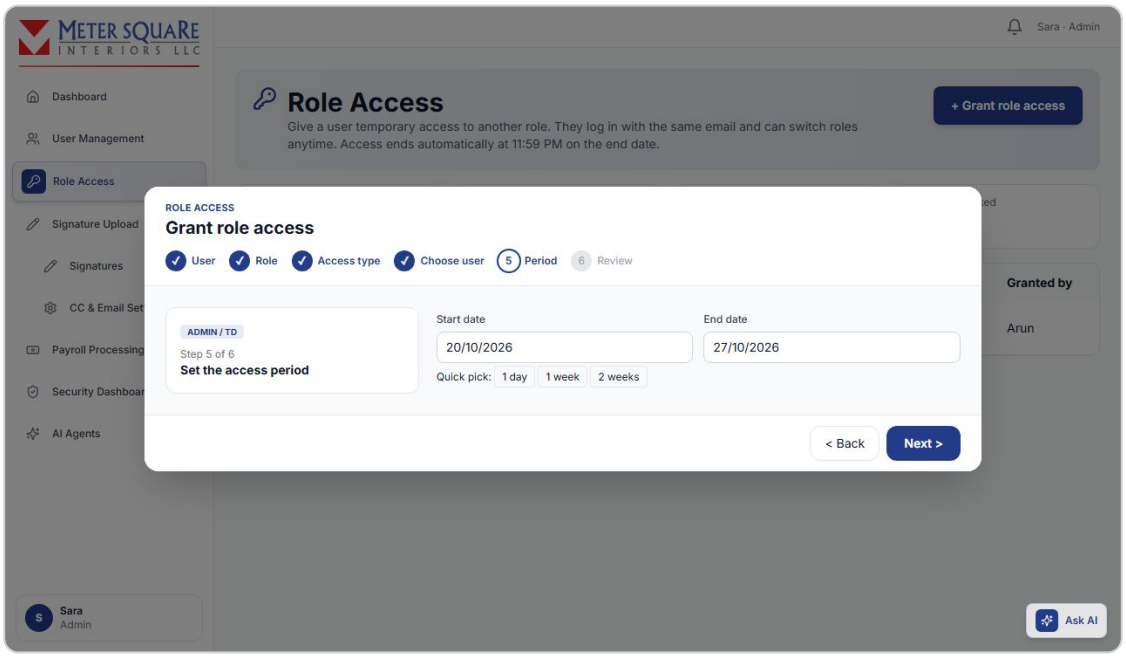

Grant role access: setting the access period

The person is notified in the app, by desktop notification and by email.

Possible errors:

- **You cannot grant a role to yourself**
- **This is already the user's own role. Use 'Same as existing user' to share another user's access.**
- **Selected user does not have the role**
- **End date cannot be in the past**
- **already shares 's access from A to B** (or **already has access as a fresh role**): that exact access already exists in an overlapping period. Use **Edit** or **Extend** on it instead.

One person can hold the same role more than once at the same time when each grant shares a different person, for example covering two Project Managers. In the wizard, a role they already hold shows a **Has access** tag but can still be chosen. On the **Access type** step, the person already shared shows **Already shared until** and cannot be picked again, and **Fresh role** is unavailable if they already have that role as a fresh role. They switch between the grants from the account menu.

How to extend or shorten role access

Use this on an **Active** row to change only the end date.

1. Click **Extend**. The **Extend role access** window shows the current period.
2. Choose a **New end date**, or use a quick pick: **+1 day**, **+1 week**, **+2 weeks** or **+1 month** (counted from the current end date).
3. An earlier date shortens the access. The button then reads **Shorten access** instead of **Extend access**.
4. Click **Extend access** (or **Shorten access**). The person is notified.

The access cannot run longer than 366 days from its start.

How to edit role access

1. Click **Edit** on an Active, Scheduled or Paused row. The **Edit role access** wizard opens with the current details.
2. Change the role, access type, shared user or dates, then click **Save changes**.
3. The screen shows **Access updated**. The person is notified.

How the change is applied depends on the status:

Status	What happens
Active	The start date cannot change. If you change the role, access type or shared user, the current access ends now and a new access starts today. The old row moves to **Revoked** with the note "Replaced by an edit". If you change only the end date, it is changed in place.
Scheduled or Paused	All changes are made to the same access.

How to pause and resume role access

Pause stops the access for a while without ending it.

1. Click **Pause** on an Active or Scheduled row.
2. Confirm **Pause access**.
3. The access moves to the **Paused** tab. The person loses the role at once: it disappears from their login role list and **SWITCH ROLE**. If they are using it, they are moved back to their own role on their next action. The dates stay as they are.

To resume:

1. Open the **Paused** tab and click **Resume**.
2. The access becomes Active again (or Scheduled, if its start date is still ahead). The person is notified.

If the end date passed while the access was paused, it cannot be resumed. You see **This access ended while paused. Use Renew to grant it again.**

How to renew role access

Use **Renew** on an Expired or Revoked row to give the same access again.

1. Click **Renew**. The **Renew role access** wizard opens, filled in from the old access.
2. Check the details and choose new dates.
3. Click **Renew access**. The screen shows **Access renewed**.

Renew creates a new access. The old row stays in the history as it was.

How to revoke role access

1. Click **Revoke** on an Active, Scheduled or Paused row.
2. Confirm **Revoke access**.
3. The person loses the role immediately. If they are using it, they are moved back to their own role on their next action. They are notified.

Handing over work before access ends

For a **Fresh role**, the person may hold work in that role, such as projects, open change requests or item assignments.

- The table shows **To hand over before end: …** while the access is active, and **Still holds …: reassign** after it has ended.
- Up to 3 days before the end date, all Admins and TDs get a reminder: **Hand over projects before role access ends**.
- If work is still assigned after the end date, Admins and TDs get an urgent alert: **Work left without an active** .

Reassign that work to another person in the normal way (for example the TD reassigns the project's PM, or the PM picks another buyer).

Signature Upload

Open **Signature Upload** → **Signatures**. These signatures appear on PDFs sent to clients and vendors.

BOQ quotation (to clients):


- **MD Signature**: on the quotation cover page.
- **Authorized Signature**: in the quotation section.

LPO signatures (purchase orders to vendors):

- **Managing Director**: name and signature.
- **Company Seal**: stamp image.
- **Technical Director**: name and signature.

How to upload a signature

1. Click the dashed **Upload** box and choose an image (PNG or JPG, up to 2 MB). It saves immediately.
2. Use **Change** to replace it, or the bin icon to remove it.
3. If you changed a **Name** field, click **Save Changes**.

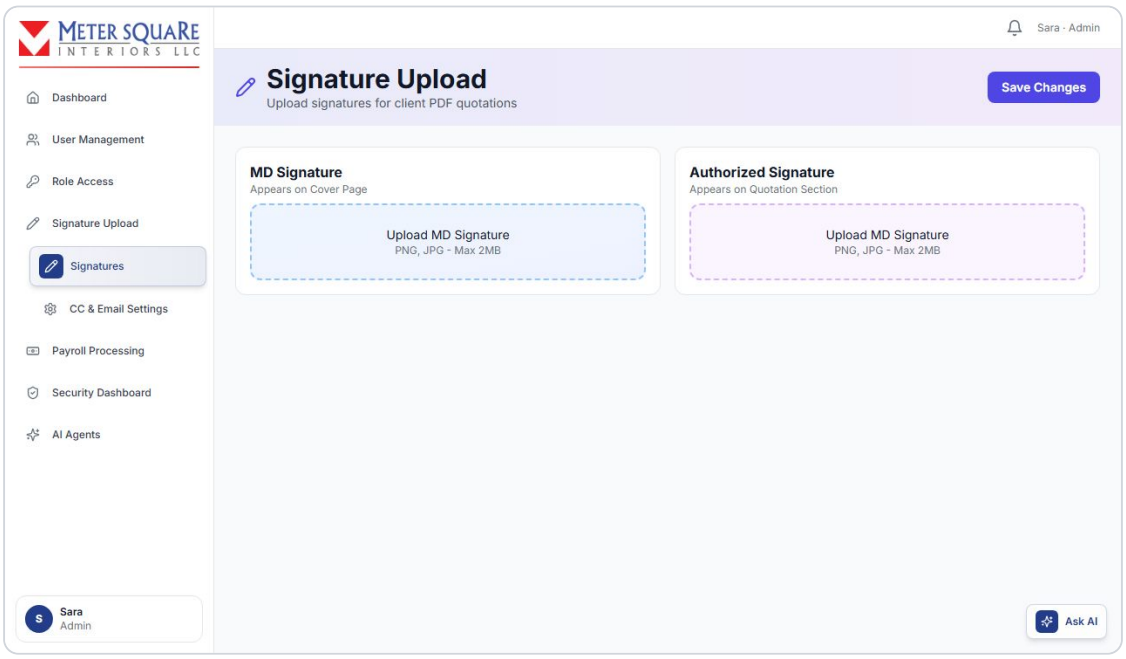

Signature Upload


The BOQ MD Signature and the LPO Managing Director signature are the same image, so changing one changes both. Estimators choose whether to include signatures when sending a BOQ to a client, and buyers when sending an LPO to a vendor.

CC & Email Settings

Open **Signature Upload → CC & Email Settings**. Addresses listed here are automatically copied (CC) on every purchase-order email sent to vendors. Buyers can untick a default or add their own CC when sending.

How to add or remove a default CC recipient

1. Under **Add New CC Recipient**, enter a name (optional) and an email.
2. Click **Add**.
3. To remove a recipient, click the ✕ next to it.

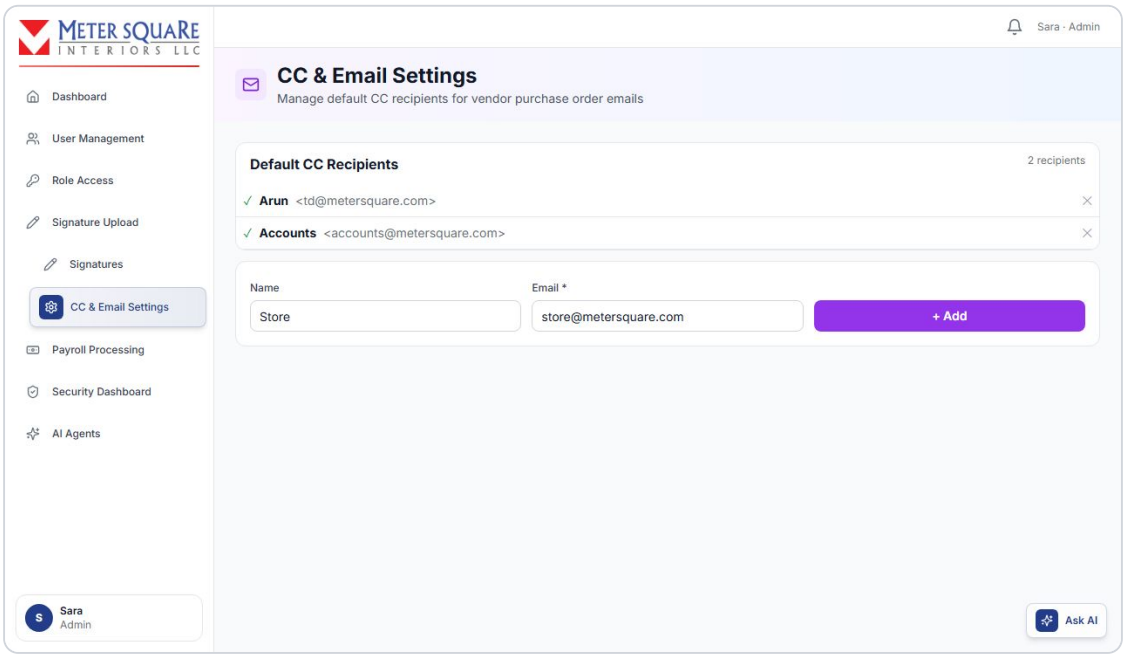


CC & Email Settings

Payroll Processing

Open **Payroll Processing** to view locked attendance and payroll cost.

1. Choose **Start Date**, **End Date** and a **Project** (or All Projects).
2. Results are grouped by project, with workers, total hours and total cost (AED). Click a project to expand it.

3. Each worker shows Days, Regular hours, Overtime, Total hours, Rate and Cost. The grand total is shown at the bottom.
4. Click **Export All** to download a PDF of all projects. To download one project only, click the **PDF** button on that project's row.

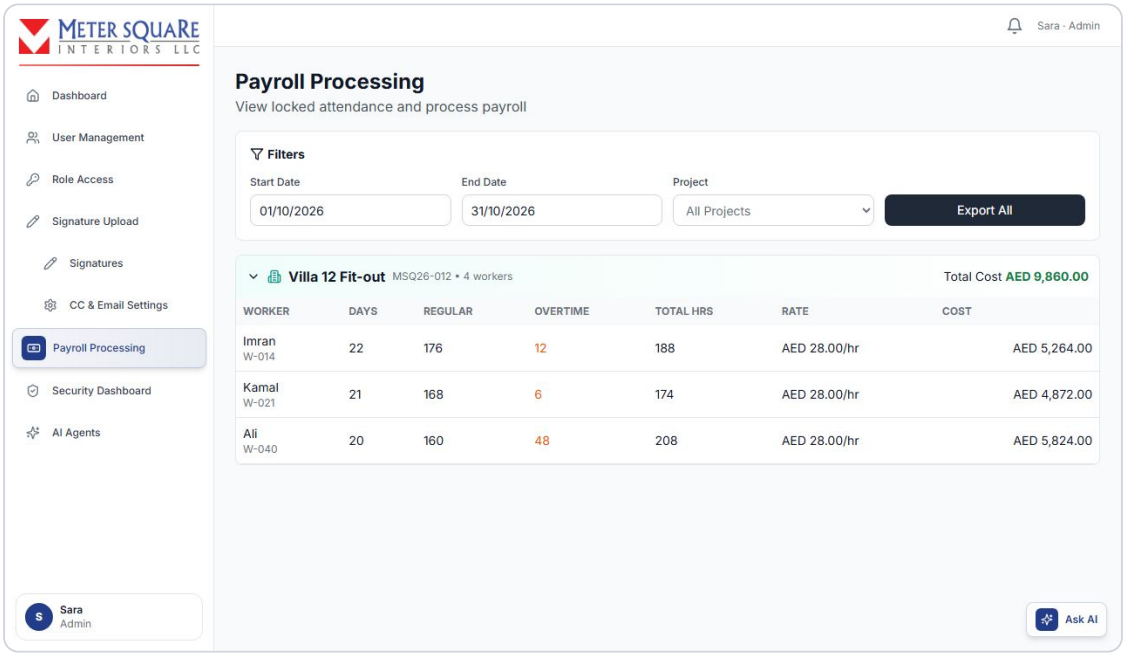

Payroll Processing


Only attendance that a Project Manager has **locked** appears here. If nothing shows, check that attendance for that period has been locked.

Security Dashboard

Open **Security Dashboard** to monitor sign-in security.

- **Cards**: Failed Logins (24h), Blocked IPs, Suspicious IPs, Total Events (24h).
- **Blocked IPs**: the list of blocked addresses. Click the unlock icon to unblock one.
- **Recent Security Events**: filter by event type (Login Failed, Login Success, IP Blocked, Suspicious, Rate Limited) and severity.

An IP address is blocked automatically after 10 failed sign-ins. Repeat blocks get longer: 24 hours, then 48 hours, 7 days, 30 days, and after that permanent.

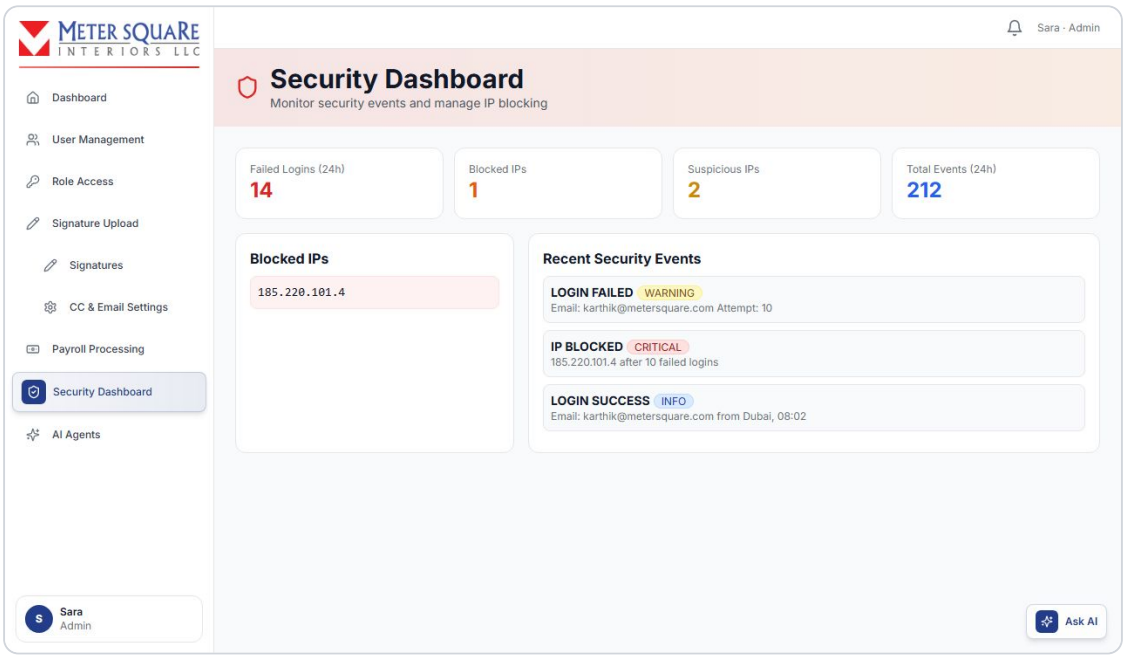

Security Dashboard

Viewing the app as another role

The Admin can look at any role's screens.

1. In the sidebar, below the admin items, click a role: Technical Director, Estimator, Project Manager, MEP, Site Engineer, Procurement or Production Manager.
2. You see **Now viewing as** and that role's dashboard. A purple pill at the top shows **Admin viewing as:** .
3. The sidebar shows that role's menu with ← **Back to Admin View** at the top.
4. Click ← **Back to Admin View** to return.

When viewing as a role, you see that role's data across all users, not one person's. To see the app exactly as one person sees it, they need to show you, or you can use Role Access with "Same as existing user" for a test account.

Estimator

The Estimator creates projects and Bills of Quantities (BOQ), gets them approved by the Technical Director, sends them to the client, handles revisions, and prices material purchase requests that contain new materials.

Estimator menu: **Dashboard**, **Projects** (Projects & BOQ Management), **Purchase Request**.

The BOQ journey at a glance


1 **Estimator**	Create the project (New Project)
2 **Estimator**	Create the BOQ (status Draft)
3 **Estimator**	Send to TD (or first Send to PM for an optional PM review)
4 **Technical Director**	Approve the BOQ (status Approved) or reject it with a reason
5 **Estimator**	Send to Client by email with Excel and/or PDF (status Sent for Confirmation)
6 **Client**	Approves, asks for changes, or does not proceed
7 **Estimator**	Record the answer: Client Approved, Revisions, or Cancel
8 **Technical Director**	Assign a Project Manager (only after the client approves)
9 **Project Manager**	Assign BOQ items to Site Engineers (Items Assigned)
10 **Project Manager**	Confirm completion (BOQ moves to Completed)

Email or in-app notification?

When a BOQ or request moves to another person (TD, PM, Estimator or Buyer), that person gets an **in-app notification**. They also get an **email only if they are offline** at that moment. Emails to the **client** are always sent.

Estimator Dashboard

- **Count tiles**: Pending, Send BOQ, Approved BOQ, Revisions, Rejected BOQ, Completed BOQ, Cancelled BOQ.
- **BOQs by Status** chart.
- **My Performance**: BOQ Approval Rate and Pending Review.
- **Lists**: Recent Created Projects, Completed Projects, Client Pending, and Client Rejected (marked "Needs Revision").

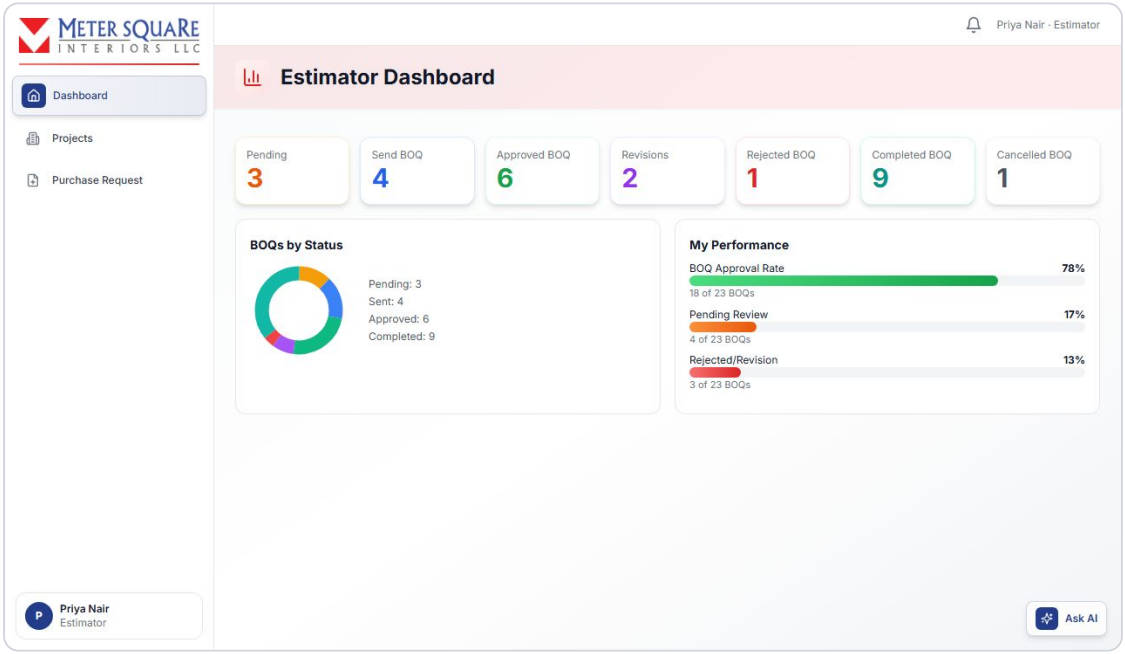

Estimator Dashboard

Projects & BOQ Management

Open **Projects** in the sidebar.

- Search by title, project, client or project code (for example MSQ26).
- Switch between **Cards** and **Table** view.
- Click **New Project** to create a project.

Tabs


Tab	What it shows
Pending	Projects with no BOQ yet, or with a BOQ still in Draft
Send BOQ	BOQs sent for review (to the TD, or to a PM) and waiting for a decision
Approved BOQ	BOQs approved by the TD, sent to the client, or confirmed by the client
Revisions	Client revisions (R1, R2…) and internal revisions after a TD rejection. Sub-tabs: **Client Revisions** and **Internal Revisions**
Rejected BOQ	BOQs rejected by the TD or by a PM. A TD-rejected BOQ you edited but did not re-send also stays here.
Completed BOQ	Projects the PM has completed
Cancelled BOQ	BOQs cancelled because the client did not proceed

How to create a project

1. In **Projects**, click **New Project**. The **Create New Project** form opens.
2. Fill in:
    - **Project Name**, **Client**, **Location**
    - **Work Type** (for example Construction or Renovation)
    - **Working Hours** (for example 8 hours/day), **Floor Name**, **Area** (for example 1000 sq.ft.)
    - **Start Date** (today or later) and **Number of Days**. The **End Date** is calculated automatically.
    - **Description** (optional)
3. Click **Create Project**.

The project gets a code (MSQ01, MSQ02…) and appears in the **Pending** tab. A project name must be unique.

- **To edit**: use **Edit Project** on the card, then **Update Project**.
- **To delete**: use the bin icon and confirm **Delete Project**.

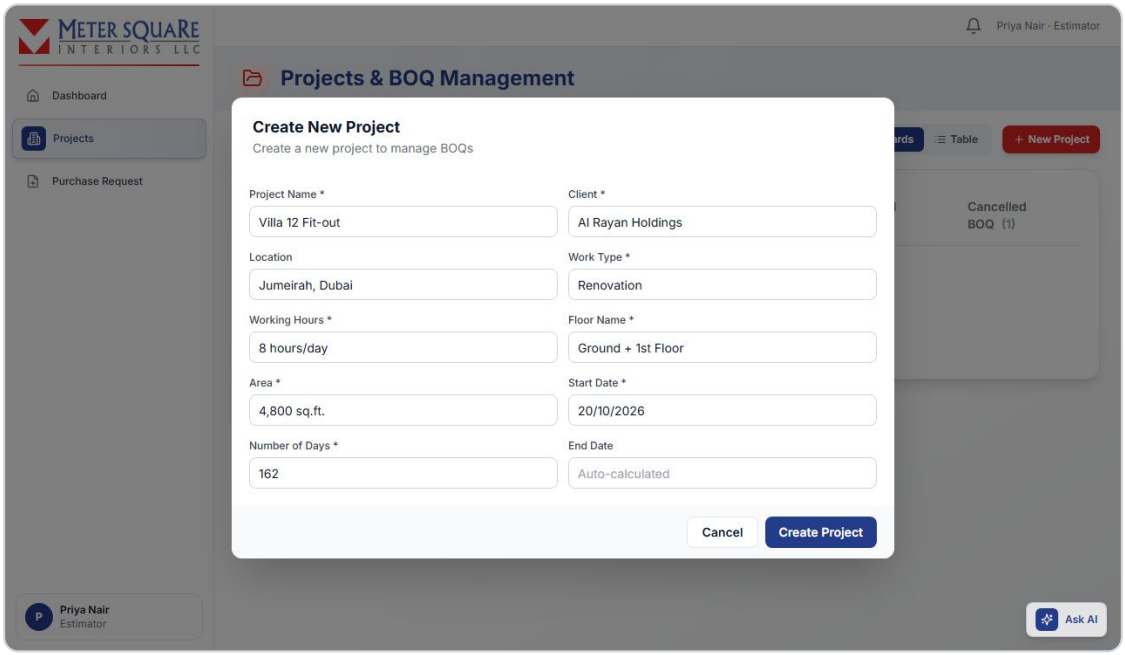

Create New Project

Project card (Pending tab)

The card shows the project name, code, client, location, number of BOQ items, work type, site engineer and created date. Buttons:

- **View Details**: project information and its related BOQs.
- **Create BOQ** (or **Resume Draft** if you have unsaved work in progress).
- **Send to TD** / **Send to PM**: appear once a BOQ exists and has not been sent.
- **BOQ Created** / **BOQ Sent**: shown greyed out once done.


How to create a BOQ

1. On the project card, click **Create BOQ**. The full-screen BOQ form opens. Your work is auto-saved in the browser as you go ("Last saved: ").
2. **BOQ Details**: enter the **BOQ Name**. The project is filled in automatically.
3. **Preliminaries & Approval Works**: tick the conditions that apply. Click **Add Custom Item** to add your own; custom items are saved to the master list for future BOQs. Fill in the cost details: quantity, unit and rate for the client amount, and the internal cost with Misc %, O&P % and Transport %.
4. **BOQ Items**: click **Add Item**.
   - Type the item name. Pick from **Master Items** or the **Buyer Catalog**, or add a new item. Duplicate items are not allowed.
   - Expand the item and click **Add Sub Item**.


    - For each sub-item, enter **Sub Item Name**, **Scope**, optional **Size**, **Location**, **Brand** and **Images**, then **Quantity**, **Unit** and **Rate**. The total is calculated.
5. **Raw Materials** (internal cost, per sub-item): click **Add Material**. Search the Raw Materials Catalog, Buyer Catalog or Master Materials, or type a new material. Enter **Qty** and **Rate (AED)**. A new material needs Brand, Size and Specification.
6. **Labour** (internal cost): click **Add Labour**. Choose the labour role, work type (Piece Rate, Contract or Daily Wages), **Hours** and **Rate/hr (AED)**.
7. **Cost Breakdown Percentages**: Misc %, Overhead & Profit % and Transport % (defaults 10%, 25%, 5%). The **Profit Analysis** shows client amount, internal cost, planned profit and negotiable margin.
8. **Total Project Value**: review Items Subtotal, Preliminary Amount and Combined Subtotal. Optionally enter an **Overall Discount** (%). The suggested safe discount is shown, and a warning appears if the profit margin drops below 15%. The **Grand Total** excludes VAT.
9. **Terms & Conditions**: tick the terms that apply, or **Add Custom Item**.
10. Click **Create BOQ**. It is enabled once there is a BOQ name and at least one item.

The BOQ is saved as **Draft**.

Each item needs at least one material or labour line, and every rate and quantity must be filled in. The form tells you exactly what is missing.

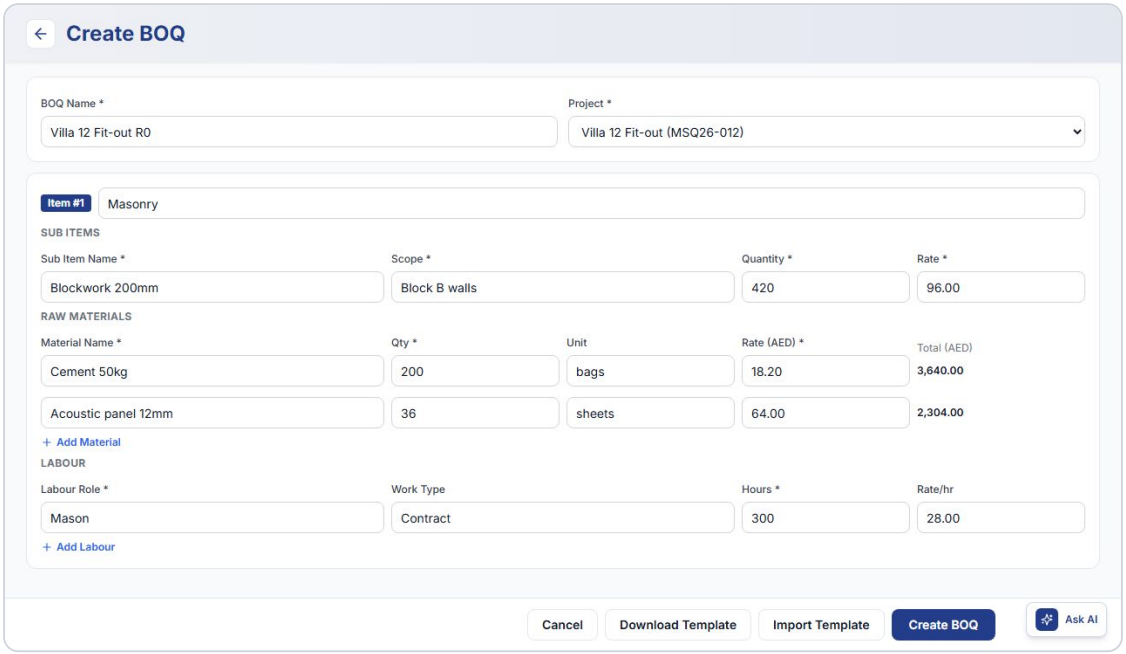

Create BOQ: item, sub-item, raw materials and labour

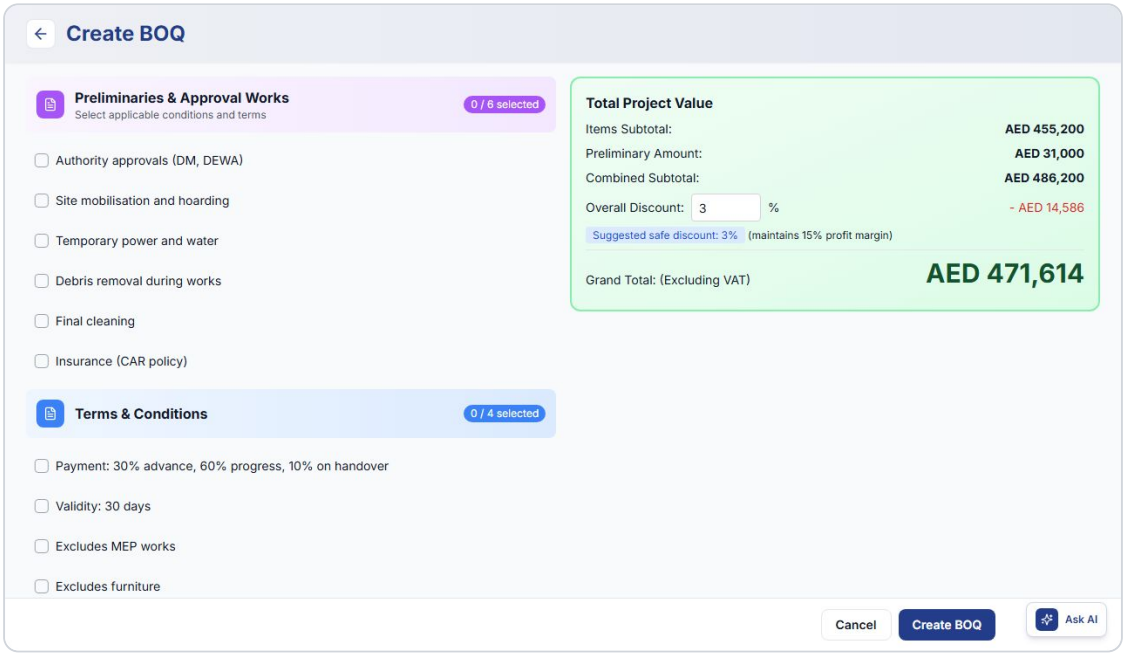

Preliminaries & Approval Works, Terms & Conditions and Total Project Value

How to import a BOQ from Excel

When you create a BOQ, the bottom of the form also shows **Download Template** and **Import Template**. These buttons are not shown when you edit a BOQ.

1. Click **Download Template** to get the Excel template.
2. Fill in the items in the template.
3. In the form, enter the **BOQ Name** first.
4. Click **Import Template** and choose the file (.xlsx or .xls, up to 10 MB).

The BOQ is created from the file and saved as **Draft**. Any warnings about the file are shown on screen.

Leaving the form

- If you close the form, choose **Save as Draft** (recommended) or **Discard Changes**. Uploaded images cannot be kept in a draft.
- After 2 hours idle you are asked to **Continue Working** or close (your draft is kept).
- When you reopen, choose **Restore Previous Work** or **Start Fresh**.

Editing or deleting a BOQ

- **Edit** (pencil icon) is available when the BOQ is in Draft, Sent for Confirmation, Under Revision or Pending Revision.
- **Delete** (bin icon) is available on a Draft BOQ, until it is sent.
- Cards with status **Internal Revision Pending**, **Client Pending Revision** or **Client Revision Rejected** also show **Edit**, **Delete** and **Send to TD**.

How to send a BOQ to the Technical Director

- **From the Pending tab**: click **Send to TD** on the project card. All BOQs of that project are sent.
- **From a Draft BOQ card**: click **Send to TD**.

The BOQ moves to **Send BOQ** with status **Pending**, and the TD is notified.

While the BOQ waits for the TD, the card shows a label instead of buttons:


- **Pending TD Approval**: sent to the TD after a PM approval.
- **Revision Pending TD Approval**: an internal revision sent to the TD.

How to send a BOQ to a Project Manager for review (optional)


You can ask a PM to review the BOQ before it goes to the TD.

1. On the project card, click **Send to PM**.
2. Select a PM and click **Send to PM**. The status becomes **Pending PM Approval** and the PM is notified.
3. **If the PM approves**: the status becomes **PM Approved** (Approved BOQ tab). Click **Send to TD** to send it for final approval.
4. **If the PM rejects**: the status becomes **PM Rejected** (Rejected BOQ tab) with the reason. Edit the BOQ, then click **Resend PM**.

Sending to a PM for review does not assign that PM to the project.

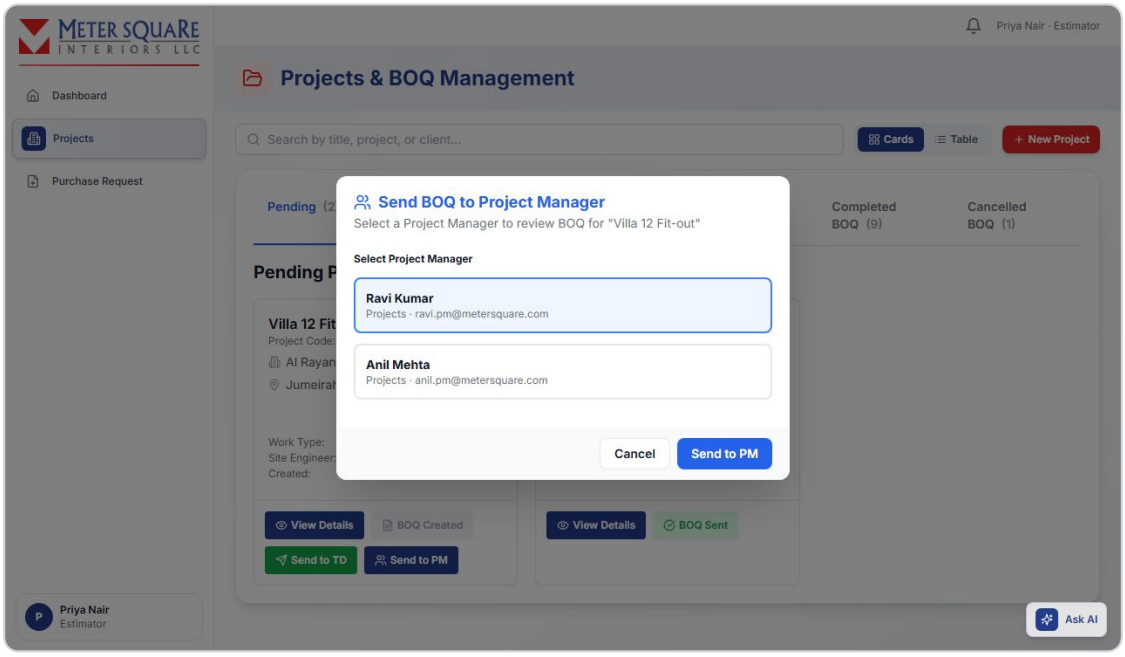

Send BOQ to Project Manager

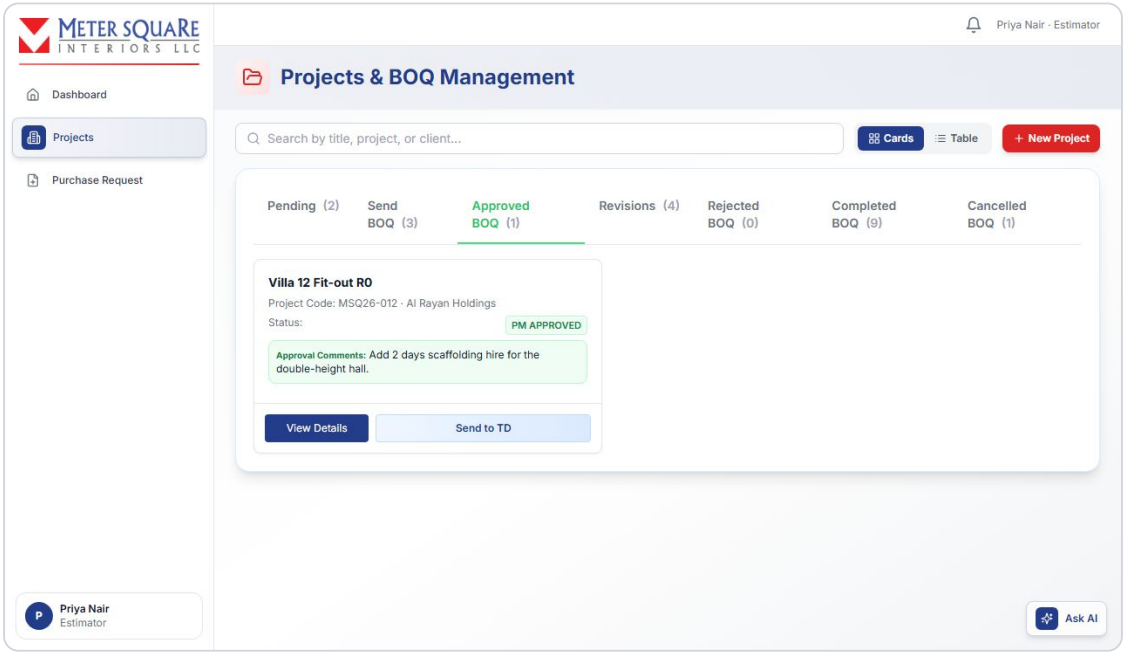

Approved BOQ: a PM-approved BOQ with Send to TD

When the TD approves or rejects


- **Approved**: the BOQ moves to **Approved BOQ** and the TD's comments appear under "Approval Comments". You can now send it to the client.
- **Rejected**: the BOQ moves to **Rejected BOQ** with the "Rejection Reason". If a PM forwarded it, the PM is notified too.

How to fix a BOQ the TD rejected (internal revision)

1. In **Rejected BOQ**, click **Edit BOQ** on the card.
2. Make the changes and click **Update BOQ**.
3. When asked "Would you like to send this BOQ to the Technical Director for approval now?":
   - **Send to Technical Director**: the status becomes **Pending Revision**.
   - **Send Later**: the status becomes **Internal Revision Pending** and it stays in **Rejected BOQ**. The card shows **Edit BOQ** and **Send to TD**. When you are ready, click **Send to TD** on the card.
4. Track it under **Revisions** → **Internal Revisions**. Select the project to compare the current version with earlier versions, starting from the Original BOQ.

The TD reviews the revision in **Revisions** → **Internal Revisions**.

- **If the TD approves**: the status becomes **Internal Revision Approved**. The card shows **Send to Client**.
- **If the TD rejects**: the status goes back to **Internal Revision Pending** and the BOQ returns to **Rejected BOQ**. Edit it and send it again.

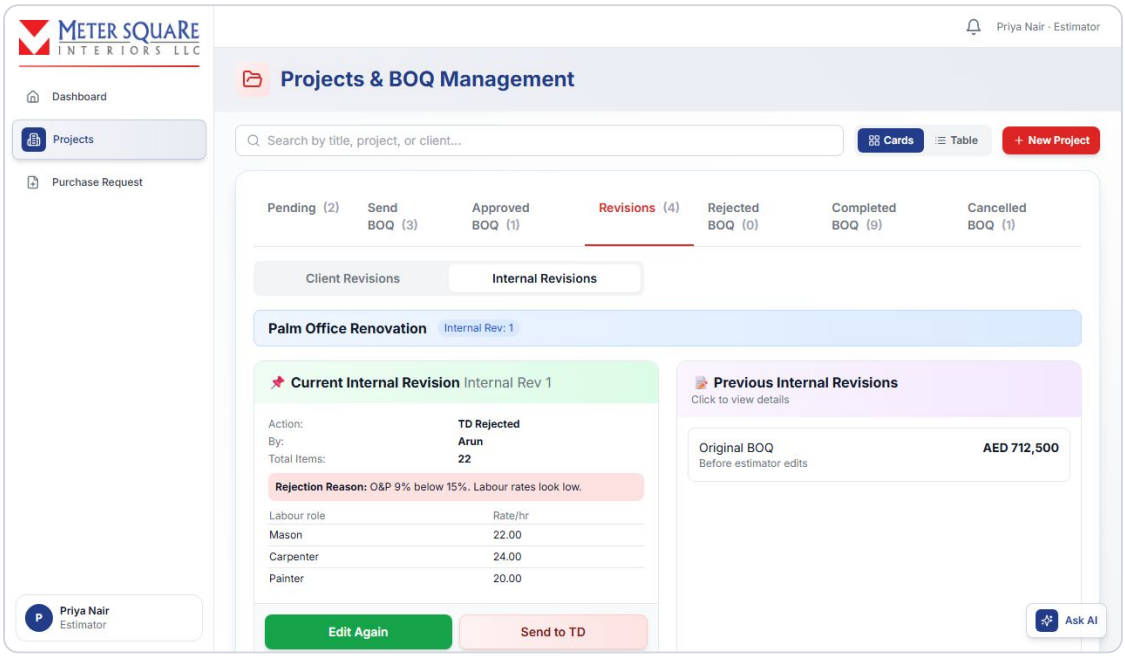


Revisions › Internal Revisions after a TD rejection

How to send a BOQ to the client

1. On an approved BOQ card in **Approved BOQ**, click **Send to Client**. For an approved client revision you can also use **Send Revision to Client** in **Revisions → Client Revisions**.
2. Enter the **Client Email(s)**. You can enter several, separated by commas, semicolons or new lines.
3. Optional: add an **Additional Message**.
4. Optional: open **Customize Email & PDF Content** to edit:
   - the email body;
   - the PDF cover page (reference number, date, recipient, company, subject, project reference, letter text, contact person, signatory);
   - **Include Authorized Signature**. Leave it unticked if the client will sign manually.
5. Choose the formats: **Excel (.xlsx)** and/or **PDF (.pdf)**.
6. Optional: use **Preview Email**, **Preview PDF**, **Download Excel** or **Download PDF** to check before sending.
7. Click **Send to Client**.

The status becomes **Sent for Confirmation**, the client email is saved on the project, and the TDs are notified that the BOQ was sent to the client.

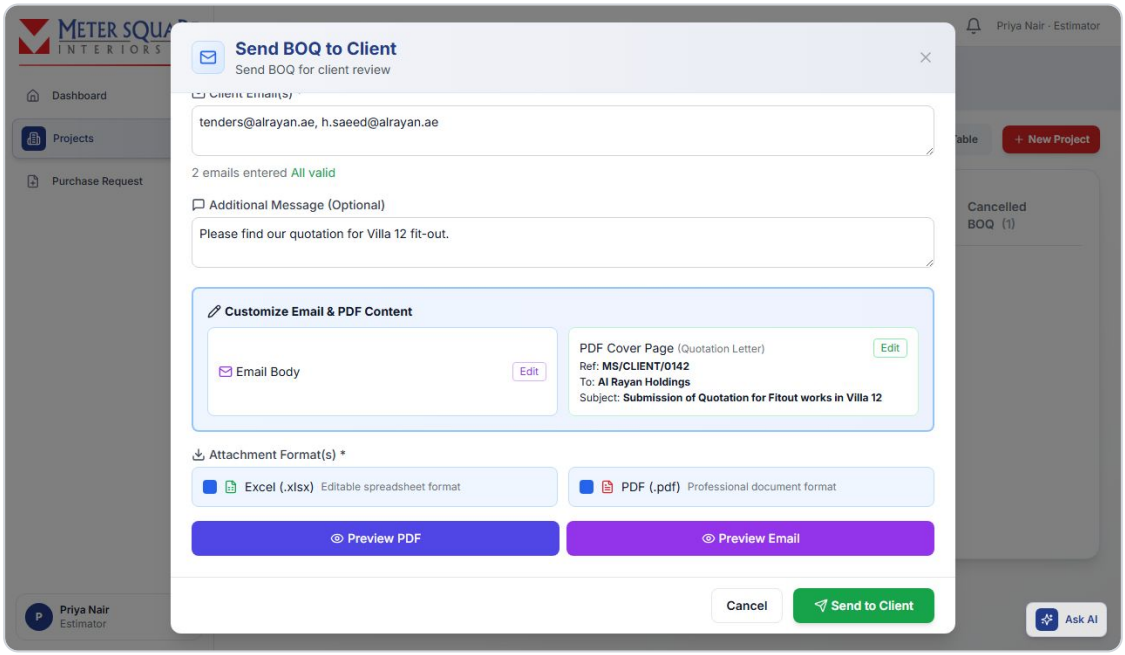


Send BOQ to Client

How to record the client's answer

When the BOQ is **Sent for Confirmation**, the card shows three buttons. These are the only ways to record the client's answer:

- **Client Approved**: the client accepted. The status becomes **Client Confirmed** and the TDs are notified. Next, the TD assigns a Project Manager.
- **Revisions**: the client wants changes. Choose **Make Revision** (or **Cancel Project**, or **Go Back**). See the next section.
- **Cancel**: the client does not want to proceed. See "How to cancel a BOQ".

There is no separate button to mark the BOQ as rejected by the client. Use **Revisions** if the client wants changes, or **Cancel** if the client does not proceed.

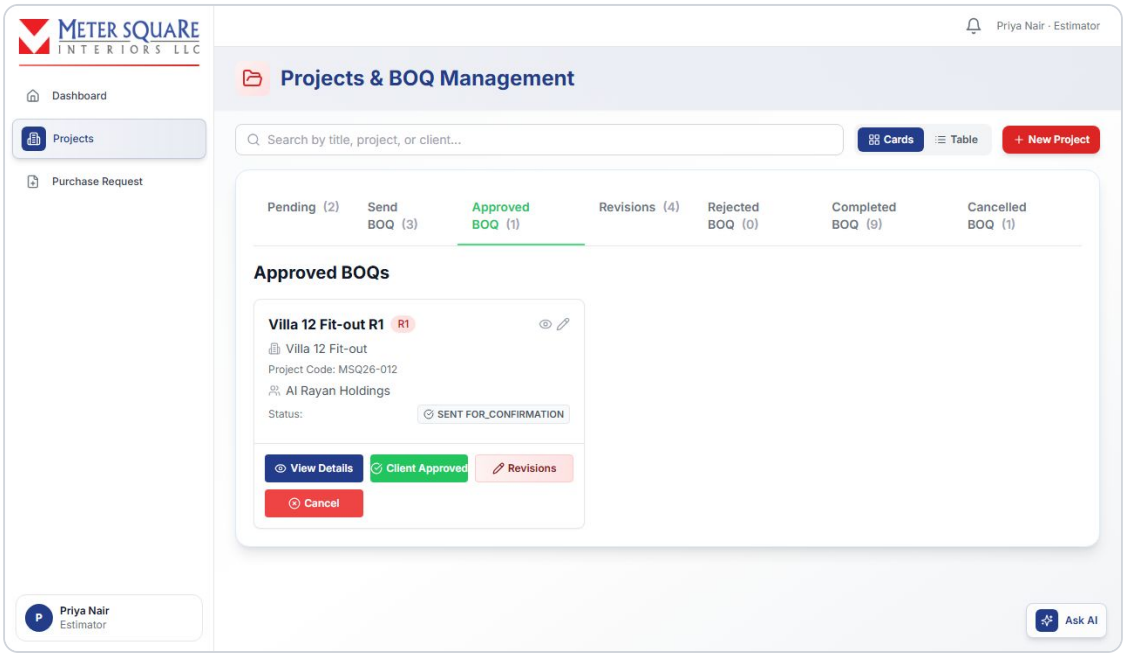


An Approved BOQ card with Client Approved, Revisions and Cancel

How to make a client revision


1. Click **Revisions** → **Make Revision**.
2. Edit the BOQ and click **Update BOQ**. The revision number goes up (R1, R2…) and the status becomes **Under Revision**. It now appears in **Revisions** → **Client Revisions**.
3. Use **Edit Again** if needed, then **Send to TD**. The TD is notified.

4. **If the TD approves**: the status becomes **Approved**. On the card in **Approved BOQ**, click **Send to Client**. In **Revisions → Client Revisions** the same button reads **Send Revision to Client**. Send it as before.
5. **If the TD rejects the revision**: the status becomes **Client Revision Rejected**. Use **Revise BOQ** and send it again, or **Cancel**.

In **Revisions → Client Revisions**, select a project to compare the current revision with previous ones. Revised BOQs also show a **Compare** button.

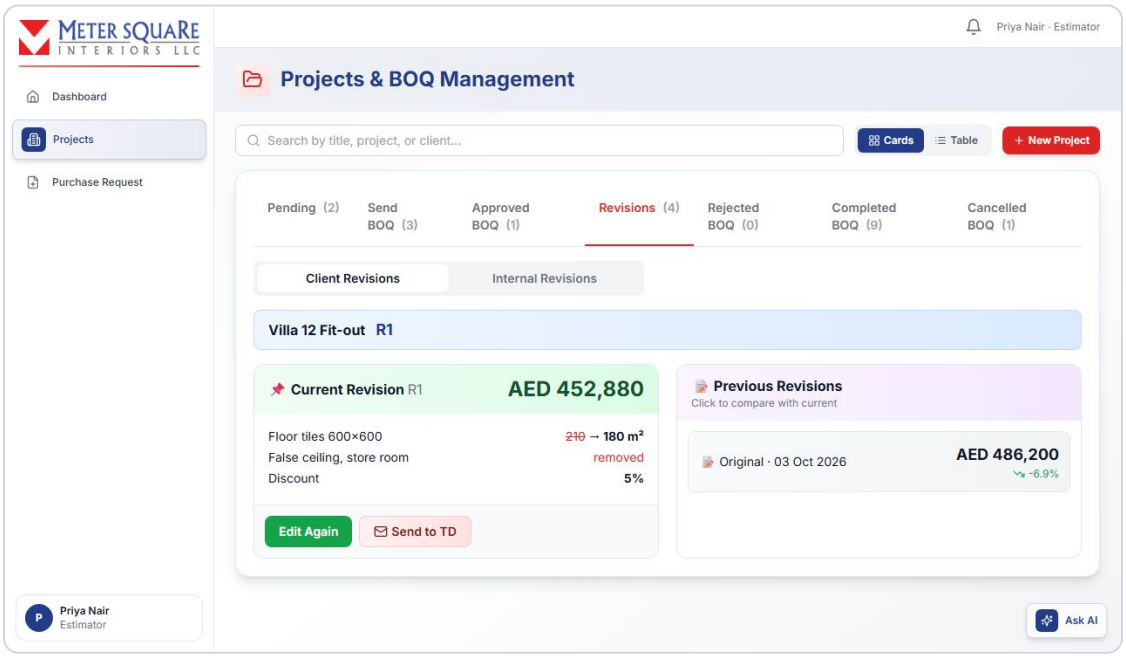

Revisions › Client Revisions

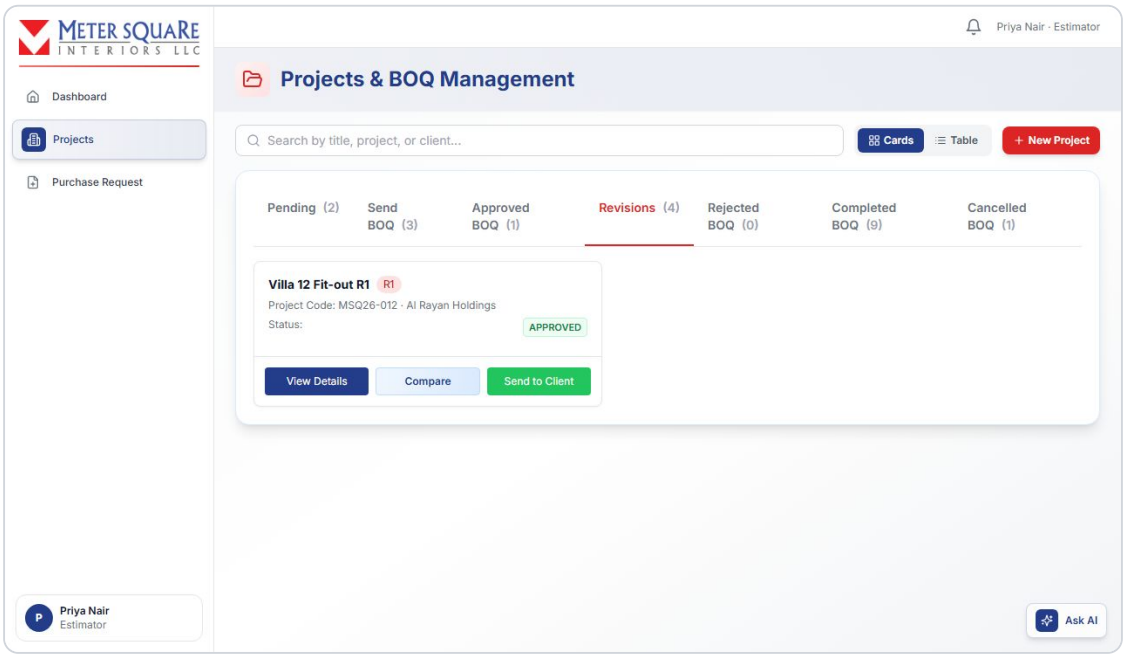


An approved client revision with Compare and Send to Client

How to cancel a BOQ (client does not proceed)

1. Click **Cancel**, or **Revisions** → **Cancel Project**.
2. Enter the **Cancellation Reason**.
3. Click **Confirm Cancellation**.

The status becomes **Client Cancelled**. The BOQ moves to **Cancelled BOQ** and shows "Project Permanently Cancelled". **Cancel** is not shown on completed BOQs.

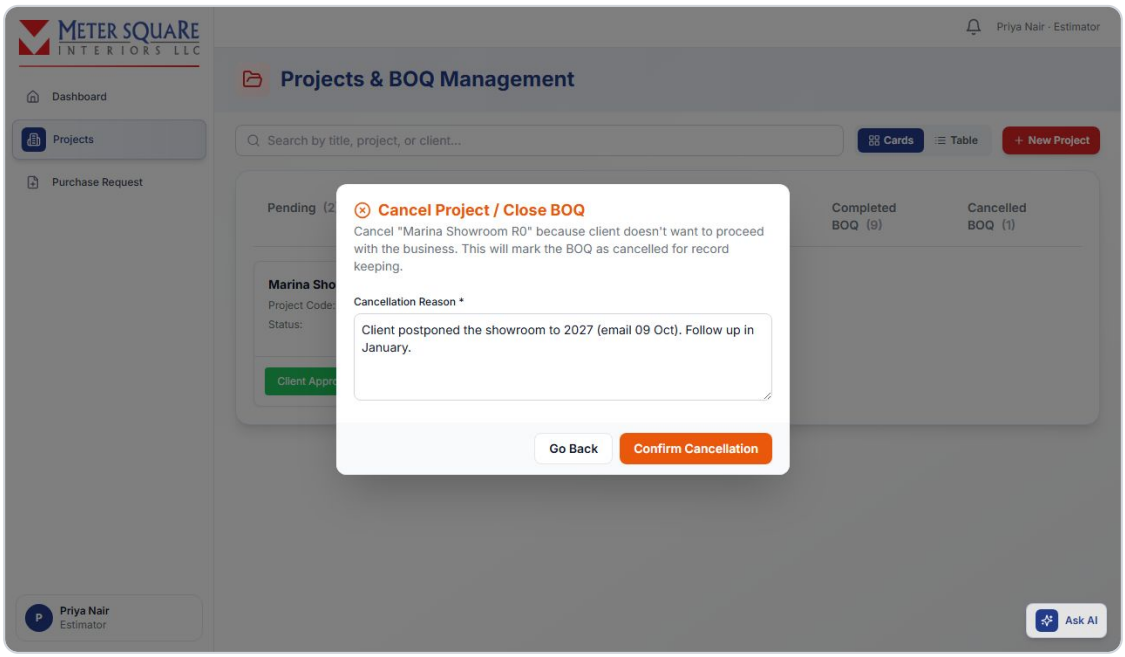

Cancel Project / Close BOQ

After the client approves

- The **Technical Director** assigns a Project Manager to the project. This is only possible after the client has approved.
- The PM then assigns BOQ items to Site Engineers. The card shows "Items Assigned to SE".
- When the PM confirms the project is complete, the BOQ moves to **Completed BOQ**.

Viewing and downloading a BOQ

Click **View Details** (eye icon) to open the full BOQ.

- **Tabs**: BOQ Details, History & Timeline, and Client Revisions (when the BOQ has revisions).
- **Download**:
  - **Internal BOQ**: includes overheads, profit margins and the detailed breakdown.
  - **Client BOQ**: final prices only.
  - Then choose **Download Excel** or **Download PDF**.

BOQ statuses


Status	Meaning	Tab
Draft	Created, not yet sent	Pending
Pending	Sent to the TD, waiting for a decision	Send BOQ
Pending PM Approval	Sent to a PM for review	Send BOQ
PM Approved	PM approved. Send it to the TD.	Approved BOQ
PM Rejected	PM rejected. Edit and resend to the PM.	Rejected BOQ
Pending TD Approval	Sent to the TD after PM approval	Send BOQ
Approved	TD approved the BOQ or a client revision. Ready to send to the client.	Approved BOQ
Rejected	TD rejected	Rejected BOQ
Internal Revision Pending	A TD-rejected BOQ was edited but not yet re-sent, or the TD rejected the internal revision	Rejected BOQ
Pending Revision	Internal revision sent to the TD	Revisions
Internal Revision Approved	TD approved the internal revision. Ready for the client.	Approved BOQ
Under Revision	Client revision being prepared	Revisions
Client Pending Revision	Client revision sent to the TD	Revisions

Status	Meaning	Tab
Client Revision Rejected	TD rejected the client revision	Revisions
Sent for Confirmation	Emailed to the client, waiting for an answer	Approved BOQ
Client Confirmed	Client approved. TD will assign a PM.	Approved BOQ
Client Cancelled	Client did not proceed	Cancelled BOQ
Items Assigned	PM assigned items to Site Engineers	Approved BOQ
Completed	Project completed	Completed BOQ

Purchase Requests (material requests needing pricing)

Open **Purchase Request** in the sidebar. These are requests for extra materials on approved projects, raised by Site Engineers or Project Managers.

- A request comes to the Estimator when the PM approves it and:
  - it contains **new materials** that are not in the BOQ. Materials picked **From Catalogue** count as new; or
  - a BOQ material's quantity is already used up or exceeded by earlier requests; or
  - the PM chooses to send it to the Estimator.
- Other requests go straight to Procurement.
- **Tabs**:
  - **Pending**: waiting for you.
  - **Approved**: sent to a buyer or further in the process.
  - **Completed**: purchase completed or routed to the store.
  - **Rejected**.
- Each card shows the request number (PO-...), project area, requester, date, number of materials and total cost.

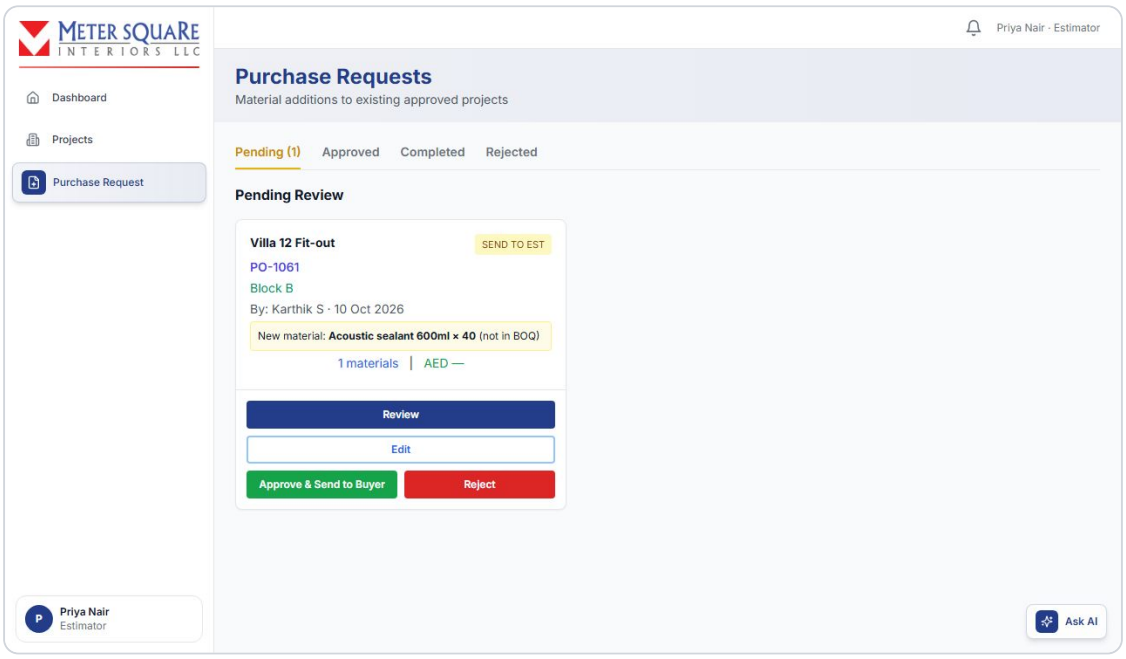

Purchase Requests: Pending Review

How to approve a purchase request and assign a buyer

1. Click **Review** to see the materials. You can edit prices there. Use **Edit** to change the request.
2. Click **Approve & Send to Buyer**.
3. Under **Assign to Procurement**, choose a buyer. Buyers are grouped **Online** and **Offline**; an offline buyer gets an email. People with temporary Procurement access show a **Granted · until** tag.
4. Optional: add **Comments**.
5. Click **Approve & Assign**.

The request goes to that buyer for purchase, the materials are added to the BOQ, and the buyer is notified.

How to reject a purchase request

1. Click **Reject**.
2. Enter a reason and confirm.

The requester is notified with the reason.

Technical Director

The Technical Director (TD) is the main approver.

- Approves BOQs.
- Assigns Project Managers and MEP Supervisors to projects.
- Approves day extensions, vendor selections and vendor return requests.
- Approves material and asset disposals.
- Can grant temporary role access to other users.


TD menu: **Dashboard**, **Project Approvals**, **Disposal Approvals** (Material Disposal, Asset Disposal), **Vendor Management**, **Purchase Orders** (All Orders, Return Approvals), **Purchase Comparison**, **Profit Comparison**, **Role Access**.

Whenever the TD acts, the person affected gets an in-app notification, and an email only if they are offline.

Technical Director Dashboard

The dashboard shows:

- **BOQ charts**: BOQ Status Overview, BOQ Status Distribution, Budget Distribution, Top 5 Projects by Budget.
- **Trends**: monthly performance, revenue and disposal requests.
- **Pending Day Extension Requests**: click **Review Request** to open Project Approvals.
- **Active Projects Overview**: each project with its Project Manager, progress, budget used, due date, and whether it is on track or delayed.

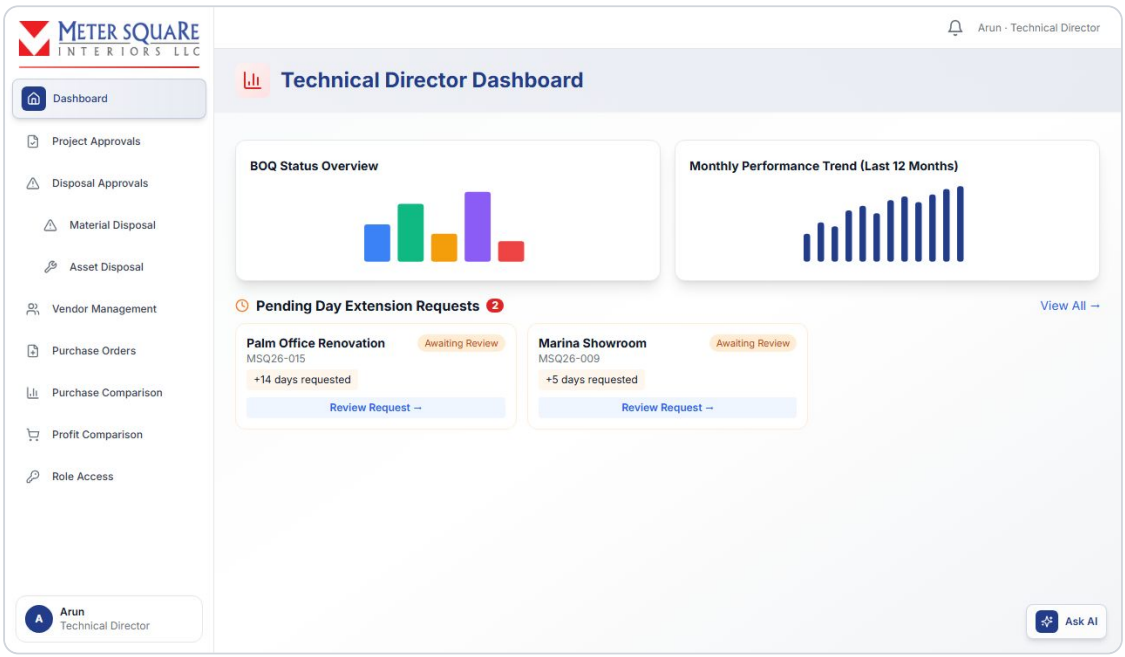

Technical Director Dashboard

Project Approvals

Open **Project Approvals**. Search by BOQ ID (B-123), project code (MSQ26), project name or client. Switch between card and table view.

Tabs

Tab	What it shows
Pending	New BOQs waiting for your approval
Approved	BOQs you approved, including those sent to the client
Client Response	BOQs the client confirmed, waiting for a Project Manager
Revisions	Client and internal revisions to review. Internal revisions the Estimator sends back after your rejection appear here under **Internal Revisions**, not in Pending.
Assigned	Projects with a Project Manager assigned
Completed	Completed projects
Rejected by TD	BOQs you rejected
Cancelled	BOQs the client cancelled


Each card shows:

- the project, client, dates and duration;
- the Total Value, Items, Labor Cost, Material Cost and O&P margin;
- any approval, rejection or cancellation remarks.

How to approve a BOQ

1. In **Pending**, click the eye icon (**View BOQ Details**). The full BOQ opens.
2. Review it and click **Approve**.
3. Optional: add **Approval Notes**, then click **Approve Project**.
4. A comparison opens: the internal version (with costs and margins) next to what the client will receive. Check it and click **Approve**.

The BOQ becomes **Approved**. The Estimator is notified and then sends it to the client.

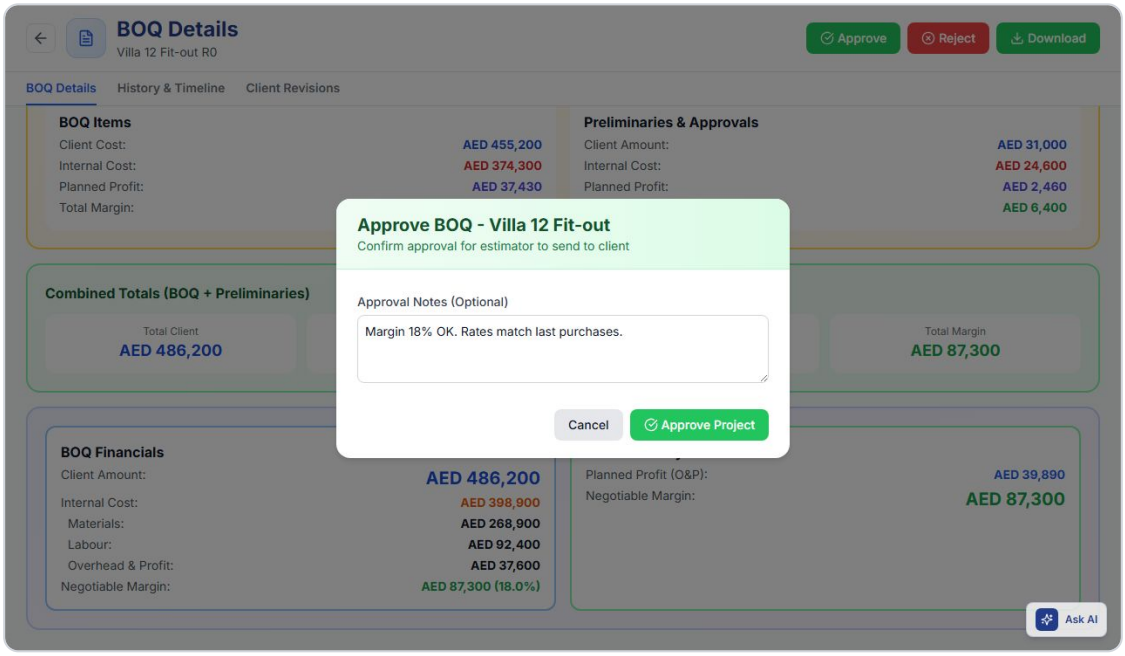


Approve BOQ from BOQ Details

How to reject a BOQ

1. Open the BOQ and click **Reject**.
2. Enter the reason. It is required and goes to the Estimator for corrections.
3. Click **Reject Project**.

The BOQ becomes **Rejected**. The Estimator, and the PM if one forwarded it, are notified.

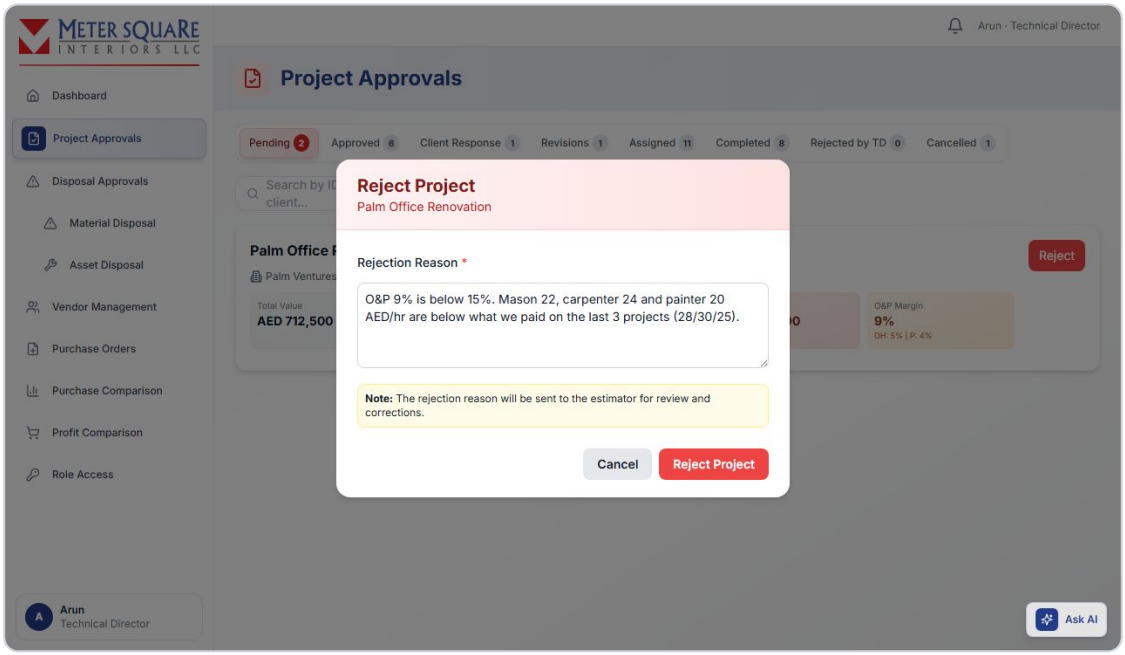


Reject Project

How to review revisions

1. Open the **Revisions** tab and select a project.
2. Compare the revisions under **Client Revisions** or **Internal Revisions**.
3. Click **Approve** or **Reject** (rejecting needs a reason).

Revision	If you approve	If you reject
Internal revision	**Internal Revision Approved**. The Estimator can send it to the client.	**Internal Revision Pending**. It goes back to the Estimator to fix.
Client revision	**Approved**. The Estimator can send it to the client.	**Client Revision Rejected**

An approved revision shows **Approved - Ready for Client**.

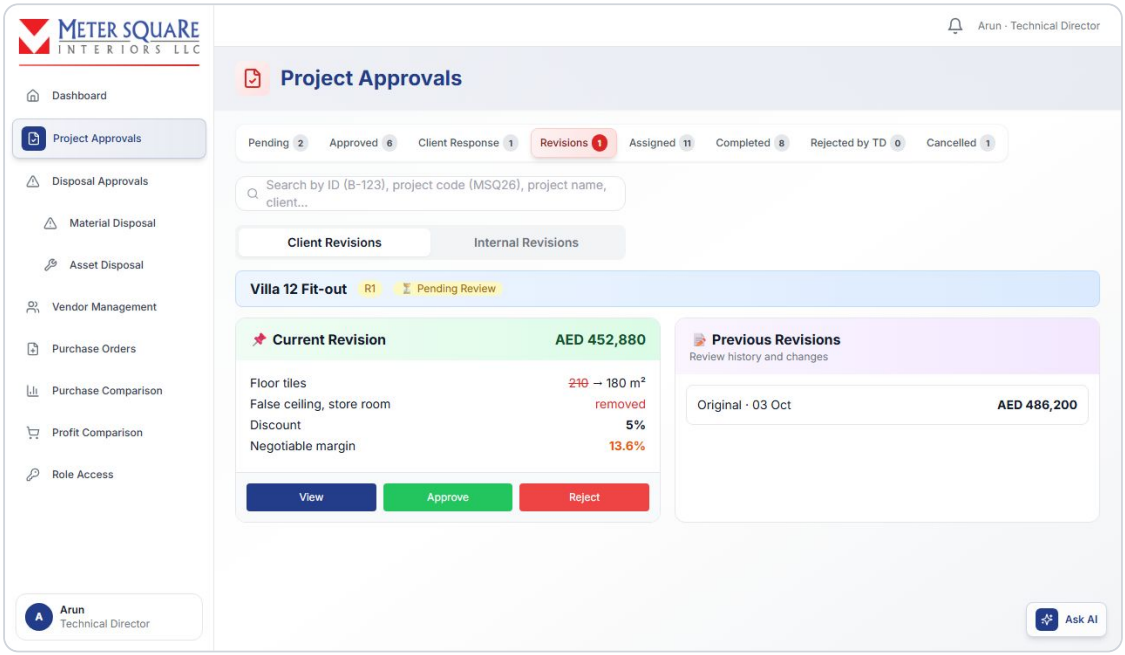

Project Approvals › Revisions › Client Revisions

How to download a BOQ


1. In the BOQ view, click **Download**.
2. Choose the **Internal** version or the **Client** version (without overhead and profit).
3. Choose **Excel** (multiple sheets) or **PDF**.

How to assign a Project Manager and MEP Supervisor

You can assign a PM only after the client has approved the BOQ. The card then shows **Assign PM**.

1. Click **Assign PM**.
2. Choose **Select Existing PM**.
   - Search for a PM. PMs are grouped Online and Offline, and each shows a workload badge: **Available** (0 projects), **Busy** (1–3) or **Overloaded** (more than 3), plus their current projects.
   - You can select more than one PM.
   - People with temporary Project Manager access show a **Granted · until** tag.
3. Optional: in **Assign MEP Supervisor**, all MEP Supervisors are ticked by default. Untick the ones you do not want, or click **Clear**.
4. Click **Assign N PM(s) to Project**.

The project moves to **Assigned** and the PM is notified with the project details. The PM now manages the project, its Site Engineers and its purchasing.

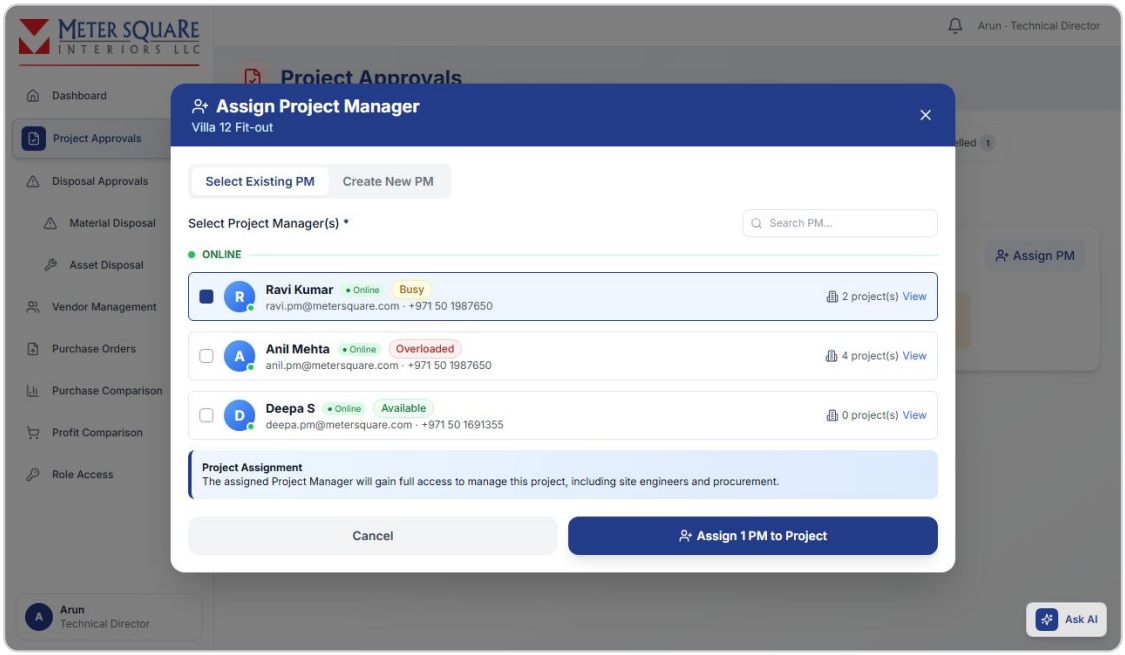

Assign Project Manager

How to create a new PM while assigning

1. In the assign window, choose **Create New PM**.
2. Enter **Full Name**, **Email Address** and **Phone Number**.
3. Click **Create & Assign**.

In this mode no MEP Supervisor is assigned. Assign MEPs separately if needed.

How to delete a Project Manager

Click the bin icon next to the PM in the assign window and confirm. A PM who is assigned to any project cannot be deleted.


How to handle a day extension request

A Project Manager or MEP Supervisor can ask for more days on a project. Assigned projects with pending requests show a blinking clock badge.

1. Click the clock badge on the project card.
2. Review the request: who asked, the current duration and end date, the additional days, the new end date and the reason.
3. Choose an action:
    - **Approve**: the project's duration and end date are extended.

- **Edit**: enter a different number in **Edit Extension Days** and an optional reason, then click **Save Changes**. The request shows "Edited by TD". You must still **Approve** or **Reject** it.
- **Reject**: enter the **Reason for Rejection** and click **Reject**.

The requester is notified.

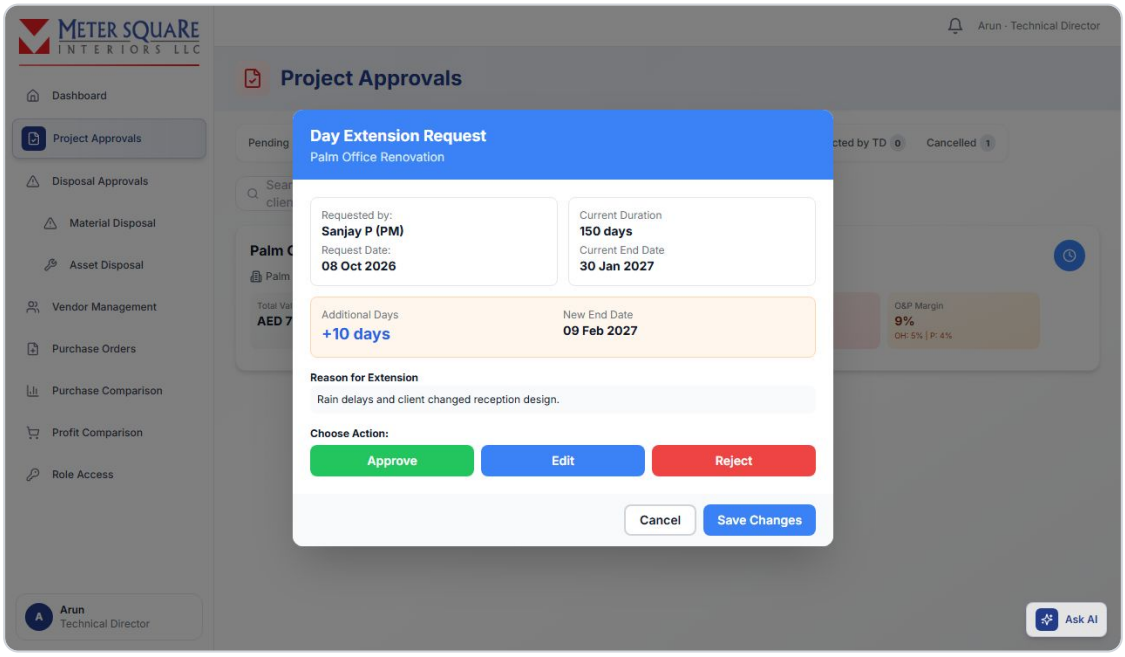

Day Extension Request

Purchase Orders: approving vendor selections

When Procurement chooses a vendor for a material purchase request, the TD must approve that vendor. Open **Purchase Orders → All Orders**.


- **Tabs**: **Vendor Approvals** and **Completed**.
- **Vendor Approvals sub-tabs**:
  - **Pending**: waiting for you.
  - **Approved**: buyers can complete the purchase.
  - **Rejected**: buyers must choose a new vendor.
- A purchase split across several vendors shows one entry per vendor, numbered for example PO-123.1 and PO-123.2.

How to approve or reject a vendor selection

1. In **Pending**, click **Details** to see the vendor, materials and total cost.

2. To approve, click **Approve Request**.
    - The status becomes **Vendor Approved**.
    - The purchase order (LPO) PDF is generated automatically.
    - The buyer is notified and can complete the purchase.
3. To reject, click **Reject**, enter the reason and click **Submit Rejection**. The vendor is cleared and the buyer must choose another vendor.

On approved items, click **View LPO** to see the purchase order details. An approved LPO cannot be edited.

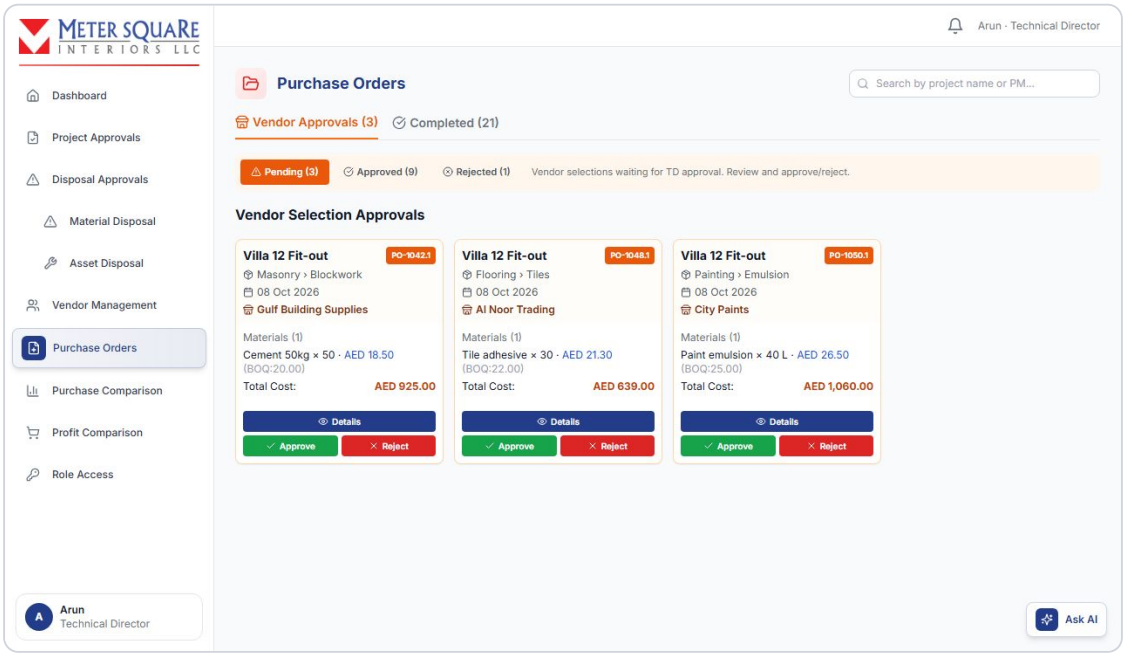

Purchase Orders › Vendor Approvals

Purchase Orders: Return Approvals

When delivered material is rejected, the buyer raises a **vendor return request (VRR)**. Open **Purchase Orders → Return Approvals**.

- **Tabs**: **Pending Return Approvals**, **New Vendor Approvals**, **History** (All, Approved, Rejected, In Progress, Completed).
- Search by VRR number, CR ID, vendor or buyer.
- Each request shows the buyer, vendor, resolution (**Refund**, **Replacement** or **New Vendor**), status, total value and date.


How to approve or reject a return request

1. Expand the request. Review the buyer notes, deadline, inspection details, rejected materials and any credit note.

2. Click **Approve Return Request**. When the resolution is a new vendor, the button reads **Approve Return & New Vendor**.
3. Or click **Reject** and enter the reason.

In **New Vendor Approvals**, review the new vendor's details and the vendor it replaces, then click **Approve Vendor** or **Reject Vendor**.

Return statuses: Pending Your Approval, Approved, Rejected, New Vendor Pending, New Vendor Pending Approval, New Vendor Approved, Return In Progress, Returned to Vendor, Awaiting PM Inspection, Completed.

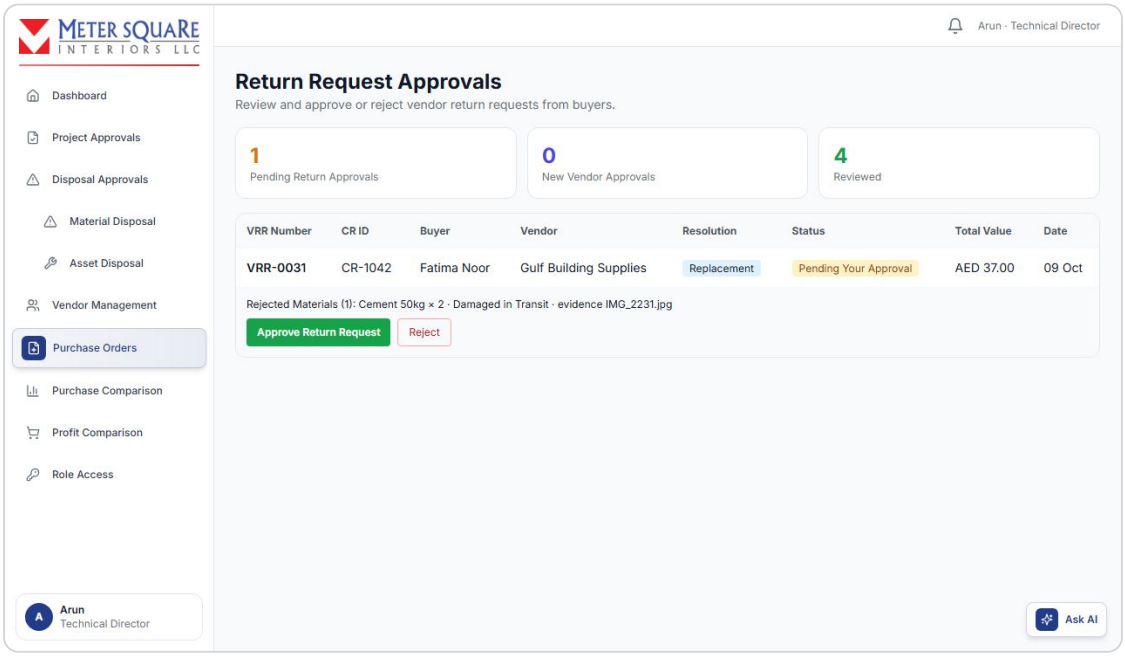

Return Request Approvals


Disposal Approvals

Material Disposal

Open **Disposal Approvals → Material Disposal**. The tabs are **Pending**, **Approved** and **Rejected**. Search by material name, code or requester.

1. Click **View Details**. Review the material, current stock, quantity to dispose, estimated value, reason and justification.
2. Enter **Your Review Notes**. Notes are optional to approve and required to reject.
3. Choose:
   - **Approve Disposal**, then **Yes, Approve Disposal**. The quantity is permanently removed from inventory.

- **Reject & Add to Backup**. The quantity is added to backup stock for repair or reuse.

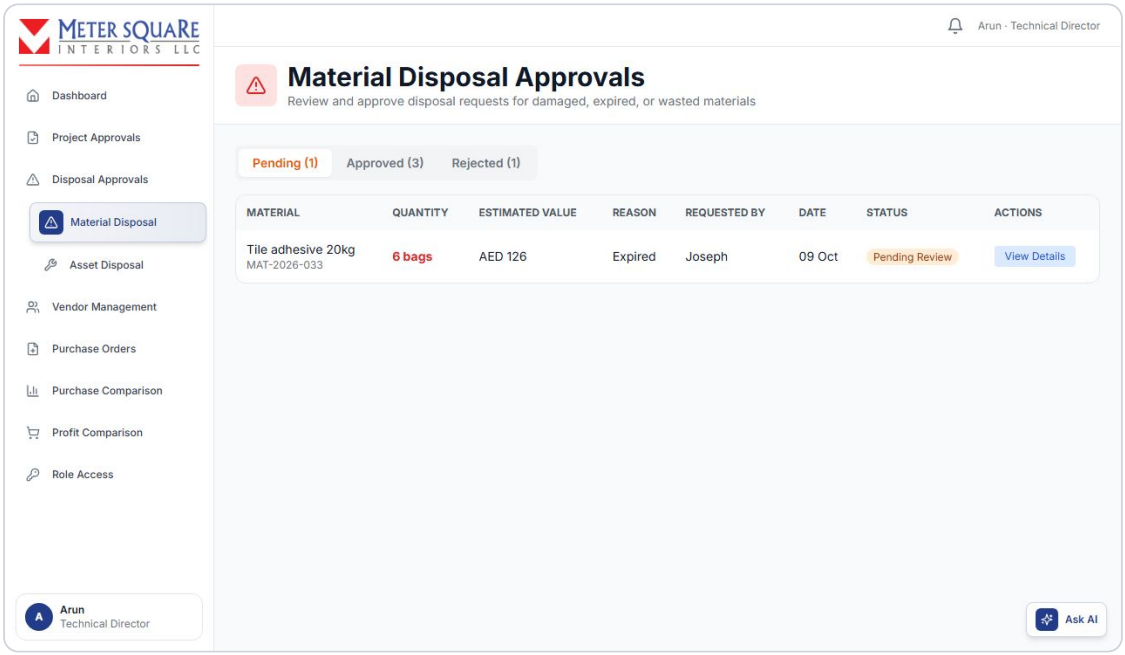

Material Disposal Approvals

Asset Disposal

Open **Disposal Approvals → Asset Disposal**. The tiles show Pending, Approved, Rejected and Pending Value.

1. Open the request. Review the asset, serial number, reason, justification and the evidence photo (click it to enlarge).
2. Choose:
   - **Approve Disposal**, then **Yes, Approve Disposal**. The asset quantity is reduced.
   - **Reject Disposal**. Choose **Return to Stock** or **Send to Repair** and enter review notes (required).

Vendor Management


Open **Vendor Management** to view and manage vendors. This is the same page Procurement uses: see **Procurement → Vendors**. Vendors are marked **Active** or **Inactive**.

The TD approves vendors for each purchase through **Purchase Orders**, not on this page.

Purchase Comparison

Compare planned budget with actual spending.

1. Open **Purchase Comparison** and choose **Live Projects** or **Completed**.
2. Find the project and click **View Comparison**.
3. Each item shows **Planned Budget** next to **Actual Spending**, with a badge: Over Budget, Under Budget, On Budget, Not Purchased or Unplanned.
4. The totals show Total Planned, Total Actual (incl. VAT) and the Balance.
5. Export with **Excel** or **PDF**.

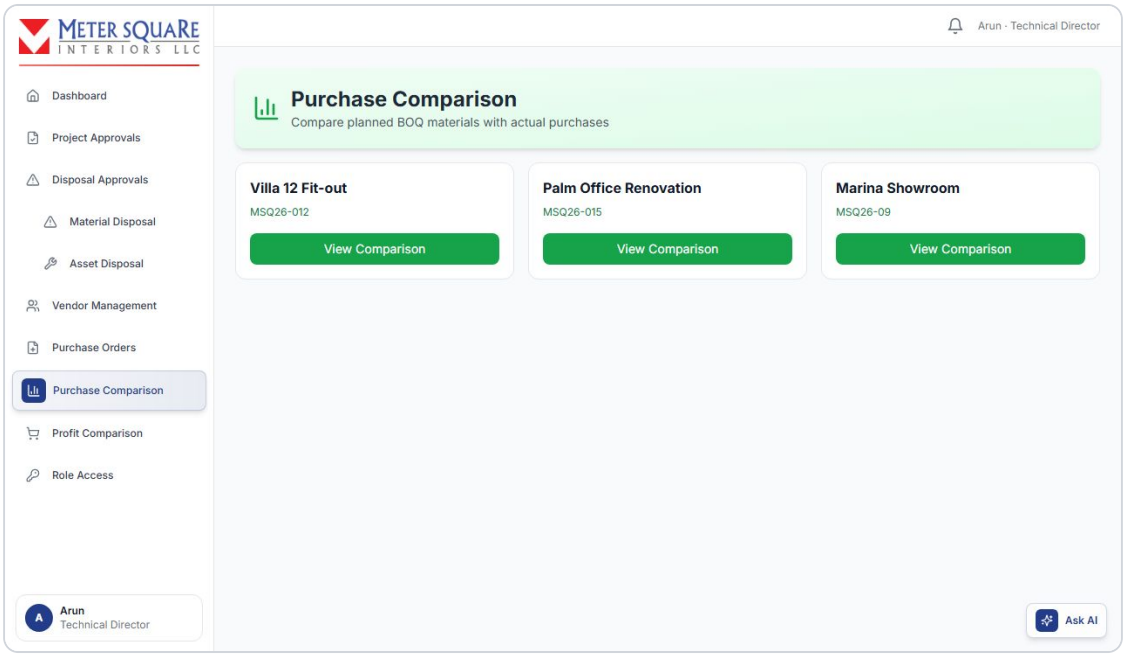


Purchase Comparison

Profit Comparison

Open **Profit Comparison** to compare the original BOQ with actual purchases.

- **Live Projects** / **Completed**: click **View Comparison** on a project.
- **Report**: select a project and click **View Report**. The detailed profit report can be filtered by **Transport**, **Material** and **Labour**.

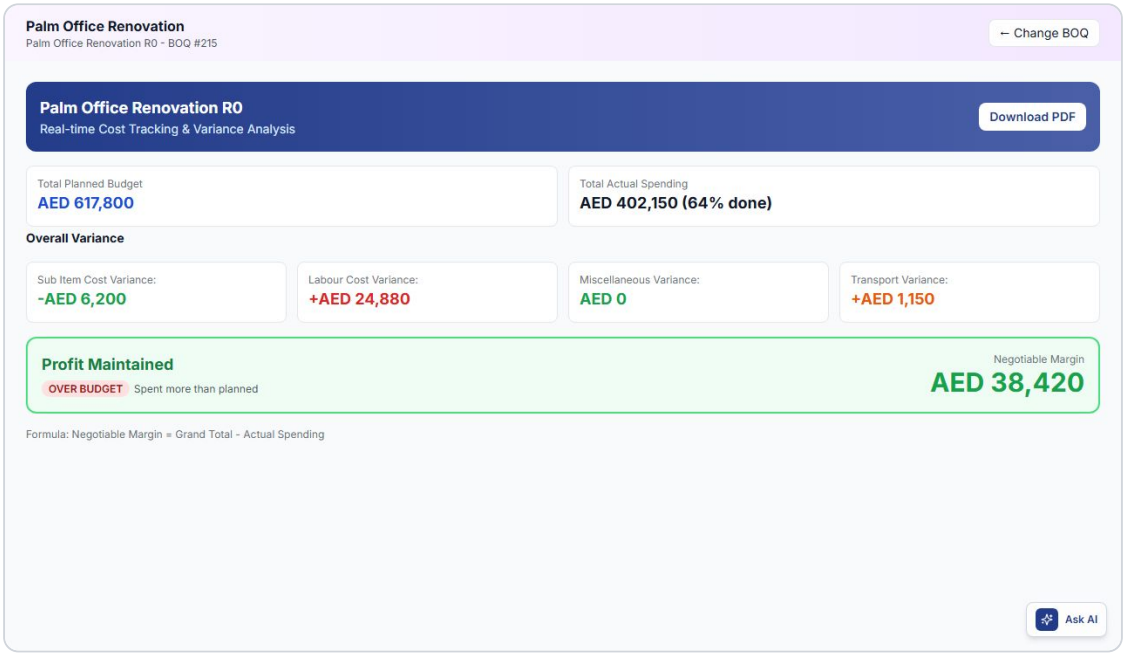

Profit Comparison: planned against actual

Role Access

The TD can give users temporary access to another role, the same as the Admin. In the TD sidebar, click **Role Access** (it is a menu item of its own, not under another menu). The screen and its steps are the same as the Admin's; the full steps are in the Admin chapter, section "Role Access".

The **Role Access** menu is hidden while you are working in a granted role yourself. Click **Switch back to Technical Director** in the amber banner to see it again.

Project Manager and MEP Supervisor

The Project Manager (PM) runs the projects the Technical Director assigned to them:

- assigns Site Engineers and BOQ items;
- approves material purchase requests from site;
- approves asset and labour requests;
- locks attendance for payroll;
- confirms project completion.

The **MEP Supervisor** uses the same screens for the projects where they are assigned as MEP. Everything in this chapter applies to both unless stated.


PM and MEP menu: **Dashboard**, **My Projects**, **Material Purchase**, **Asset Requisition Approvals**, **Labour** (Requisition Approvals, Attendance Lock).

When you act, the person affected gets an in-app notification, and an email only if they are offline.

Dashboard

The **Project Manager Dashboard** (MEP: **MEP Supervisor Dashboard**) shows:

- **Tiles**: Total BOQ Items, Items Assigned, Pending Assignment, Assets Approved, Labour Pending, Labour Approved, Attendance Locked and POs Completed.
- **Charts**: BOQ Status, Labour & Attendance (PM only), Purchase Orders and Asset Requisitions.
- **Recent SE Requests**: the latest requests from your Site Engineers.

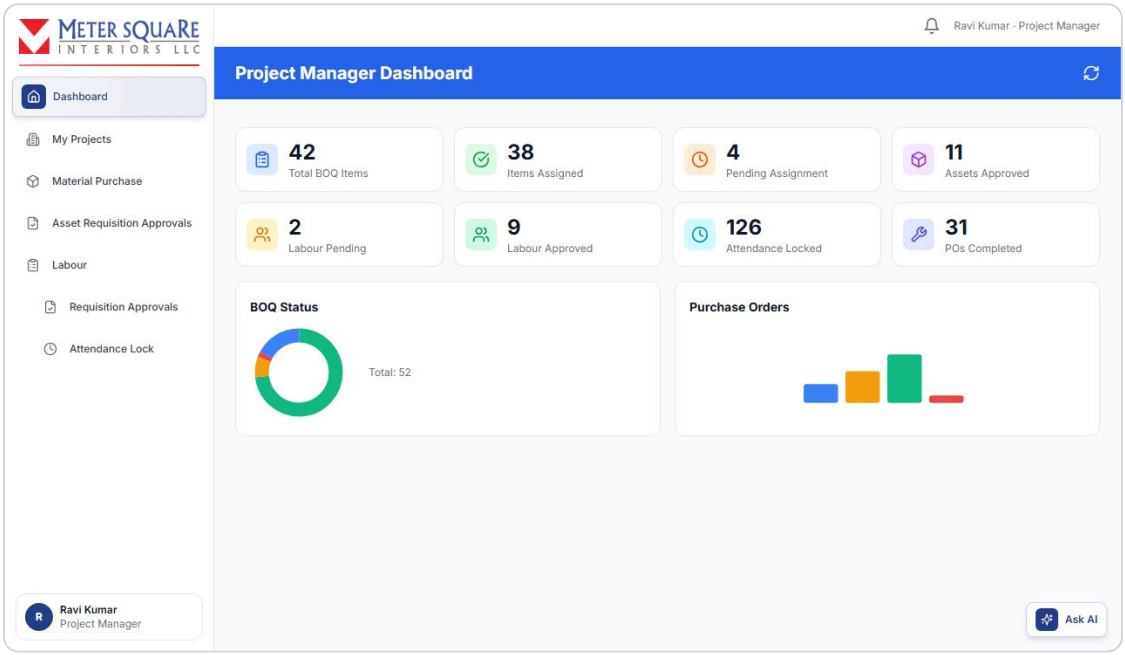

Project Manager Dashboard

My Projects

Open **My Projects**. Search by project, client or location. Switch between card and table view.

Tabs


Tab	What it shows
For Approval	BOQs the Estimator sent to you for review
Pending	Approved projects whose BOQ items are not all assigned yet
Assigned	Projects with items assigned to Site Engineers
Approved	BOQs you approved
Rejected	BOQs you rejected
Completed	Completed projects

Each card shows:

- the project, client and Site Engineer;
- the location, status, start and end date (marked **Extended** after an approved extension);
- the items assigned or still pending.

How to review a BOQ the Estimator sent you

1. In **For Approval**, click the eye icon (**View Details**).
2. Choose:
   - **Edit**: change the BOQ in the full BOQ editor and save.
   - **Approve**: add optional comments and confirm. The BOQ goes back to the Estimator as **PM Approved**, ready to send to the TD.
   - **Reject**: enter the reason. The BOQ goes back to the Estimator as **PM Rejected**.

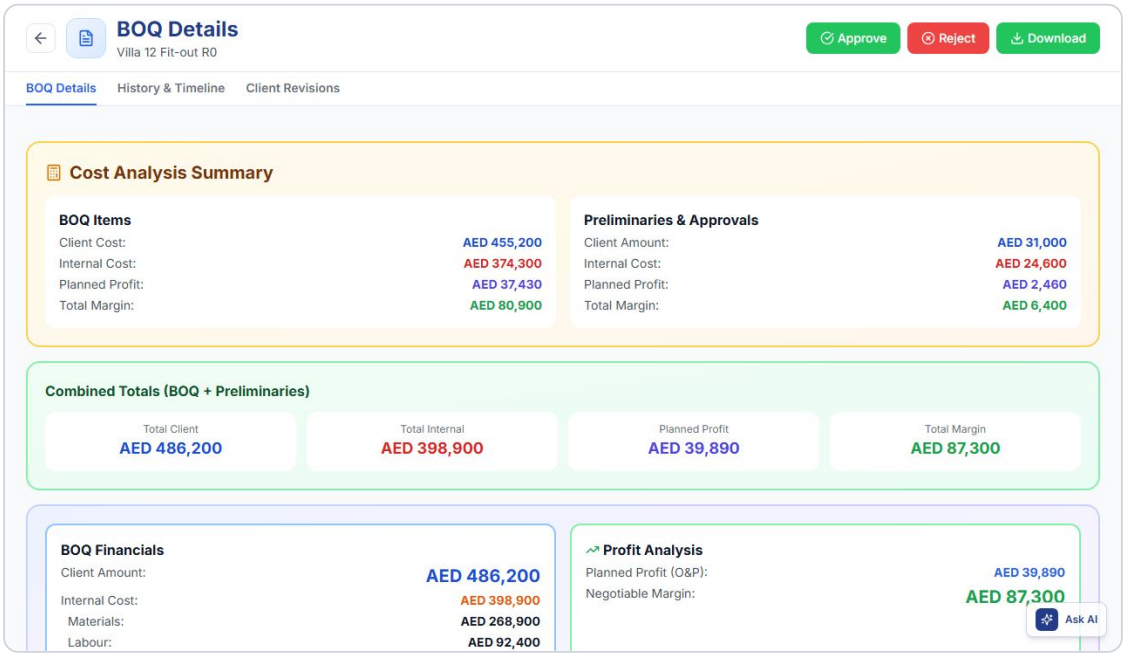

BOQ Details opened from For Approval, with Approve, Reject and Download


How to assign BOQ items to a Site Engineer

In **card view**:

1. On the project card, click **Assign Items to Site Engineer**. It is greyed out when all items are already assigned.
2. On the left, choose **Select Existing SE** and pick a Site Engineer. Each one shows their current projects.
   - Or choose **Create New SE**: enter Full Name, Email and Phone, then click **Create & Select SE**.
3. On the right, under **Items to Assign**, tick the items. Picking an SE selects all items; untick any you want to give to someone else. Already assigned items are listed under **Assigned Items**.
4. Click **Confirm Assignment**.

In **table view**, a project with no Site Engineer yet shows **Assign Site Engineer**. It assigns one Site Engineer to the whole project. Here, people with temporary Site Engineer access show a **Granted · until** tag.

The Site Engineer is notified, and the project moves to **Assigned**. Each Site Engineer can be assigned to at most **3 projects**.

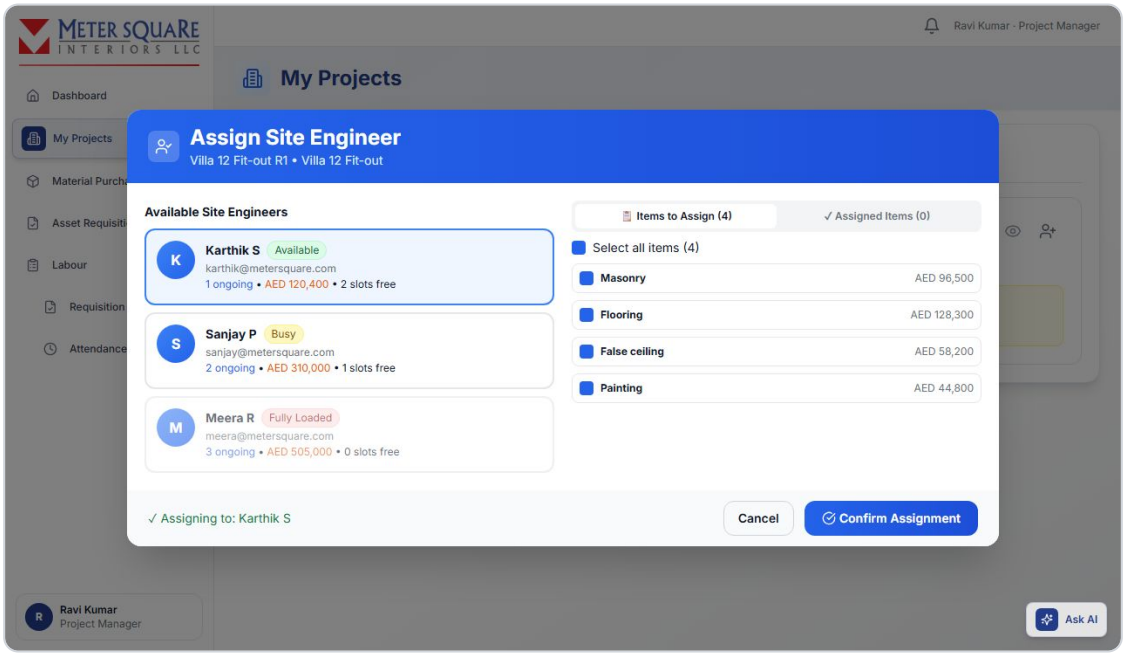

Assigning BOQ items to a Site Engineer

How to edit or remove a Site Engineer

On the project card, use the icons next to the Site Engineer's name:

- **Edit Site Engineer Details**: change the Full Name, Email or Phone, then click **Save Changes**.
- **Delete Site Engineer**: confirm **Delete**. This removes the user from the system.

How to confirm project completion

When Site Engineers finish, they request completion.

In **card view**:


1. Click the **x/y confirmations** button on the card. It pulses orange when a Site Engineer has requested completion.
2. The panel lists each Site Engineer assignment with one of: "SE requested completion", "Awaiting SE completion request" or "PM confirmed".

3. Click **Confirm Complete** for each finished assignment.

In **table view**, click **SE Requested Completion - Click to Approve**, then **Confirm Complete** in **Approve Completion Request**.

When everyone has confirmed, the project is marked complete automatically ("Project automatically marked as complete!"). The BOQ appears in the Estimator's **Completed BOQ** tab.

The project does **not** complete while any material purchase in the project is still unfinished or any asset return is still open. You then see "Project will auto-complete when all purchases and returns are finished".

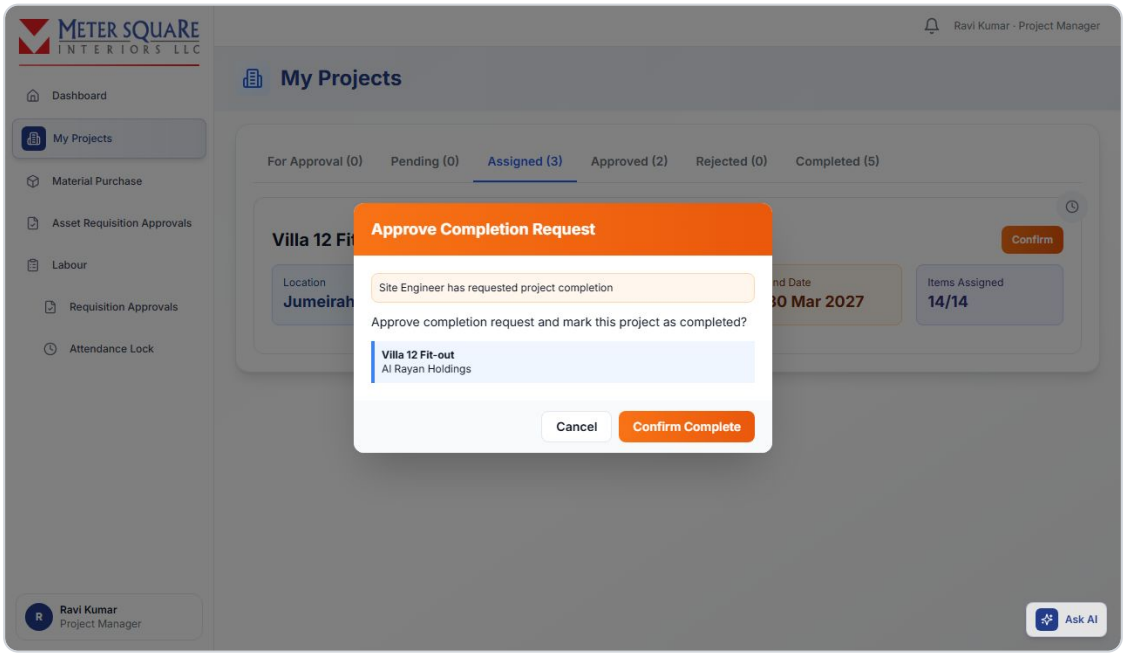


Approve Completion Request

How to request a day extension

1. Open the BOQ and click **Request Extension**, or click the clock badge on an assigned project card.
2. Enter **Additional Days Requested**. The new end date is previewed.
3. Enter the **Reason for Extension**.
4. Click **Send Request**.

The Technical Director is notified and approves, edits or rejects it. You cannot send another request while one is pending. The request history shows Pending TD Approval, Approved or Rejected.

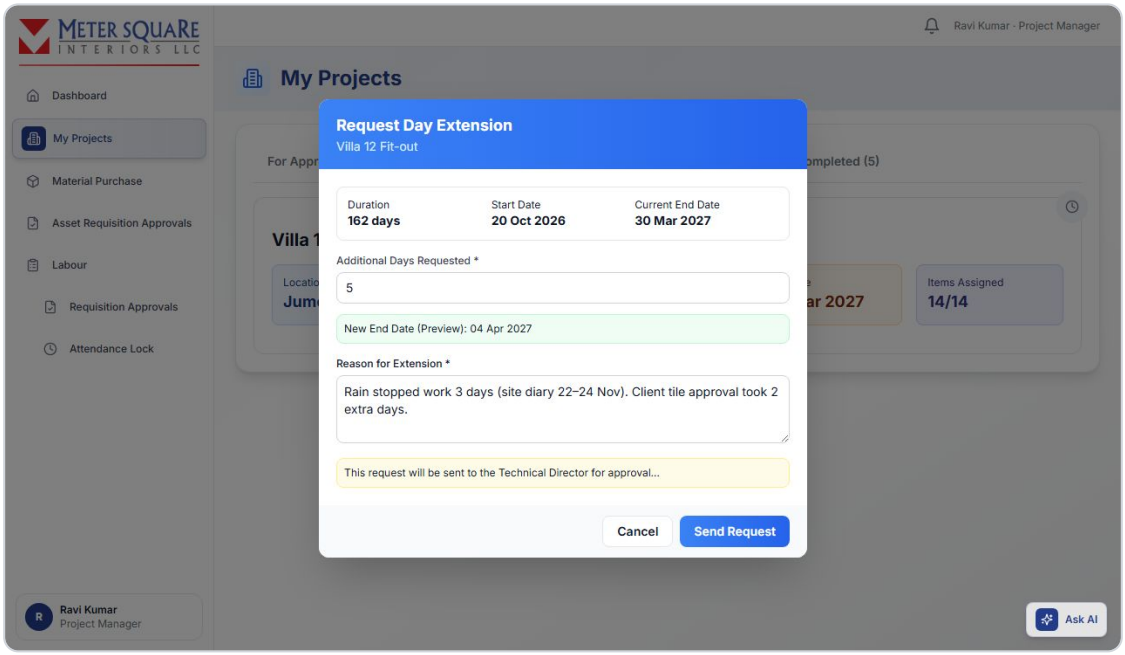

Request Day Extension

Material Purchase (change requests)

Site Engineers and PMs request extra materials for an approved project through **Material Purchase**. These requests are also called change requests (CR) or purchase requests (PO-...).

In the Project Manager view, prices are hidden. The MEP Supervisor sees prices.

How a material purchase request moves

1 **Site Engineer**	Creates the request and clicks Send to PM
▼	
2 **Project Manager**	Approves (or rejects with a reason)
▼	
3 **Estimator**	Prices and approves requests that contain new materials, then picks a buyer
▼	
4 **Procurement**	Selects the vendor
▼	
5 **Technical Director**	Approves the vendor selection
▼	
6 **Procurement**	Sends the purchase order and completes the purchase
▼	
7 **Production Manager**	Receives the delivery at the M2 Store and dispatches it to site
▼	
8 **Site Engineer**	Confirms delivery on site

Routing rules:

- If the request contains **new materials** (not in the BOQ), approval sends it to the **Estimator** first. Materials picked **From Catalogue** count as new.
- If **all materials are existing BOQ materials**, approval sends it **directly to a buyer** you choose.
- If an **MEP Supervisor** assigned the item to the Site Engineer, the request goes to that MEP instead of the PM.


Tabs

Tab	What it shows
SE Requested	Requests from your Site Engineers waiting for your approval
My Requests	Your own requests: **Drafts (Not Sent)**, **Sent to Estimator**, **Sent to Buyer**
Accepted	Approved requests in progress (with the Estimator, buyer or TD, or sent to the store)
Completed	Purchase completed or routed to the M2 Store


Tab	What it shows
Rejected	Rejected requests, with the reason and who rejected it

How to approve or reject a Site Engineer's request

1. In **SE Requested**, click **Review Details**. Use **Edit** to change quantities or materials if needed.
2. Approve it:
   - **Approve & Send to Estimator** is shown when the request has new materials. The Estimator is notified.
   - **Approve & Send to Buyer** is shown when all materials are existing. Choose the buyer under **Assign to Procurement**. Buyers are grouped Online and Offline; an offline buyer gets an email; people with temporary Procurement access show a **Granted** tag. Add optional comments and click **Approve & Assign**.
3. Or click **Reject**, enter the reason and click **Submit Rejection**. The Site Engineer is notified.

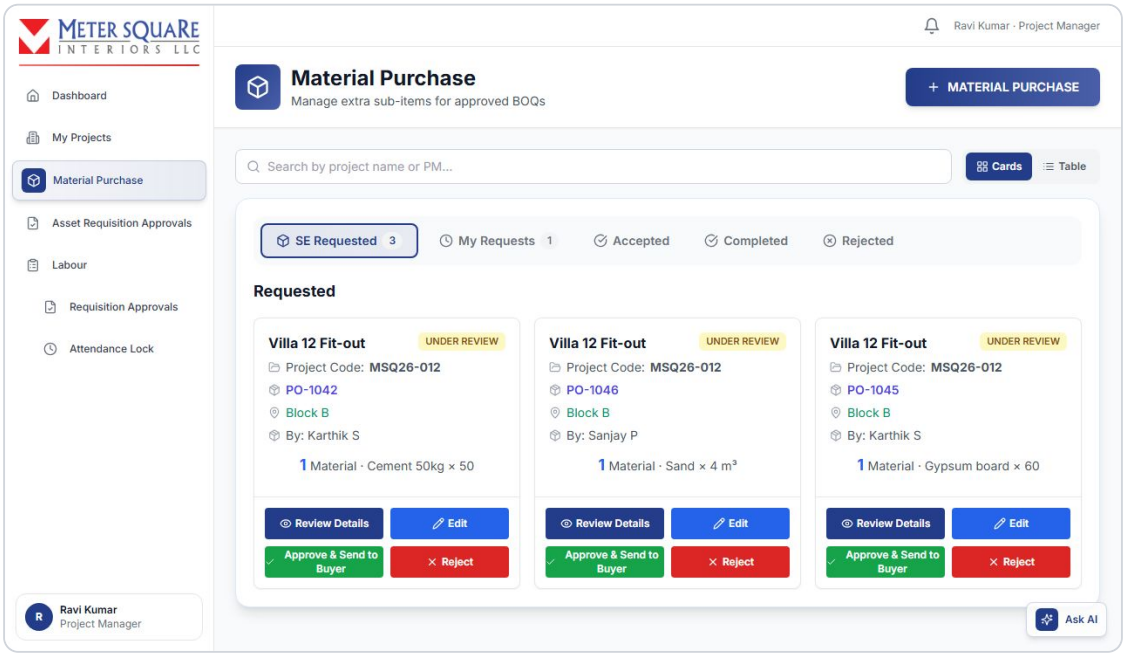

SE Requested: requests waiting for the Project Manager

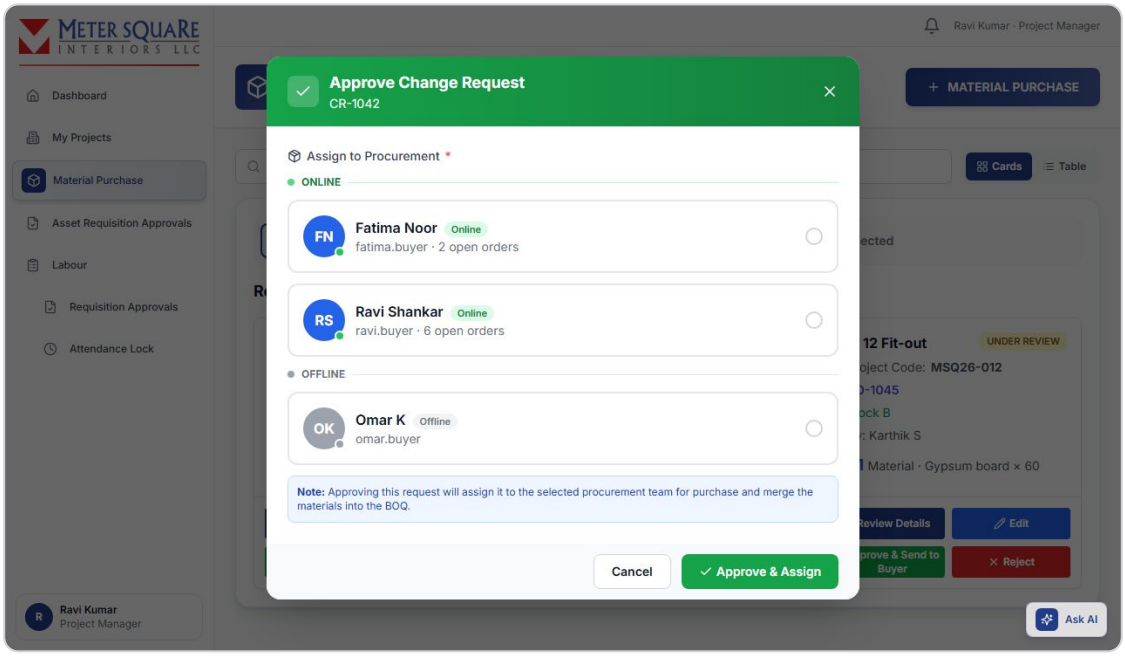

Approve Change Request: choosing the buyer under Assign to Procurement

How to create your own material purchase request

1. Click **MATERIAL PURCHASE**.
2. On the **Materials** tab, select the **Project Name**, **Area**, **BOQ**, **BOQ Item** and **Sub-Items (Scopes)**.
3. For each sub-item, add materials in one of two ways:
   - **Select Material**: pick an existing material from the BOQ.
   - **Add New** for a material not in the BOQ, then choose **From Catalogue** (search by name, brand or category) or **Enter Manually** (name and optional brand, size and specification).

   One request uses one way only. Once a sub-item uses **Select Material**, **Add New** is disabled for the others ("Another sub-item is using … mode"), and the other way round. Put existing and new materials in separate requests.

   Existing BOQ materials are tagged **BOQ**, new ones **NEW**. Fully used materials show "Fully Consumed".
4. Enter the **Request Quantity** and **Unit** for each material. The quantity cannot exceed what is allocated in the BOQ.

5. Write a **Justification** (at least 10 characters):
    - one for each new material;
    - one common justification for the existing materials.
6. Optional: add **Remarks**.
7. Click **Create Purchase Request**. The request is saved as a draft under **My Requests → Drafts (Not Sent)**.

How to send your draft


In **Drafts (Not Sent)**, click:

- **Send to Estimator** when the request has new materials, or
- **Send to Buyer** when all materials are existing. Choose the buyer and click **Approve & Assign**.

How to request preliminaries

On the **Preliminaries** tab of **MATERIAL PURCHASE**:

1. Choose from the preliminaries selected in the BOQ.
2. Enter the **Purchase Amount (AED)** and an optional justification and remarks.
3. Click **Create Request**. It is saved as pending and can be sent to a buyer later.

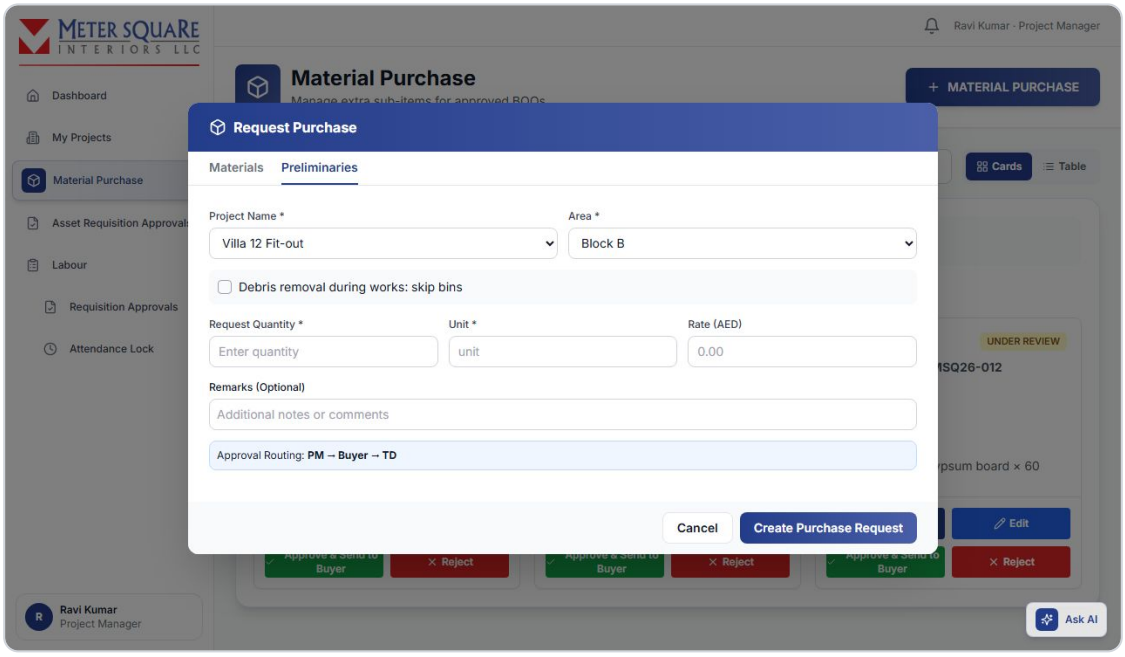

Request Purchase: the Preliminaries tab

Change request statuses


Status shown	Meaning
Pending	Created, not yet sent
PM Approval Pending	Sent by the Site Engineer, waiting for the PM (or the MEP Supervisor)
Estimator Approval Pending	Waiting for the Estimator to price new materials
TD Approval Pending	Buyer chose a vendor. Waiting for TD vendor approval.
Under Review	Waiting for another approver
APPROVED BY PM	Approved by the PM
SENT TO ESTIMATOR	Approved by the PM/MEP. New materials need pricing.
SENT TO BUYER / ASSIGNED TO BUYER	With a buyer for purchase
APPROVED BY TD	Approved by the Technical Director
VENDOR APPROVED	TD approved the vendor. Buyer can complete the purchase.
ROUTED TO M2 STORE	Purchase completed. Vendor delivers to the M2 Store.
PURCHASE COMPLETED	Delivery received at the store and processed
REJECTED	Rejected, with the reason shown

When a buyer splits a purchase across vendors, the request shows a **Split into N Vendors** box with the state of each vendor order (Completed, Vendor Approved or Pending TD).

Asset Requisition Approvals

Site Engineers request returnable assets (tools and equipment) for site. Open **Asset Requisition Approvals**. The tabs are **Pending**, **Approved** and **Rejected**.

1. Review the request: purpose, required date, site location, assets and urgency.
2. Click **Approve** (optional notes). It goes to the Production Manager for final approval and dispatch.
3. Or click **Reject** and enter the **Rejection Reason**. The Site Engineer can edit and resend it.

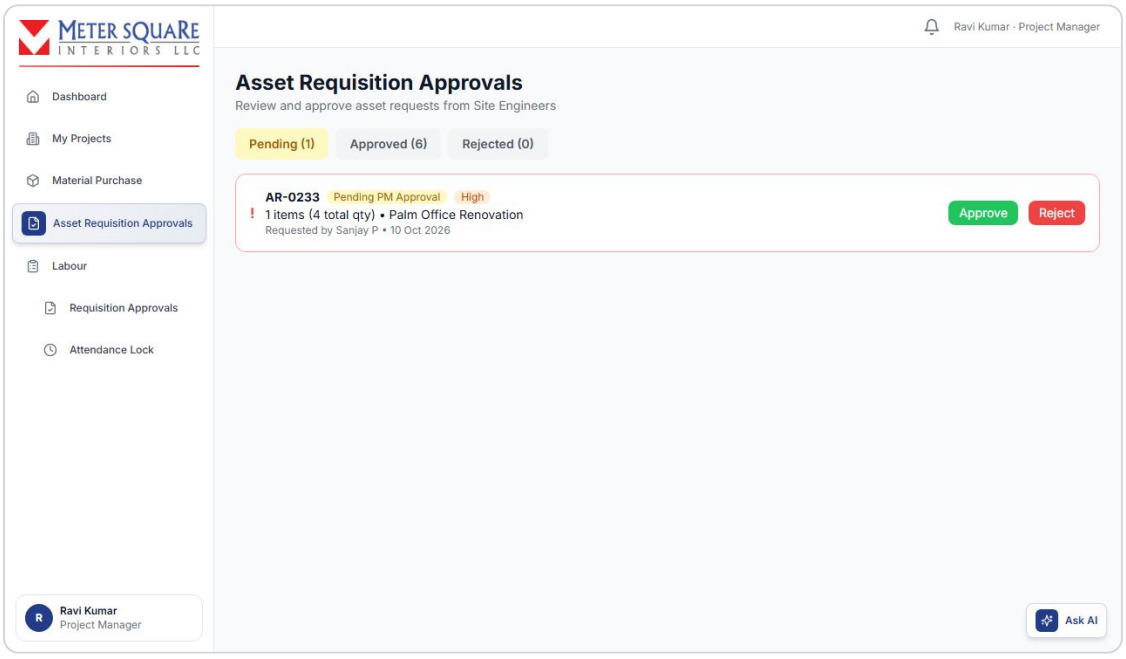

Asset Requisition Approvals


Labour: Requisition Approvals

Open **Labour → Requisition Approvals**. Tabs: **My Pending**, **SE Pending**, **Approved**, **Rejected**.

How to approve Site Engineer labour requests

1. In **SE Pending**, click **View** to see the labour items, number of workers, dates, shift and preferred workers.

2. Click **Approve**. It goes to the Production Manager to assign workers.
3. Or click **Reject** and enter the reason. The Site Engineer can edit and resend it.

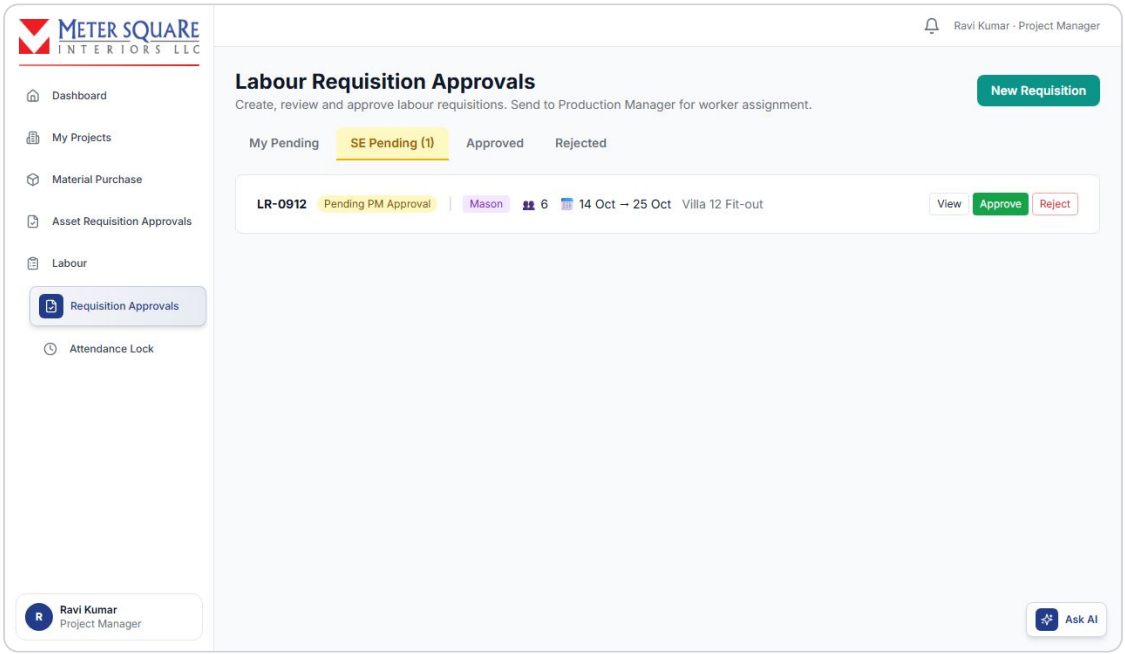

Labour Requisition Approvals: SE Pending

How to create your own labour requisition

1. Click **New Requisition**.
2. Select the **Project**. The site is filled in automatically.
3. Enter the **Start Date**, **Start Time** and **End Time**. The end date is calculated; for a night shift it becomes the next day.
4. Optional: choose **Preferred Workers**.
5. Choose the labour items from the project's BOQ and set the number of workers for each.
6. Click **Create N Requisition(s)** (N is the number of labour items). One requisition is created holding all the items.
7. In **My Pending**, click **Send to Production**. The Production Manager is notified to assign workers.


Labour: Attendance Lock

Locked attendance is what goes to payroll. Open **Labour** → **Attendance Lock**.

1. Choose the **Project** (default: All Projects) and, optionally, a **Date**.

2. Review the records in **Pending Lock**: worker, clock in/out, hours, overtime and cost. Click **View** for the full detail (regular and overtime hours, rate, break, overtime multiplier, total cost).
3. Lock the records you have checked:
   - **Lock** on one row, or
   - tick rows and click **Lock Selected**, or
   - **Lock All for Day**, shown once you have chosen both a project and a date.

Locked records move to **Locked** and the Admin is notified for payroll. Only locked attendance appears in **Payroll Processing**.

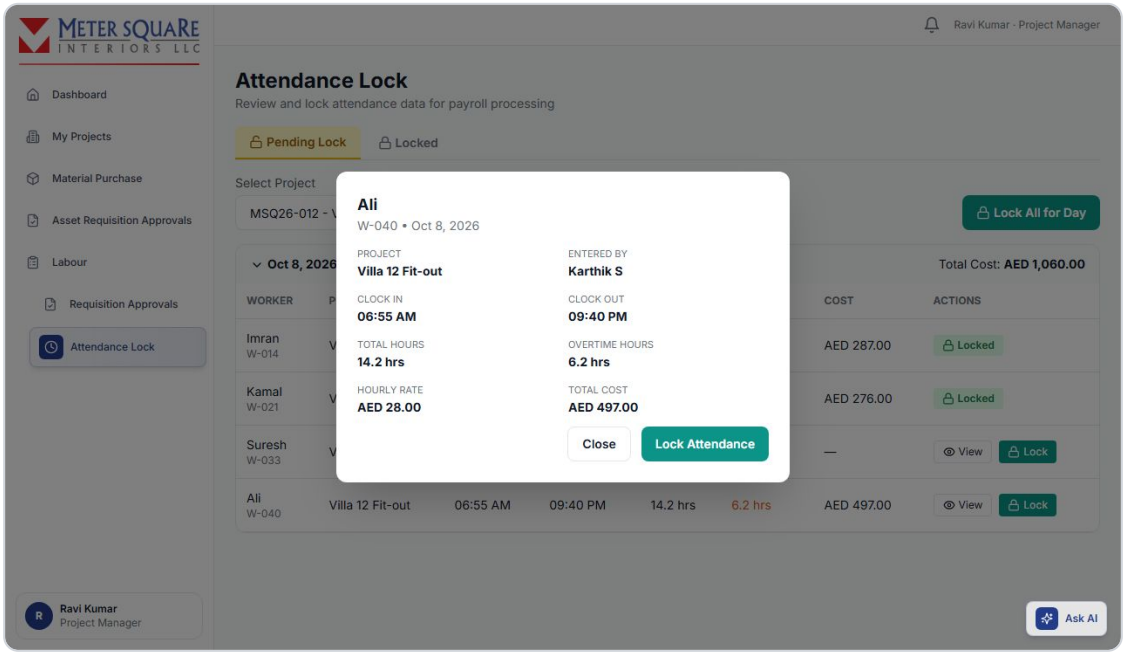

Attendance Lock: one record opened with View

How hours and cost are calculated

- **Total hours** = clock-out time minus clock-in time, minus breaks.
- **Overtime** = time worked after the requisition's shift end time. If no shift was set, overtime is anything over 8 hours.
- **Cost** = regular hours × rate + overtime hours × rate × 1.5.

Site Engineer

The Site Engineer (SE) works on site. They:

- see the BOQ items assigned to them;
- request extra materials;
- confirm deliveries from the M2 Store and return unused materials;
- request and return assets (tools and equipment);
- request labour and record worker attendance;
- ask the PM to mark the project complete.

Site Engineer menu:


- **Dashboard**
- **Projects**
- **Site Assets**
- **Material Receipts**
- **Material Purchase**
- **Labour**: Labour Requisition, Arrival Confirmation, Attendance Logs

You can sign in with your email or, if a phone number is saved on your account, by SMS (choose **Phone (SMS)** at sign-in).

Site Engineer Dashboard

- **Header**: your efficiency percentage and a period selector (7, 30 or 90 days).
- **Performance**: Project Completion, Item Completion and CR Approval Rate.
- **Cards**:
  - Projects (active / completed)
  - BOQ Items (pending / completed)
  - Change Requests (pending / cost)
  - Labour Reqs (pending / workers)
  - Assets at Site (dispatched / returned)
  - Deliveries (in transit / delivered)
- **Attention Required**: overdue projects, pending items, pending labour and pending asset returns.

- **Charts**: work overview, labour requisitions, asset flow and change request activity.

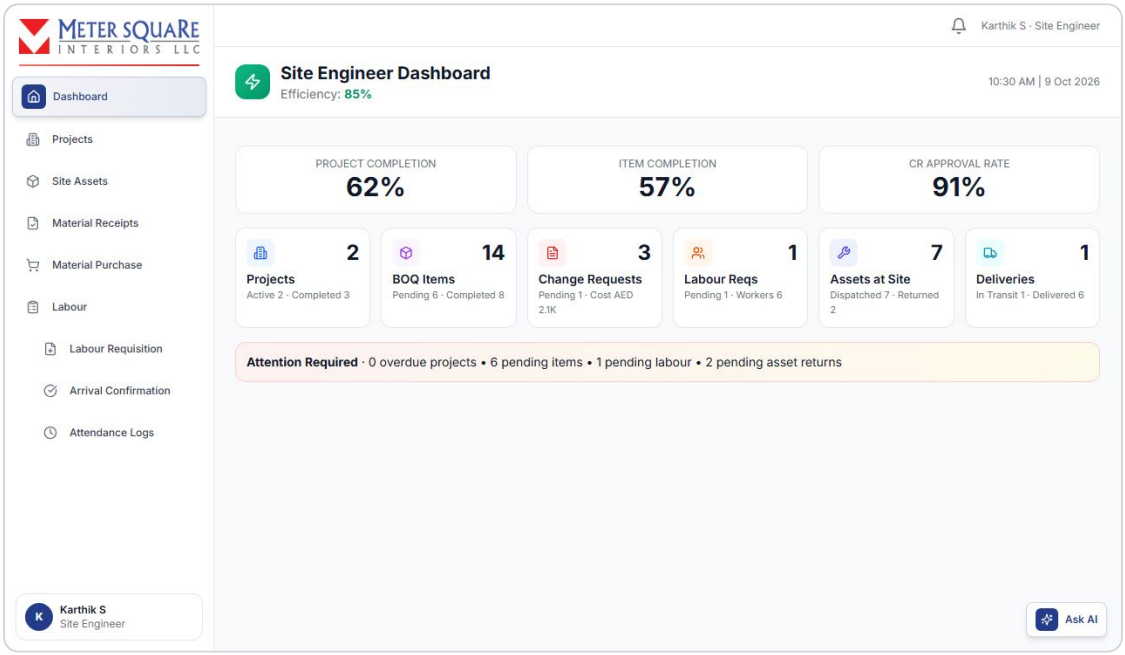

Site Engineer Dashboard

Projects

Open **Projects** (My Projects). The tabs are **Ongoing** and **Completed**. Each card shows the project, client, dates, location and status.

How to see the work assigned to you


Click the eye icon (**View Details**) on a project. You see the BOQ items your Project Manager assigned to you, with their materials and labour. Materials added later through purchase requests are marked **New Material Purchase**.

If you see "No Items Assigned Yet", ask your Project Manager to assign BOQ items to you.

How to request project completion

1. Click **Request Completion** on the project. It appears once items are assigned.
2. If purchases or asset returns are still open, you see **Cannot Request Completion** with the list of incomplete purchases and returns. Finish those first.
3. Otherwise click **Send Request**.

The card shows **Pending Approval**. When your PM confirms, it shows **Confirmed**. The project is **Done** when everyone has confirmed and every purchase and asset return in the project is finished, so your card can show **Confirmed** while the project is not yet **Done**.

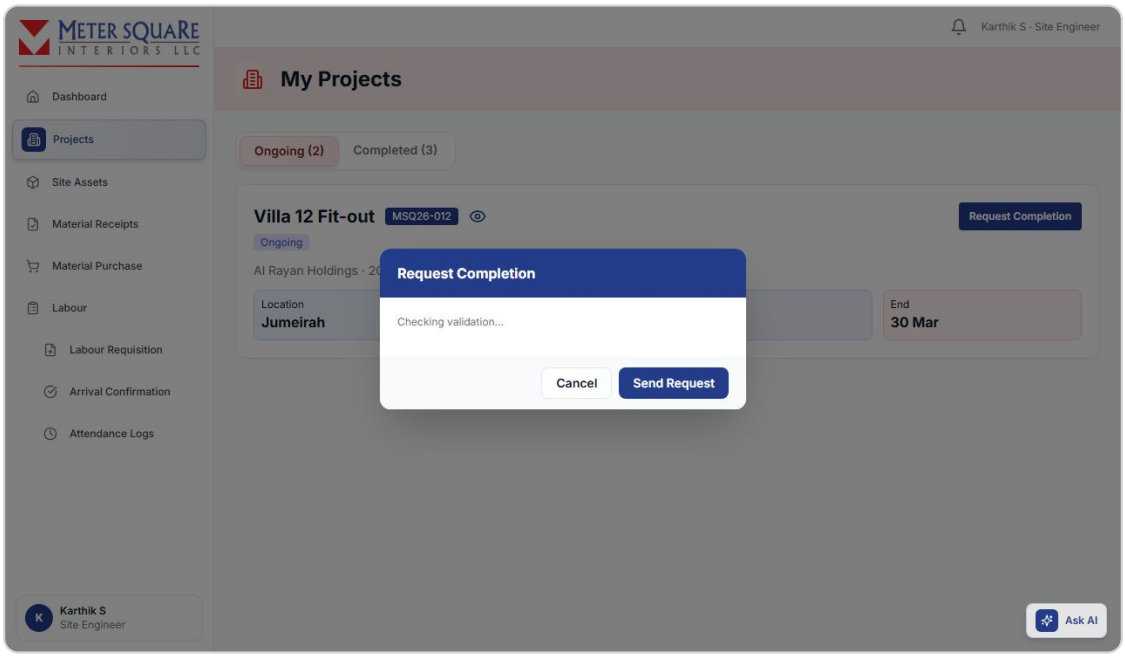

My Projects with Request Completion

Material Purchase (requesting extra materials)

Use **Material Purchase** when site needs materials for an assigned project.

How to request materials


1. Open **Material Purchase** and click **MATERIAL PURCHASE**.
2. Select **Project Name**, **Area**, **BOQ**, **BOQ Item** and one or more **Sub-Items (Scopes)**. If earlier requests exist for this item, they are shown so you do not duplicate them.
3. For each sub-item, the **BOQ Materials Allocation Status** shows how much is allocated, already requested or purchased, and still available.
4. Add materials in one of two ways:
    - **Existing BOQ material**: pick it from **Select Material** and enter the **Request Quantity**. You cannot request more than the BOQ allocation.

- **New material**: click **Add New**, then **From Catalogue** (search by name, brand or category) or **Enter Manually**. Enter the name, optional brand, size and specification, the **Request Quantity**, the **Unit**, and a **Justification** of at least 10 characters. Materials picked from the catalogue also count as new.

One request uses one way only: once a sub-item uses **Select Material**, **Add New** is disabled for the others, and the other way round. Put existing and new materials in separate requests.

5. For existing materials, write a **Common Justification for Existing Materials** (at least 10 characters).
6. Optional: add **Remarks**.
7. The **Approval Routing** box shows where the request will go:
   - new materials (including catalogue materials): SE → PM → Estimator → Buyer → TD;
   - existing BOQ materials: SE → PM → Buyer → TD.
8. Click **Create Purchase Request**.

The request is saved in the **Pending** tab. It has not been sent yet.

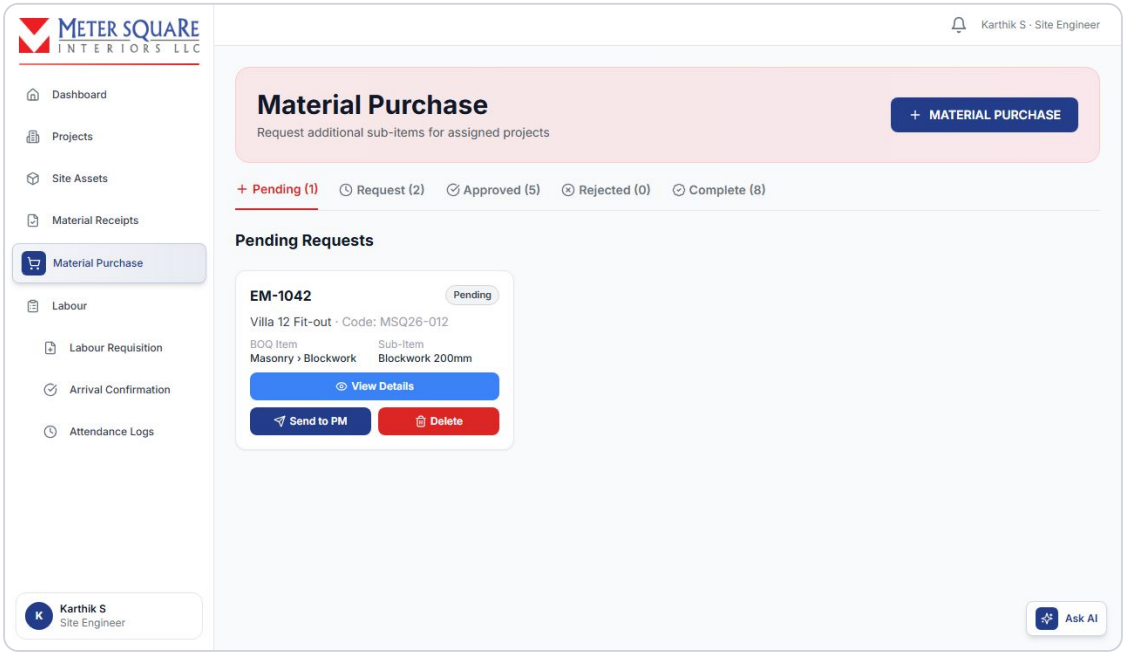

Material Purchase: a request in Pending with Send to PM

How to send a request for approval

In the **Pending** tab, click **Send to PM** on the request. It goes to the person who assigned you the item: your Project Manager, or the MEP Supervisor for MEP items.

Before you send it, you can **Edit** the request, or click **Delete** to remove it.

Tabs

Tab	What it shows
Pending	Created, not yet sent
Request	Sent and waiting for PM approval
Approved	Approved and moving through purchasing
Rejected	Rejected, with the reason
Complete	Purchased and routed to the M2 Store

Request statuses you will see

Label	Meaning
Pending	Not yet sent
PM Approval Pending	Waiting for your PM
PM Approved - Under Review	PM approved, next approver reviewing
Sent to Estimator	New materials being priced
Sent to Buyer	Sent to Procurement
Awaiting Purchase	Assigned to a buyer, purchase not started
TD Approval Pending	Waiting for the TD to approve the vendor
TD Approved - Final Review	The TD approved; final checks before purchase
Approved	Approved
Vendor Approved	Vendor approved, purchase in progress
Split to Vendors	Bought from more than one vendor
Sent to M2 Store	Purchased. The vendor delivers to the store, then it comes to you.

Label	Meaning
Purchase Complete	Purchase finished
Rejected	Rejected, with the reason

Request numbers appear as **EM-**.


Material Receipts (deliveries and returns)

Open **Material Receipts**. Tabs: **Pending**, **Materials** (Returnable Materials, Return Delivery Notes), **History** (Material Returns, Received Deliveries).

How to confirm a delivery

1. In **Pending**, find the Delivery Note (DN). Deliveries are grouped by project and marked In Transit, Dispatched or Issued.
2. Expand it to check where it came from (usually the M2 Store), the vehicle and driver details, and the materials. Click **Download PDF** to keep a copy.
3. When the materials arrive, click **Confirm Receipt**.
4. Optional: add **Notes** about the delivery.
5. Click **Confirm Receipt** in the window.

The delivery becomes **Delivered**. The buyer and the Production Manager are notified, and the materials become returnable.

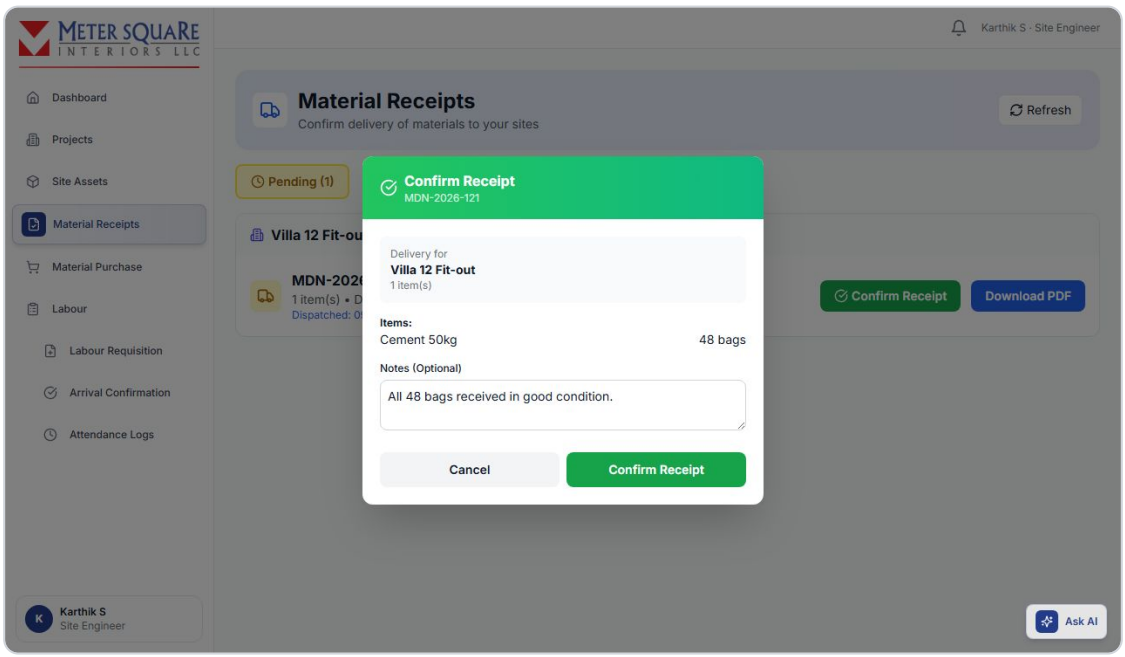

Confirm Receipt on a delivery note


How to return unused or damaged materials

Step 1: select the materials

1. Open **Materials → Returnable Materials**. The table shows each material, its original DN, and the quantities dispatched, returned and returnable.
2. Click **Select Materials** for the project.
3. Tick the materials. For each one, split the quantity by condition:
   - **Good**
   - **Damaged**: describe the damage (required).
   - **Defective**: describe the defect (required).
4. Optional: add a return reason.
5. Click **Save Selection**.

Step 2: create the Return Delivery Note (RDN)

1. Click **Create RDN**.
2. Enter the **Return Date** and **Driver Name** (required), plus the **Vehicle Number**, **Driver Contact** and transport fee.
3. Upload the delivery document (required; PDF, JPG, PNG or DOC, up to 10 MB). Add notes if needed.
4. Click **Create RDN**. It is created as a **Draft**.

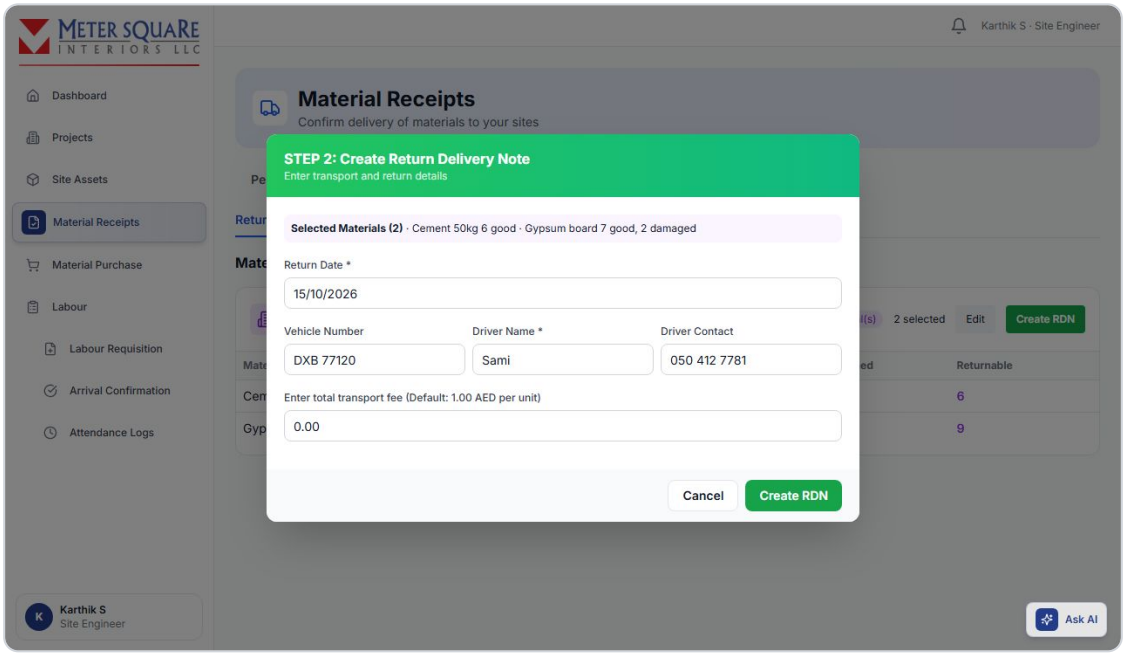

Step 2: Create Return Delivery Note

Step 3: issue and dispatch

1. In **Return Delivery Notes**, click **Issue**. You can download the RDN PDF.
2. When the vehicle leaves, click **Dispatch**. The RDN becomes **In Transit**.

The Production Manager receives it at the store.

- **Good** material goes back into stock.
- **Damaged** or **Defective** material goes for repair or, with TD approval, disposal.

Follow the outcome in **History** → **Material Returns** (Pending Review, Approved for Disposal, Disposed, Repaired).


Site Assets (tools and equipment)

Open **Site Assets**. Tabs: **My Assets**, **Requisitions**, **Rejected**, **Returns**, **History**.

How to request assets

1. Click **Request Asset**.
2. Select the **Project** and add one or more items (asset category and quantity).
3. Enter the **Required Date**, **Urgency** (Low, Normal, High or Urgent), **Purpose / Justification** and **Site Location**.
4. Click **Submit Request**. It is saved as a **Draft**.
5. In **Requisitions**, click **Send for Approval** and confirm **Send to PM**.

The request goes to your Project Manager, then to the Production Manager for dispatch.

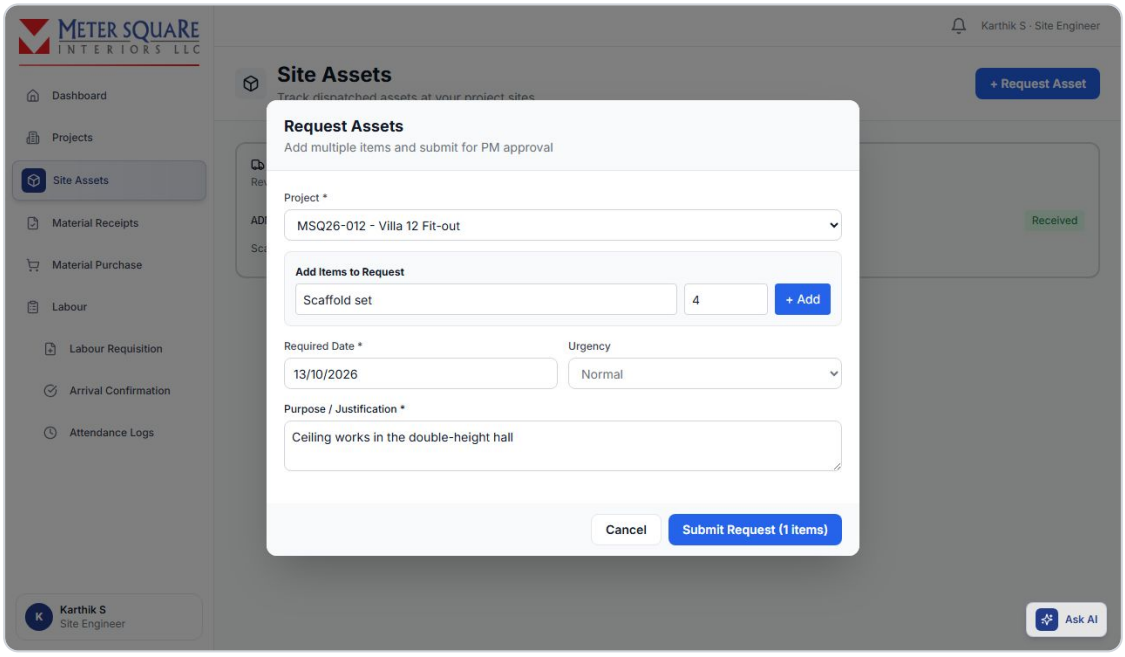

Request Assets


Status	Meaning
Draft	Not yet sent
Pending PM Approval	Waiting for your PM
PM Approved	Approved by your PM
PM Rejected	Rejected by your PM. Edit and resend.
Pending Store Approval	PM approved. Waiting for the Production Manager.
Store Rejected	Rejected by the store. Edit and resend.
Ready for Dispatch	Approved by the store
Dispatched	On its way, or a delivery note was created
Completed	You confirmed receipt
Cancelled	The request was cancelled

Rejected requests appear in **Rejected**. Click **Edit** and **Resend**.

How to receive assets

1. In **My Assets → Dispatched - Pending Your Receipt**, tick the items that arrived.
2. Click **Receive Selected**, or **Receive All**.
3. If you receive only part of a delivery, enter the reason (required).


You can also click **Confirm Receipt** on the requisition.

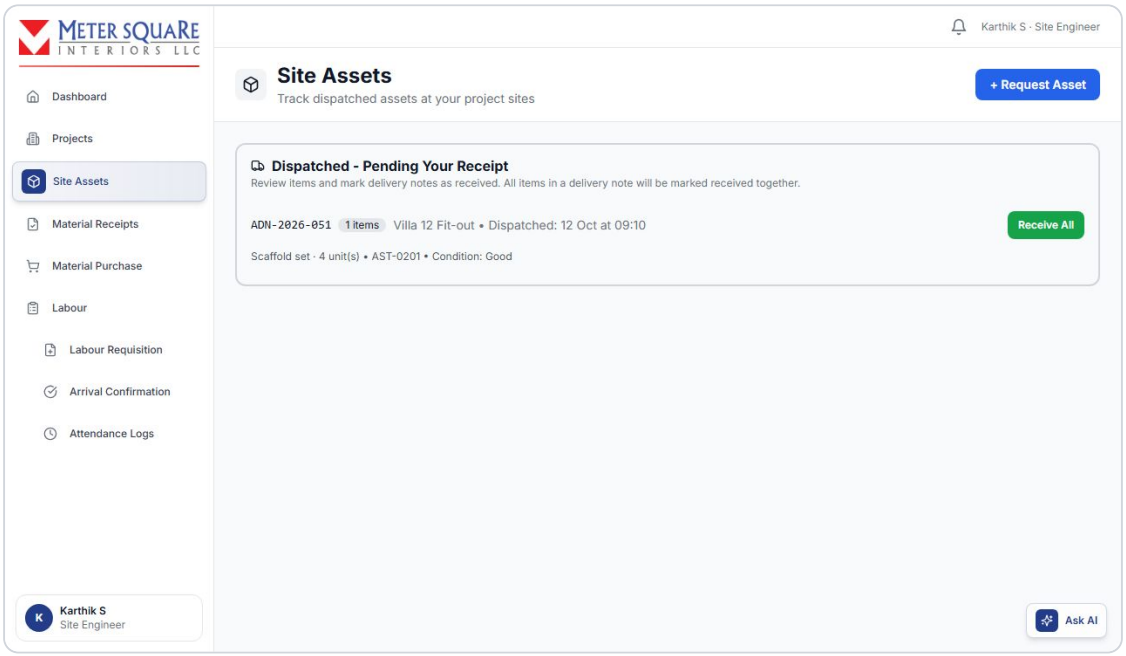

Site Assets: Dispatched - Pending Your Receipt

How to return assets

1. In **My Assets → Received at Your Sites**, tick the items and click **Return Selected**.
2. Split the quantity by condition: **Good**, **Fair**, **Poor** or **Damaged**. Fair, Poor and Damaged need a description.
3. Add a reason and click **Create Return Note**.
4. In **Returns**, click **Issue**, then **Dispatch**. Enter the driver name, vehicle number and driver contact (required), plus the transport fee, an optional file and notes.

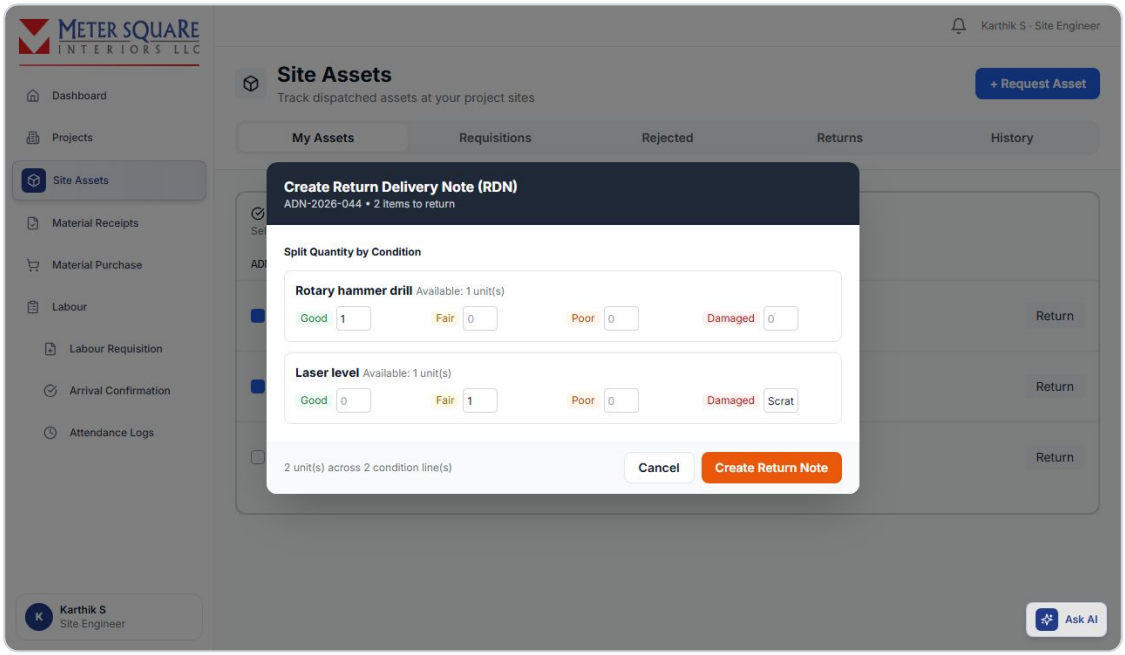


Create Return Delivery Note for assets, split by condition

The Production Manager receives and processes the return.

Labour

How to request labour

1. Open **Labour** → **Labour Requisition** and click **New Requisition**.
2. Select the **Project**. The site is filled in.
3. Enter the **Start Date**, **Start Time** and **End Time**. The end date is calculated; for a night shift it is the next day.
4. Under **Select Labour Requirements**, choose labour lines from your assigned BOQ items and enter the number of **Workers** for each.
5. Optional: choose **Preferred Workers**.
6. Click **Create Requisition(s)**.
7. On the requisition, click **Send to PM** and confirm.

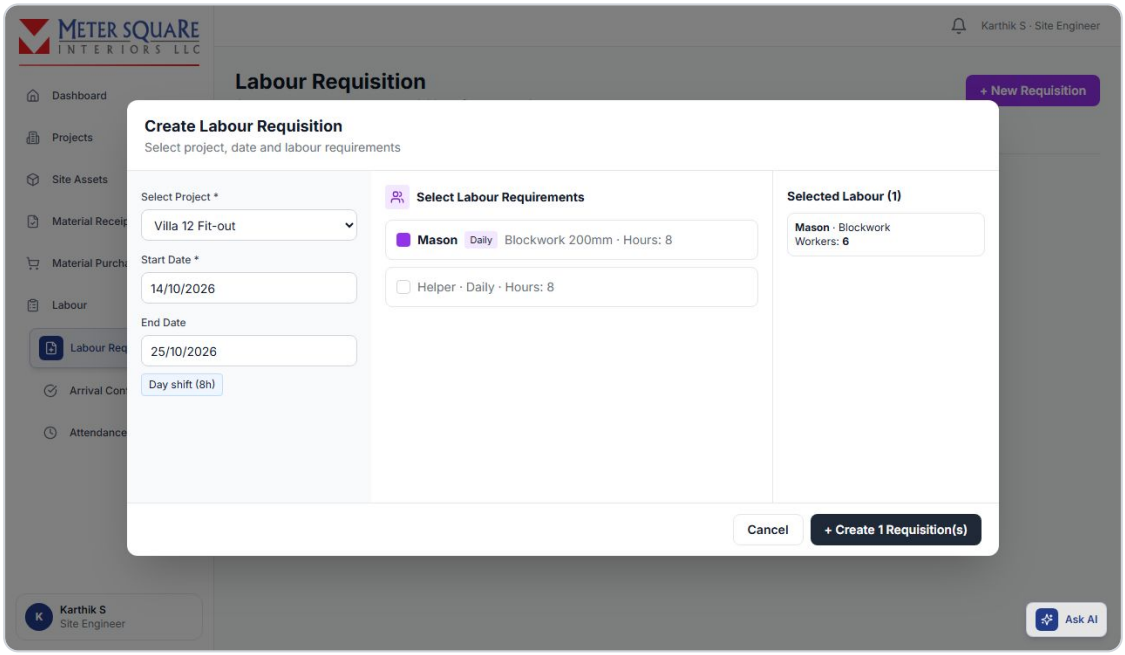

Create Labour Requisition

The tabs are **Pending**, **Approved**, **Rejected** and **Assigned**.


- Before sending, you can **Edit** or **Delete** a requisition.
- A rejected requisition can be edited and resent with **Resend to PM**.
- An approved, assigned requisition can be repeated for another day with **Reassign**: same workers, new date. The copy needs PM approval again.

After the PM approves, the Production Manager assigns workers. The workers receive WhatsApp messages with the details.

How to confirm worker arrival

1. Open **Labour** → **Arrival Confirmation** and select the project and date.
2. For each worker, click:
   - **Arrived**: from 30 minutes before shift start until shift end.
   - **No Show**: from 1 hour after shift start.
   - **Late Arrival**: for a worker marked No Show who arrives later.
3. At the end of the shift, click **Clock Out**. The worker moves to the attendance log.

Status badges: Awaiting, Working, Left and No Show. Use **Quick Select** to act on many workers at once (for example **Mark Arrived** for all pending workers).

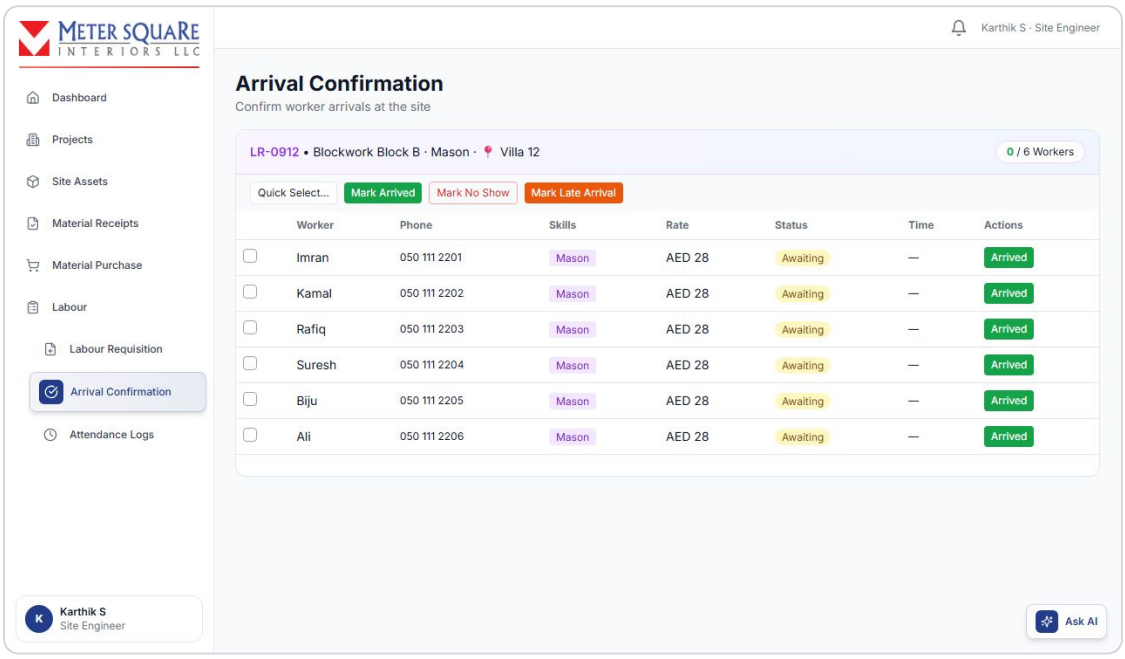


Arrival Confirmation

Attendance Logs

Open **Labour** → **Attendance Logs** and select the project and date.

- The summary shows Total Workers, Clocked In, Clocked Out and Total Time.
- You can also **Clock In** (choose the labour role, which links the hours to the right BOQ labour item) and **Clock Out** here.

Your Project Manager then locks the attendance for payroll.

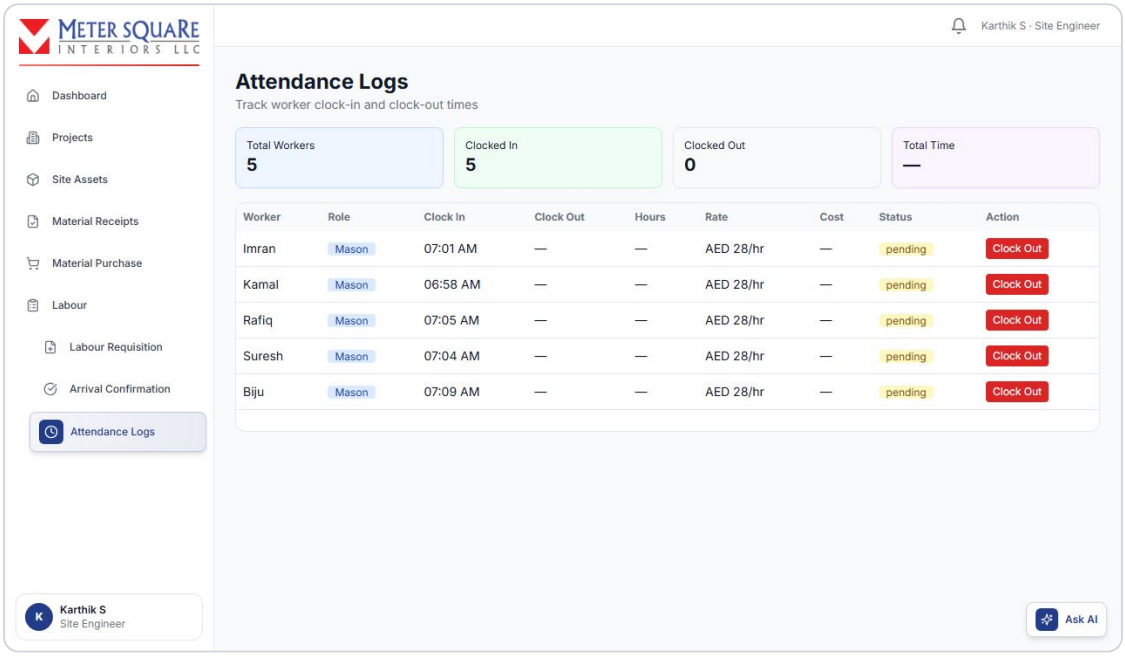

Attendance Logs

Procurement (Buyer)

Procurement buys the materials approved for projects:

- chooses vendors (the TD approves each vendor selection);
- sends the purchase order (LPO) to the vendor;
- completes the purchase so the vendor delivers to the M2 Store.

Procurement also manages vendors, browses store stock, transfers materials and handles vendor returns.

Procurement menu:

- **Dashboard**
- **Purchase Orders**
- **Vendors**
- **Store**: Store Items, Material Transfer, Raw Materials
- **Vendor Returns**: Rejected Deliveries, Return Requests

From request to site: the purchase flow


1 **Project Manager**	Approves the material request and assigns it to a buyer (via the Estimator if materials are new)
2 **Procurement**	Selects a vendor for each material, or gets the materials from the M2 Store
3 **Procurement**	Submits the vendor selection for TD approval
4 **Technical Director**	Approves the vendor (the LPO is generated)
5 **Procurement**	Sends the LPO to the vendor by Email and/or WhatsApp
6 **Procurement**	Clicks Complete & Send to Store
7 **Vendor**	Delivers to the M2 Store
8 **Production Manager**	Inspects, stocks in and dispatches to site
9 **Site Engineer**	Confirms delivery on site

All purchased materials go to the **M2 Store** first, where they are inspected. They are never delivered straight to site.

Buyer Dashboard

- **Top figures**: Completion Rate, Avg Processing (days), Total Completed Value.
- **Cards**:
  - Ongoing (pending purchase / store approved / vendor approved)
  - Pending Approval (store pending / vendor pending TD)
  - Completed (purchase orders / split POs)
  - Store Pipeline (pending vendor / at store)
  - Deliveries (in transit / delivered)
  - Vendors (approved / pending)

- **Attention Required**: shown only when there are more than 5 orders that need action, any rejected POs, or more than 3 pending deliveries.
- **Charts**: Purchase Order Pipeline, M2 Store Pipeline, Delivery Status, Purchase Activity.

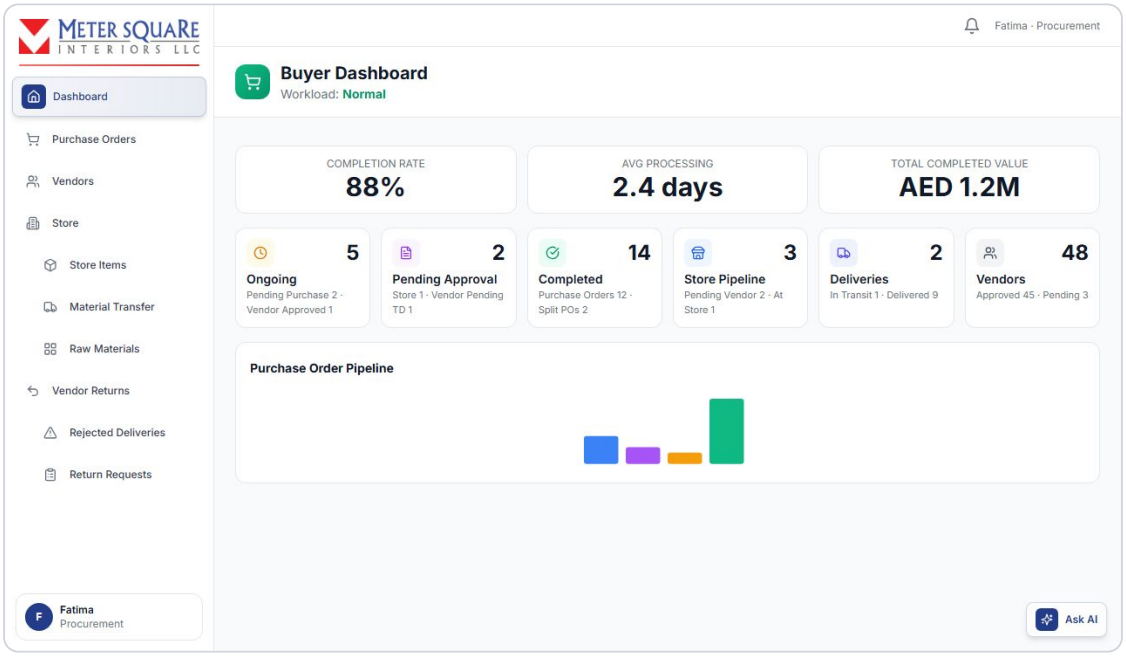

Buyer Dashboard

Purchase Orders

Open **Purchase Orders**. This is your main working page.

- Search by project, client, item or PO number.
- Switch between card and table view.
- A purchase is numbered **PO-**. When it is split across vendors, each vendor's part is numbered **PO-.1**, **.2** and so on.

Tabs

Tab	Sub-tab	What it shows
Ongoing	Pending Purchase	New purchases: choose a vendor or get from store
Ongoing	Store Approved	Store requests approved by the Production Manager
Ongoing	Vendor Approved	Vendor approved by the TD. Send the LPO and complete.

Tab	Sub-tab	What it shows
Pending Approval	Sent to Store	Waiting for the Production Manager to approve a store request
Pending Approval	Vendor Pending TD	Waiting for the TD to approve the vendor
Rejected		Rejected by the TD (purchase or vendor), or by the store
Completed		Completed purchases, including those sent to the M2 Store (**Routed to M2 Store**)

What to do at each stage

1. **New purchase (no vendor yet)**: **Select Vendor**, **Get from Store**, **Edit Prices** or **View Details**.
2. **Waiting for the TD**: the card shows "Vendor Selection Pending – Waiting for TD approval".
3. **Vendor approved**: send the LPO with **Email** and/or **WhatsApp**. Once either is sent, **Complete & Send to Store** appears. Click it.
4. **Rejected**:
   - **Select New Vendor** after the TD rejected the vendor.
   - **Select Vendor Instead** after the store rejected a store request.
   - **Resend** for a purchase the TD rejected.


How to select a vendor and send for TD approval

1. Click **Select Vendor**. The **Select Vendors for Materials** window lists each material with how many vendors offer it. The **AI-Powered Vendor Selection** banner at the top of the window is for information only.
2. Expand a material to compare vendors: their products, unit price and estimated total.
   - **Edit a vendor's price**: enter the new price, then click **This BOQ** to use it for this purchase only, or **All Future** to update the vendor's product price permanently.
   - **Compare with the BOQ estimate**: each price shows Over Budget, Under Budget or On Budget.
   - **Supplier notes**: add notes for the vendor (for example exact cut sizes) and click **Save**. Notes are highlighted in the LPO.

3. Choose a vendor for each material. To take a material from the M2 Store instead, click **Send to Store** on it.
4. Check the **Selection Summary**: totals by vendor, compared with the BOQ total.
5. Review the **LPO** (purchase order). Changes save automatically. You can edit:
   - Quotation Ref#, Subject, LPO Message;
   - VAT (on/off, percentage or amount);
   - Delivery Terms and Payment Terms;
   - whether to include the MD signature, company stamp and TD signature (uploaded by the Admin).
6. Submit:
   - **One vendor for everything**: click **Submit for TD Approval**, then **Confirm & Submit**.
   - **Several vendors**: click **Send This Vendor to TD** on each vendor group, check the LPO, and click **Confirm & Send to TD**. A separate PO (PO-x.1, PO-x.2…) is created for each vendor.

Once sent, you cannot add more materials to that vendor submission, so check carefully before sending.

A split PO card (PO-x.1) that has not been sent yet has its own **Send for TD Approval** button. Click it to send that vendor's PO. The card then shows **Sent to TD**.

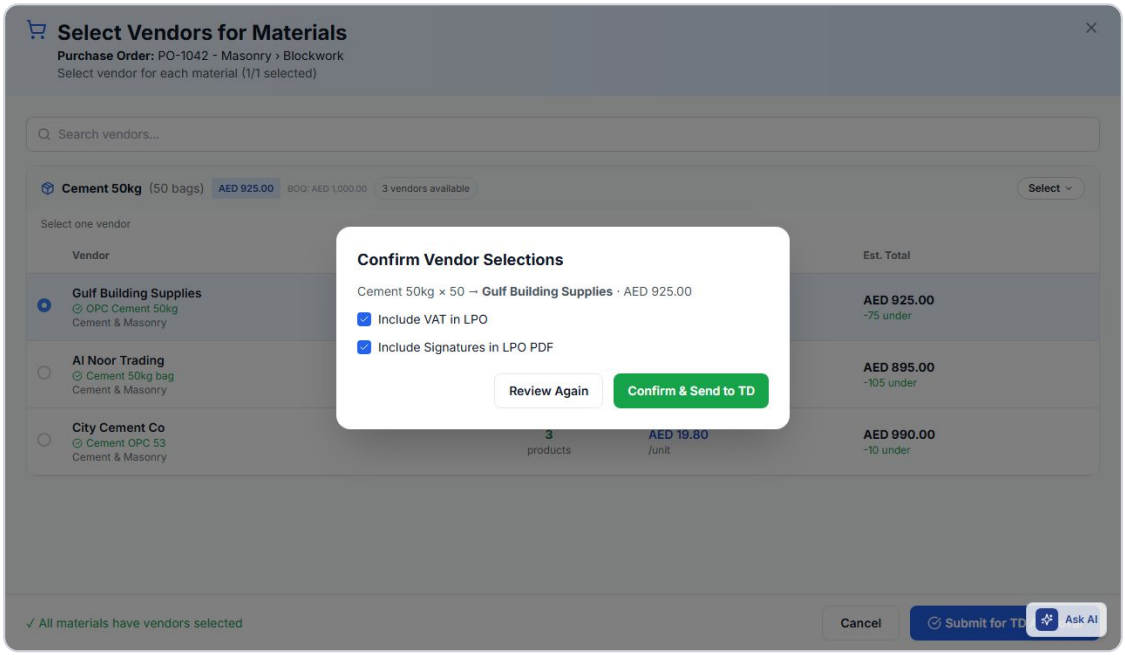

Select Vendors for Materials: confirming the selection


The TD is notified.

- **Approved**: the purchase moves to **Ongoing → Vendor Approved**.
- **Rejected**: it moves to **Rejected**. Choose a new vendor.

How to get materials from the M2 Store

If the store already has the materials, you can take them from stock instead of buying.

1. Click **Get from Store**. The window checks stock and shows:
   - **Available**: tick these (they are pre-selected).
   - **Already Sent to Store**.
   - **Not Available**: these must be bought from a vendor.
2. Click **Request Selected**. A store request is created.

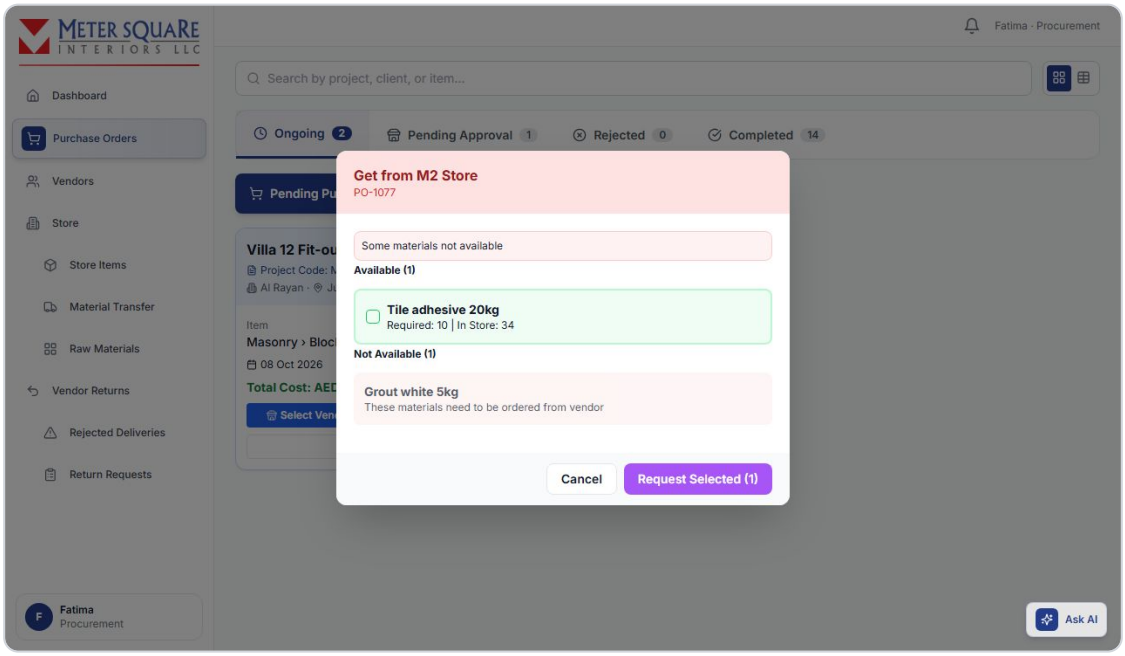

Get from M2 Store

The Production Manager is notified and approves or rejects the request.

- **Approved**: you are notified ("Material Request Approved"). The purchase completes automatically and moves to **Completed**. You do not need to do anything.
- **Rejected**: you are notified with the reason ("Store Material Request Rejected"). The notification links to the **Rejected** tab. Click **Select Vendor Instead**.

Any remaining materials can still be bought from a vendor. The purchase completes when all its materials are covered.

How to edit negotiated prices

Click **Edit Prices** on a new purchase. Change the unit price per material and click **Save Changes**. The negotiated prices are used for vendor selection and in the LPO. The window shows the original total, the negotiated total and the difference.

How to send the LPO to the vendor

You can send the LPO only after the TD approves the vendor.

By email

1. Click **Email**.
2. Confirm the vendor's email address. You can enter several, separated by commas.
3. Add **CC Recipients** if needed. The Admin's default CC addresses are included; untick any you do not want.
4. Optional: add attachments.
5. The **LPO PDF** is attached automatically. Click **Preview** to check it. It cannot be edited after TD approval, so make LPO changes during vendor selection.
6. Click **Preview Email**, adjust the greeting, message, instructions and delivery requirements, then click **Send Email**.

By WhatsApp

1. Click **WhatsApp**. It shows **No Phone** if the vendor has no phone number saved.
2. Check the preview and the LPO PDF.
3. Click **Send WhatsApp**.

What the card shows after sending

Purchase	After Email	After WhatsApp only
Single vendor	**Sent to Vendor**	The **Email** button stays. The WhatsApp button shows **Sent**.


Purchase	After Email	After WhatsApp only
Split PO (PO-x.1)	**Sent to Vendor**. Both buttons are hidden.	**Sent to Vendor**. Both buttons are hidden.

Complete & Send to Store appears as soon as either one is sent.

How to complete a purchase

After sending the LPO, click **Complete & Send to Store**.

- **For a split PO** (PO-x.1): first choose the **Site Engineer / Recipient** who will receive the materials on site.
- The purchase becomes **Routed to M2 Store** and moves to **Completed**.
- A material request is created for the M2 Store automatically, one per purchase.
- The Production Manager is told a vendor delivery is coming, and the requester is told the purchase was routed to the store.

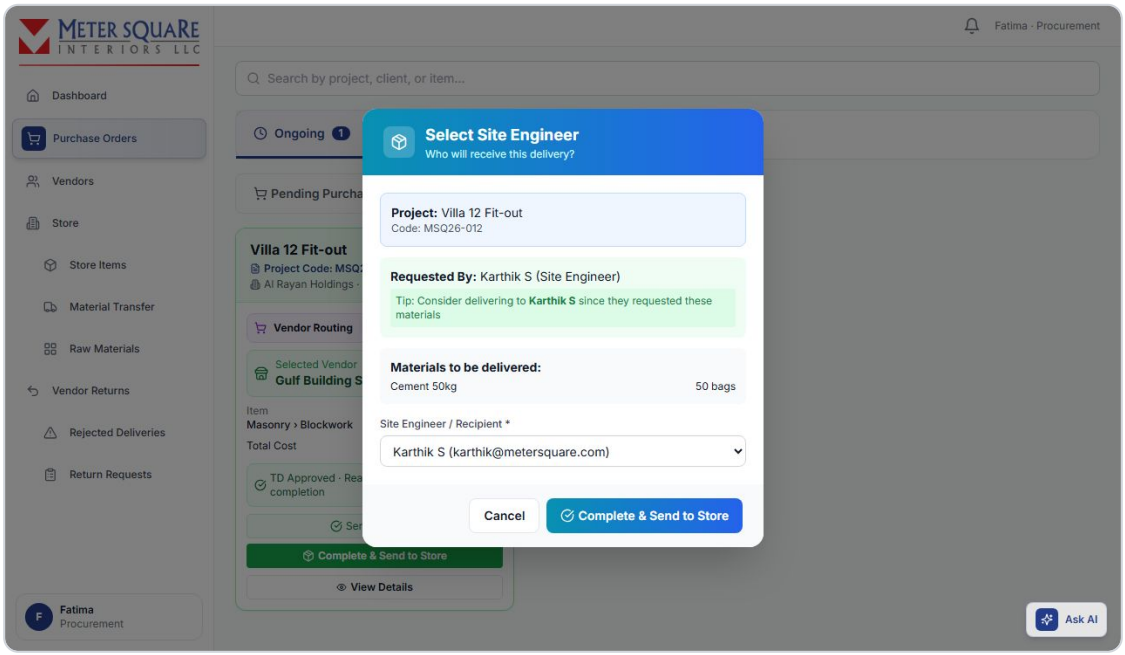

Choosing the receiving Site Engineer before Complete & Send to Store

Next, the vendor delivers to the M2 Store.

1. The Production Manager inspects the delivery. You are notified if it was **fully approved**, **partially approved** or **fully rejected**.

2. The Production Manager stocks it in and creates a Delivery Note to site. When the Delivery Note is issued, you get a "Materials Being Prepared" notification.
3. The Production Manager dispatches it. You are notified when it is dispatched and when the Site Engineer confirms delivery.


A purchase split across several vendors is complete when all its vendor POs are complete.

Vendor Returns

When the Production Manager rejects delivered materials at inspection, you arrange the return.

How to create a return request

1. Open **Vendor Returns** → **Rejected Deliveries**. Search by CR ID or vendor.
2. Click **Create Return Request** on the delivery. Review the rejected materials (quantity, price, reason) and the inspection evidence.
3. Choose the **Resolution Type**:
   - **Refund**: the vendor refunds or issues a credit note.
   - **Replacement**: the vendor replaces the material.
   - **New Vendor**: buy from another vendor. Select it.
4. Optional: set an **SLA Deadline**, **SLA Notes** and **Notes**.
5. Click **Create Return Request**.

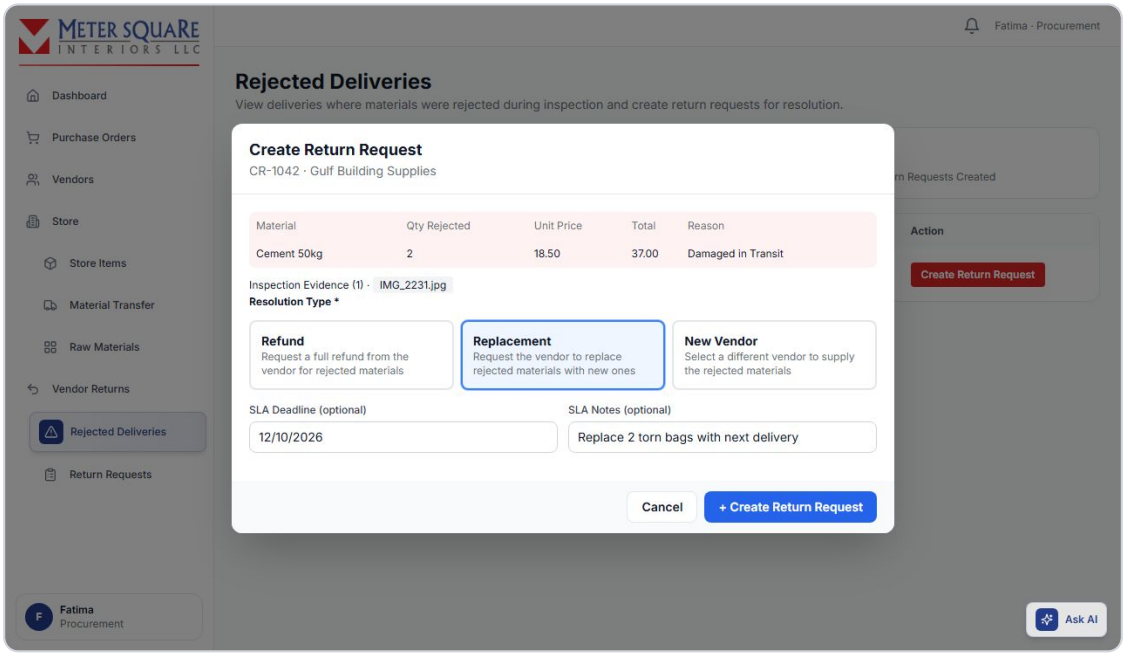


Create Return Request from Rejected Deliveries

The return request (VRR) goes to the TD for approval.

How to follow a return request

Open **Vendor Returns** → **Return Requests**. Filter by All, Pending Approval, TD Approved, In Progress, Completed or Rejected. Expand a request to act on it:

- **Edit & Resubmit**: when the TD rejected it. The rejection reason is shown.
- **Initiate Return to Vendor**: after TD approval, for a refund or replacement.
- **Confirm Refund Received**: enter the **Credit Note Number** and **Credit Note Amount (AED)** and upload proof. The request is completed.
- **Confirm Replacement at Store**: enter an optional vendor reference and proof. The Production Manager inspects the replacement, and the request completes when they approve it.
- **Select New Vendor**: for a new-vendor resolution. The TD approves the new vendor, then click **Generate LPO for New Vendor**. The new purchase appears in Purchase Orders.
- **View Full Timeline**: see the inspection history.

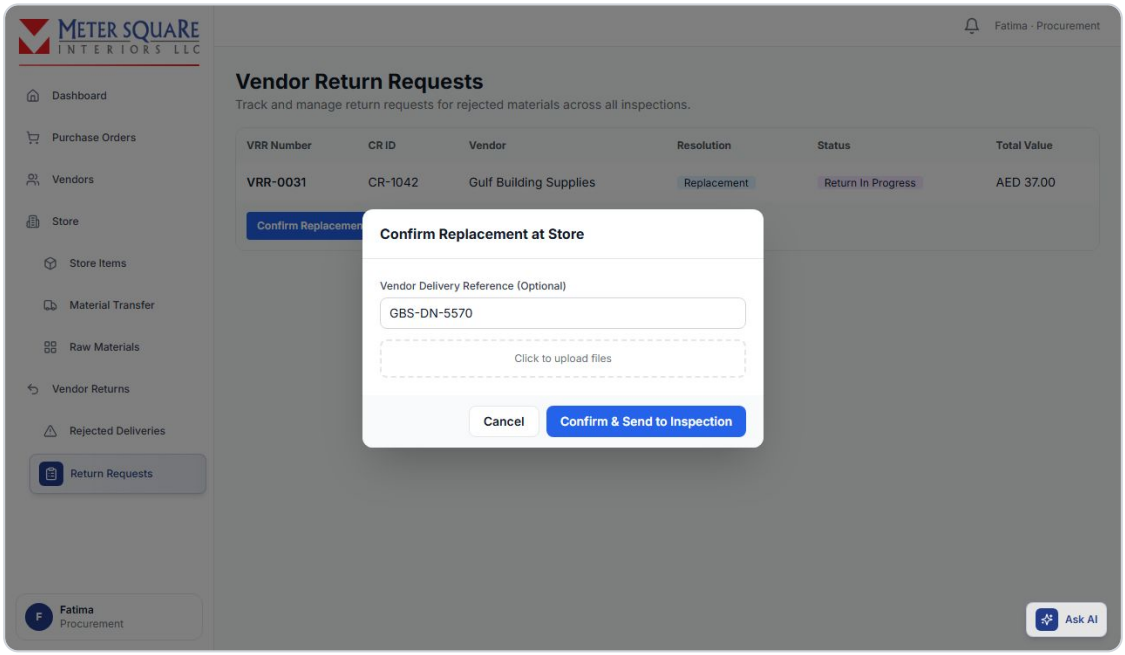

Confirm Replacement at Store

Return statuses

Status	Meaning
Pending TD Approval	Waiting for the TD
TD Approved / TD Rejected	TD decision
Return In Progress / Return Initiated	Material being returned to the vendor
Refund Confirmed	Refund or credit note received
Awaiting PM Inspection	Replacement delivered, waiting for inspection
Replacement Ordered	Replacement requested
Vendor Pending TD Approval	New vendor waiting for TD approval
New Vendor Selected / New Vendor Approved	New vendor chosen or approved
Completed / Closed	Finished

Vendors

Open **Vendors** (Vendor Management). Search vendors and filter by category and status (Active or Inactive).

How to add a vendor


1. Click **Add Vendor**.

2. Enter:
    - **Company Name** and **Email** (required);
    - Category (or **+ Add New Category**) and Status (**Active** or **Inactive**);
    - Contact Person, Country, Phone and the tax number (TRN or GST, depending on the country);
    - optionally the address.
3. Click **Add Vendor**.

Only **Active** vendors are offered when selecting vendors. Use **Edit** to update a vendor and **Delete** to remove one.

How to add a vendor's products

1. Click **View** on the vendor.
2. Under **Products & Services**, click **Add Product**.
3. Enter the **Product/Service Name**, Category, Description, Unit and **Unit Price (AED)**.
4. Click **Add Product**.

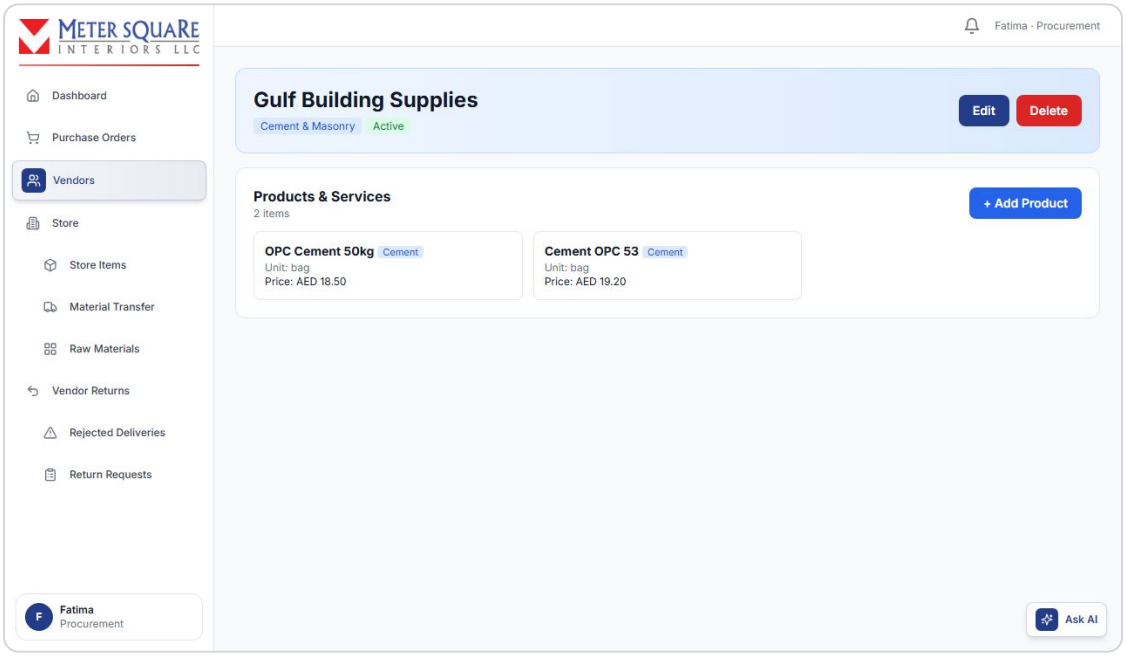

A vendor's Products & Services

Vendor product prices are used to compare vendors when you select one.

Store


Store Items

Open **Store → Store Items** to browse M2 Store stock: material, description, category, unit price, unit, available stock and status. This page is read-only.

Material Transfer

Use this to transfer materials yourself, either to a site or to the M2 Store.

1. Open **Store → Material Transfer → Create Transfer**.
2. Choose the **Transfer Destination**:
   - **Construction Site (Direct)**: also select the **Site Engineer** and **Project**.
   - **M2 Store (Warehouse)**.
3. Click **Add Material** for each material (name, quantity, unit).
4. Enter the **Transfer Date**, vehicle, driver, driver contact, transfer fee and notes.
5. Click **Create Delivery Note**. It is created as a draft.
6. In **Transfer History**, click **Dispatch**, then **Dispatch Now**. The delivery is **In Transit**. A PDF is available.

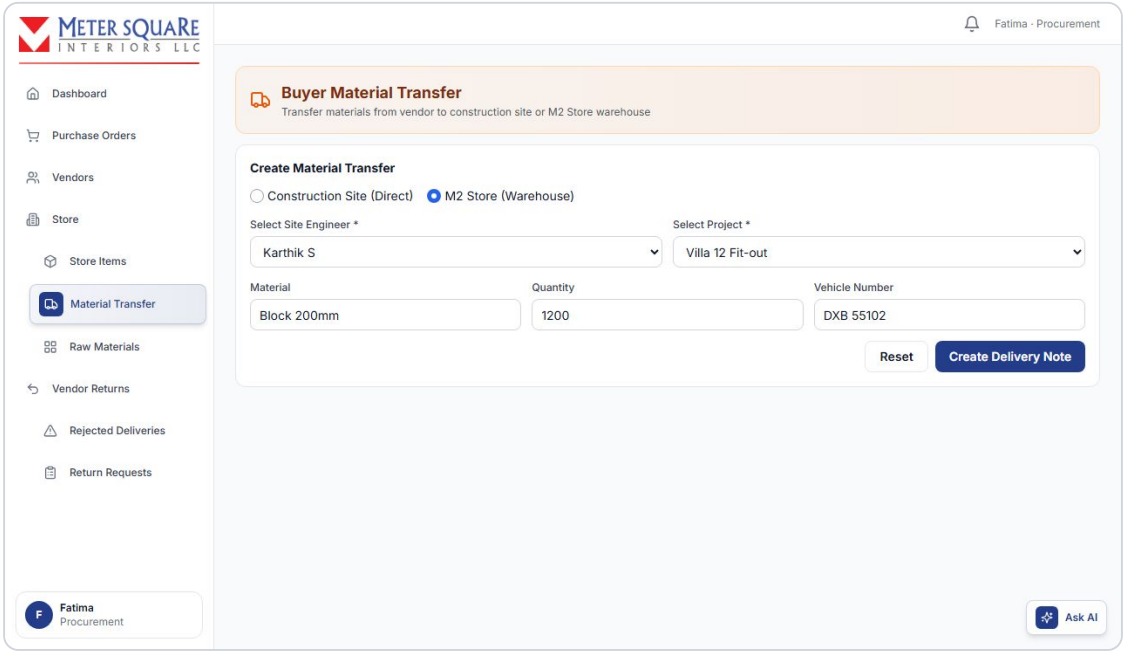


Buyer Material Transfer

Transfers to the M2 Store are received by the Production Manager under **Stock In → Buyer Transfers**.

Raw Materials

Open **Store** → **Raw Materials** to manage the raw materials catalog used in BOQs.

- **Materials** tab: click **Add Material** and enter the name, description, brand, size, specification, unit, **Unit Price (AED)** and category.
- **Items & Sub-Items** tab: link materials to items with **Link Material**.

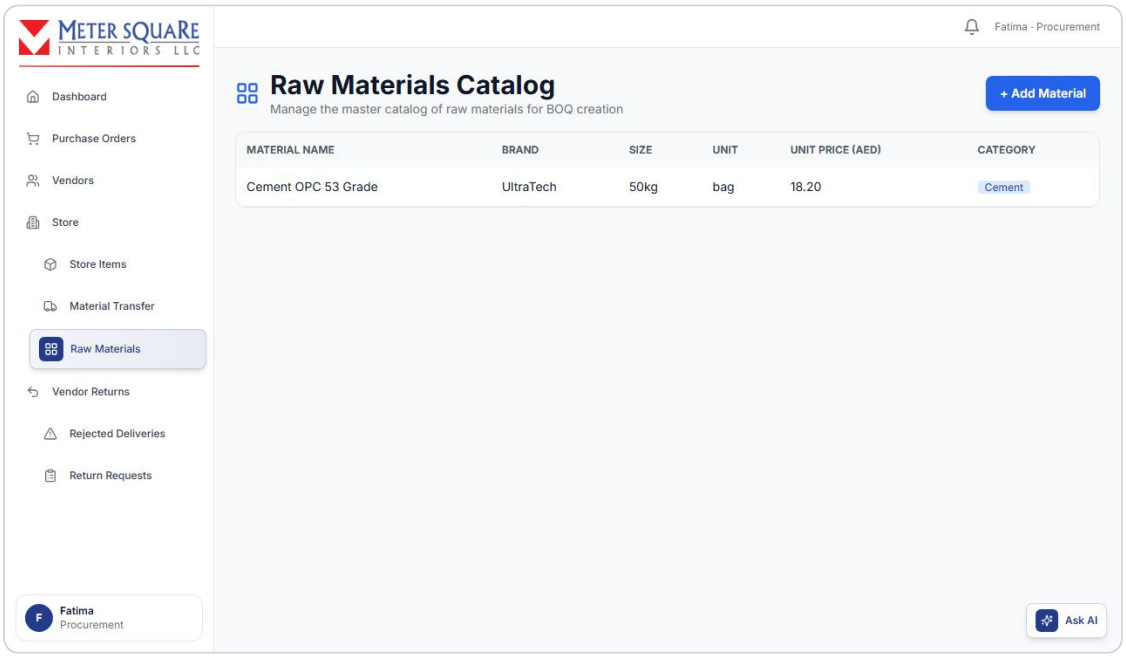

Raw Materials Catalog

Production Manager (M2 Store)

The Production Manager runs the **M2 Store** warehouse. All purchased materials pass through the store for inspection before going to site. The Production Manager also manages returnable assets (tools and equipment) and the labour registry.

Production Manager menu:

- **Dashboard**
- **Inventory Management**: Materials Catalog, Stock In, Stock Out, Receive Returns, Repair, Disposal
- **Returnable Assets**: Asset Catalog, Stock In, Stock Out, Process Returns, Repair, Disposal
- **Labour**: Labour Registry, Assign Workers

Material flow through the M2 Store


1 **Procurement**	Completes a purchase. The request is routed to the M2 Store
2 **Vendor**	Delivers the materials to the M2 Store
3 **Production Manager**	Inspects the delivery (Stock In, Vendor Deliveries)
4 **Production Manager**	Records Stock In for the accepted materials. This approves the material request
5 **Production Manager**	Creates a Delivery Note for the site
6 **Production Manager**	Issues and dispatches the Delivery Note to site
7 **Site Engineer**	Confirms receipt on site (Delivered)
8 **Site Engineer**	Sends unused material back with a Return Delivery Note
9 **Production Manager**	Receives the return: Good to stock, Damaged to repair, or Disposal

Production Dashboard

The **Production Dashboard** shows the store at a glance.

- **Cards**: Total Materials, Inventory Value, Stock Alerts, Pending Actions, Delivery Notes (in transit), Material Requests (pending), Incoming Returns, Stock Movement (30 days).
- **Panels**:
  - Stock Health: healthy, low, critical, out of stock, and the backup stock value.
  - Delivery Notes by status.
  - Material Requests by status.
  - Top Categories.
  - Returns & Disposal.
  - Today's Activity.

- Recent Delivery Notes and Recent Activity.

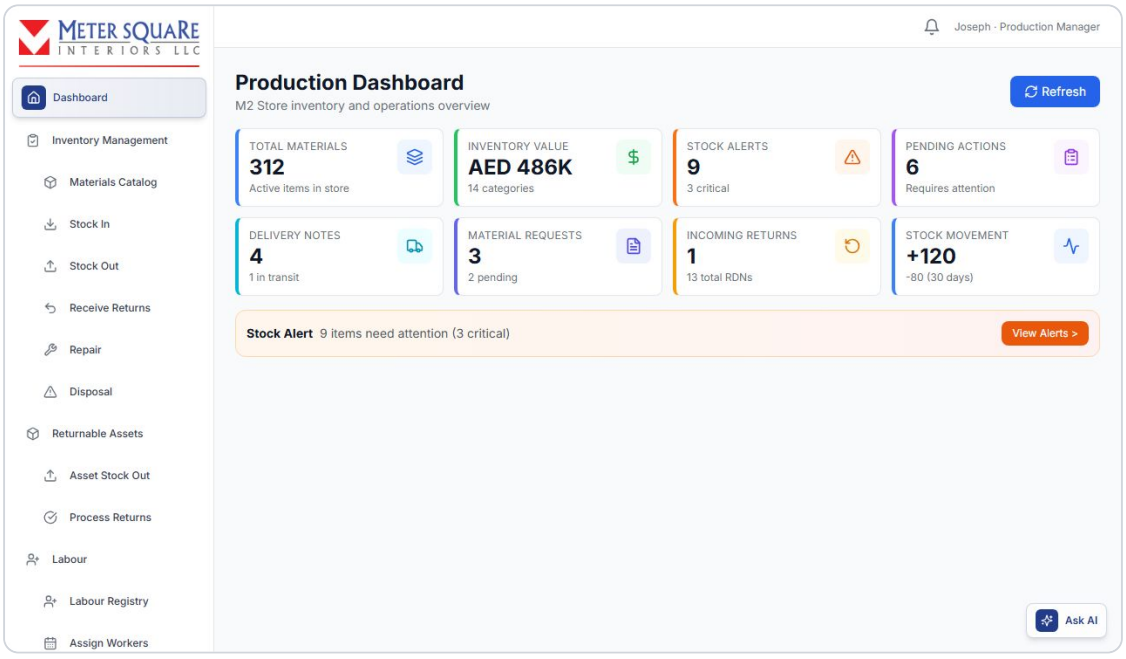

Production Dashboard

What the stock colours mean

- **Out of stock**: the stock is 0.
- **Critical**: well below the minimum stock level.
- **Low**: at or below the minimum stock level.
- **Healthy**: above the minimum.

Main stock and backup stock

Each material has two stock figures:


- **Current stock (main stock)**: usable stock.
  - Goes **up** with Stock In, buyer transfers received, good returns and repaired items.
  - Goes **down** when a material request is approved, and with TD-approved disposals.
- **Backup stock**: damaged or partly usable stock.
  - Goes **up** when returned items are sent for repair, or when the TD rejects a disposal.
  - Goes **down** when an item is marked repaired, which moves it to main stock.

The Materials Catalog shows backup stock as a blue **+N backup** badge.

Materials Catalog

Open **Inventory Management → Materials Catalog**.

- Search by name, code or brand, and filter by category.
- **Columns**: Code, Name (and brand), Category, Availability, Current Stock (with **Min** underneath), Unit Price.
- Current stock is red at 0, orange at or below the minimum, and green otherwise.
- New materials are added automatically when you record a Stock In. There is no separate "add" button here.

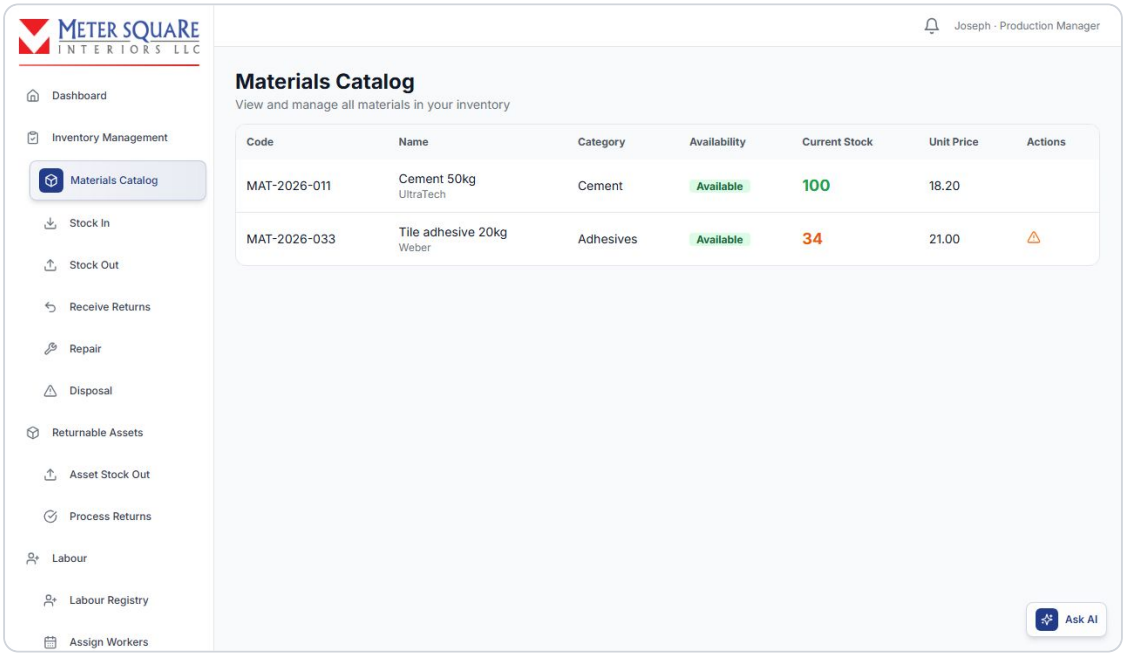

Materials Catalog

How to request disposal of a damaged or wasted material

1. Click the orange warning icon on the material's row. It is shown only when stock is above 0.
2. Enter the **Quantity to Dispose**. The estimated value is calculated.
3. Choose a **Reason for Disposal**: Damaged/Defective, Expired, Wasted, Obsolete, Lost/Missing or Other.
4. Add **Additional Notes**.
5. Click **Submit for TD Approval**.

Stock does not change until the Technical Director approves. On approval, current stock is reduced.

Stock In (receiving into the store)


Open **Inventory Management** → **Stock In**. The page lists purchases received, grouped by material. Expand a material to see each receipt: date, quantity, price, reference, delivery note, driver, vehicle and transport fee.

There are three header buttons:

- **Buyer Transfers**
- **Vendor Deliveries** (the red badge shows how many deliveries are waiting for inspection)
- **Record Stock In**

How to inspect a vendor delivery

1. Click **Vendor Deliveries**. The **Inspection Centre** opens.
2. In **Pending Inspections**, click **Inspect** on the delivery. A replacement delivery from a vendor return carries a **Replacement** badge.
3. For each material, enter the **Accepted** quantity. The rejected quantity is calculated. Use **Accept All** or **Reject All** as shortcuts.
4. For anything rejected, choose a **Rejection Reason**: Quality Defect, Wrong Specification, Quantity Shortage, Damaged in Transit, Expired / Outdated or Other. Notes are optional.
5. Fill in **Transport Details**: Driver Name, Vehicle Number, Reference / PO Number.
6. Add **Overall Inspection Notes**.
7. Upload **Inspection Evidence**. This is required if anything is rejected. You can upload images (up to 2 MB), PDF (up to 10 MB) or video (up to 50 MB).
8. Click **Submit Inspection**.

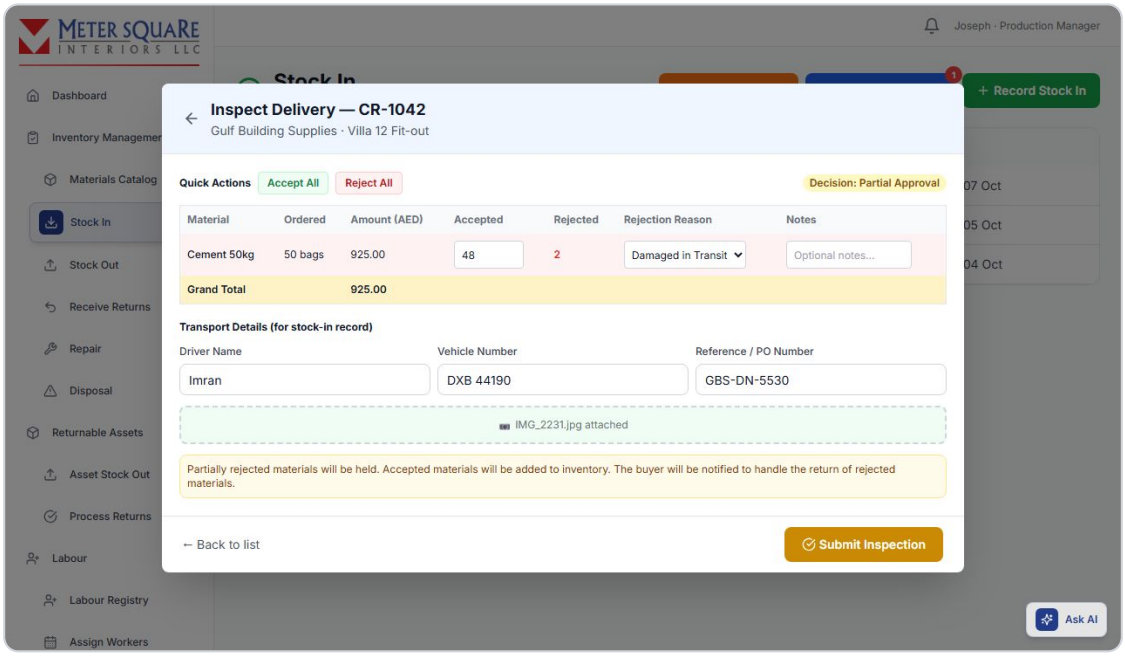

Inspect Delivery

What happens next:

- **Everything accepted**: the Record Stock In form opens pre-filled. You can stock in now, or later from the **Awaiting Stock In** tab.
- **Partly accepted**: the Record Stock In form opens pre-filled with the accepted materials. The buyer is notified about the rejected items. Rejected quantities are listed under **Held Materials**.
- **Everything rejected**: nothing enters stock and the buyer is notified to handle the return.

Submitting an inspection does **not** add stock. Stock is added when you complete **Record Stock In**. Completing the Stock In from an inspection also approves the material request for that delivery.

Other Inspection Centre tabs:

- **Awaiting Stock In**: inspected deliveries not yet stocked in. Click **Stock In** to finish one.
- **Inspection History**: filter by Fully Approved, Partially Approved or Fully Rejected.
- **Held Materials**: rejected quantities kept at the store until the buyer arranges the return, with refund or credit-note details.


How to record Stock In

1. Click **Record Stock In**, or **Stock In** on an inspected delivery.

2. Select the **Project** and the **Material**. If the material is not in the catalog, choose **+ Create New Material**.
3. Enter **Quantity Received** and **Actual Purchase Price (AED)**. The total is calculated.
4. Optional: enter the **Reference Number (PO/Invoice)** and **Notes**.
5. Enter transport details: **Driver Name**, **Vehicle Number** and the transport fee (default 1.00 AED per unit).
    - Use **Recent Deliveries** or **Last Delivery** to reuse details from the same truck.
    - Materials from the same delivery share one batch reference. Only the first material should carry the transport fee.
6. Upload the **Delivery Note from Vendor** (PDF, JPG, PNG, DOC or DOCX, up to 10 MB).
7. Click **Confirm Stock In**, then **Confirm**.

Current stock increases by the quantity. For an inspected delivery with several materials, the form lists them all; click **Confirm Stock In (N materials)** and then **Confirm All**.

If an accepted material is not in the catalog, it is listed under **Not in Inventory Catalog**. Click **Add Material** on it to add it to the catalog and include it in the Stock In.

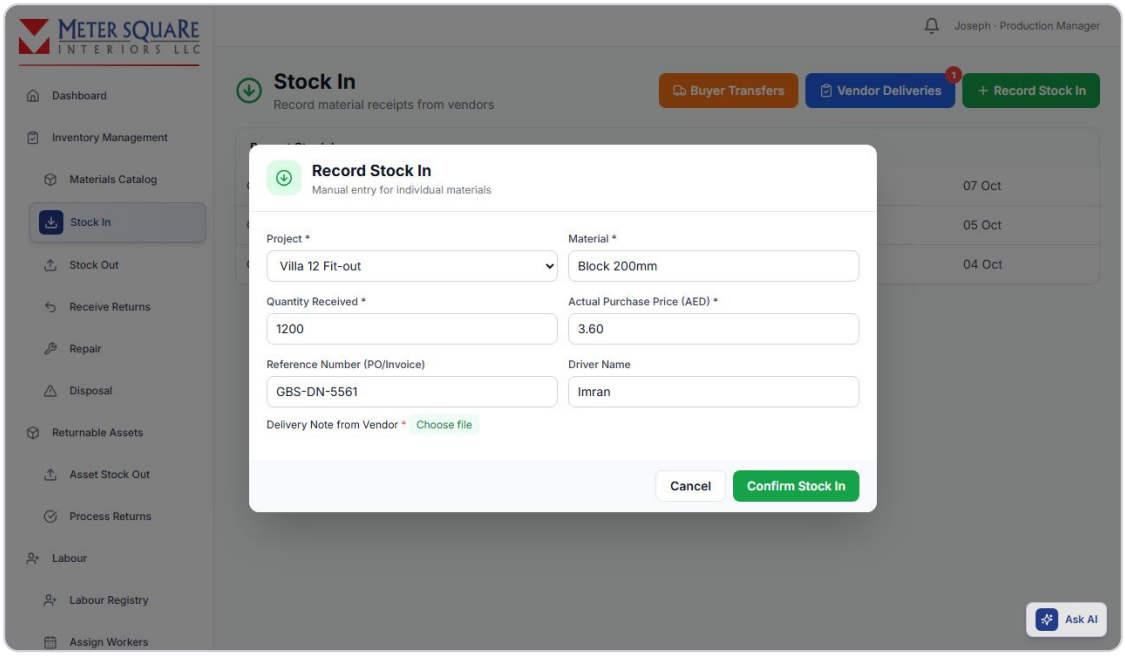

Record Stock In

How to add a new material

When **+ Create New Material** opens:

1. Enter **Material Name** and **Unit**. If you type a unit that does not exist, it is created.
2. Optional: **Brand**, **Size**, **Category**, **Min Stock Level** and **Description**.
3. Click **Create Material**.

The material starts with 0 stock. Its price is set on the first Stock In.

How to receive a buyer transfer

Buyers can send materials to the M2 Store directly.

1. Click **Buyer Transfers**.
2. In the **Pending** tab, check the transfer and click **Receive**.

The materials are added to inventory. The **History** tab keeps received transfers, each with a PDF.

Stock Out (material requests and delivery notes)

Open **Inventory Management → Stock Out**. Tabs: **Pending**, **Approved**, **Draft DN**, **Issued DN**, **Completed**, **Rejected**, **Delivered DN**.

Material requests (IMR)

A material request is created automatically when **Procurement** completes a purchase that goes through the store, or routes a request to the store. One request covers all materials of a purchase.

The table shows Request #, Project, Requester, Material, Qty, Stock / Destination, Status, Date and Actions. A **Vendor Delivery** badge marks materials coming from a vendor, with the destination site shown.

How to approve or reject a material request

1. In **Pending**, check the stock shown for the materials.
2. Click **Approve**. The button is disabled when stock is not enough.
3. Or click **Reject** and enter a **Rejection Reason**.

What happens:

- **Approve**: the stock is deducted from current stock and the request moves to **Approved**. The buyer is notified.
- **Reject**: the buyer is notified with the reason.

Requests from a vendor delivery

A request marked **Vendor Delivery** is approved through inspection, not from Stock Out:

1. Open **Stock In** → **Vendor Deliveries**.
2. Click **Inspect** on the delivery and submit the inspection.
3. Complete **Stock In** from the inspection. This approves the request, and it moves to **Approved**.

On Stock Out, a vendor delivery row shows **Confirm Receipt** instead of **Approve**. **Confirm Receipt** approves the request straight away without an inspection record, so use **Inspect** first when the delivery needs checking.

How to create a Delivery Note (DN) to site


1. In **Approved**, click **Create DN** on the request. If the stock is not enough, the row shows **Awaiting Stock** instead.
2. Check the project and **Attention To (Site Engineer)**. This is pre-selected from the buyer's chosen recipient or the project's Site Engineer.
3. Enter:
    - **Delivery Date** (default today)
    - **Requested By** (pre-filled)
    - the transport fee (default 1.00 AED per unit, must be above 0)
    - **Driver Name** (letters only), **Vehicle Number** and **Driver Contact**
4. Check the items and add **Notes**.
5. Click **Create Delivery Note**.

The DN is created as **Draft** and appears in **Draft DN**. It is numbered MDN--.

How to issue and dispatch a Delivery Note

1. In **Draft DN**, click **Issue** and confirm. The DN becomes **Issued** and the buyer is notified that materials are being prepared. You can **Cancel** a DN only while it is a draft.

2. In **Issued DN**, click **Dispatch** and confirm. The DN becomes **In Transit**. The project's Site Engineers and the buyer are notified with the materials, vehicle and driver.
3. The Site Engineer confirms receipt on site. The DN becomes **Delivered** (or **Partial** if less arrived) and the request becomes **Fulfilled**. The buyer and the Production Managers are notified.

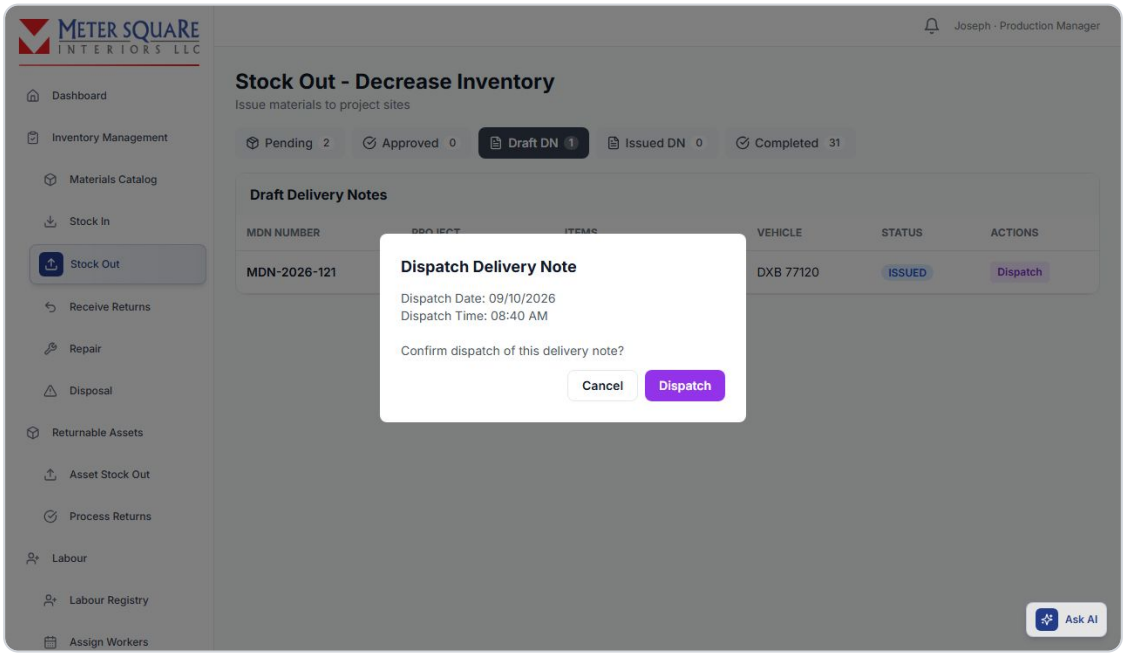

Dispatch Delivery Note

Every DN can be downloaded as a PDF or printed.

Material request statuses

Status	Meaning
Pending	Waiting for your approval, or waiting for the vendor delivery to arrive and be inspected
Inspected, awaiting Stock In	The vendor delivery was inspected (fully or partly accepted) but not yet stocked in. It is not listed on Stock Out. Finish it from **Stock In → Vendor Deliveries → Awaiting Stock In**.
Approved	Approved and stock deducted. Ready for a Delivery Note.
DN Pending	Added to a draft Delivery Note
Dispatched	The Delivery Note was issued or dispatched
Fulfilled	The Site Engineer confirmed delivery

Status	Meaning
Rejected	Rejected by you (the buyer is told why), or the vendor delivery was fully rejected at inspection

Delivery Note statuses

Status	Meaning
Draft	Created. Can be issued or cancelled.
Issued	Being prepared. Requests show Dispatched.
In Transit	On the way to site
Delivered	Site confirmed receipt of everything
Partial	Site received less than was sent
Cancelled	Cancelled while still a draft

Receive Returns (material returns from site)


Site Engineers return unused or damaged material with a **Return Delivery Note (RDN)**, numbered RDN--. Open **Inventory Management → Receive Returns**.

- **In Transit**: returns on the way, or received but not fully processed.
- **Received**: fully processed returns.

How to receive and process a return

1. When the RDN is **In Transit**, click **Confirm Receipt**. Later, use **Process Items** for anything left unprocessed.
2. Each item shows its condition from site (**Good**, **Damaged** or **Defective**) and the return reason. Choose the action:
   - **Good → Add to Stock**: added to current stock.
   - **Damaged/Defective → Send for Repair**: added to backup stock and listed under **Repair**.
   - **Damaged/Defective → Mark for Disposal**: sent to the TD for approval. A note explaining why is required.
3. Optional: add **General Acceptance Notes**.

4. Click **Process** on each item, or **Confirm & Process All**.

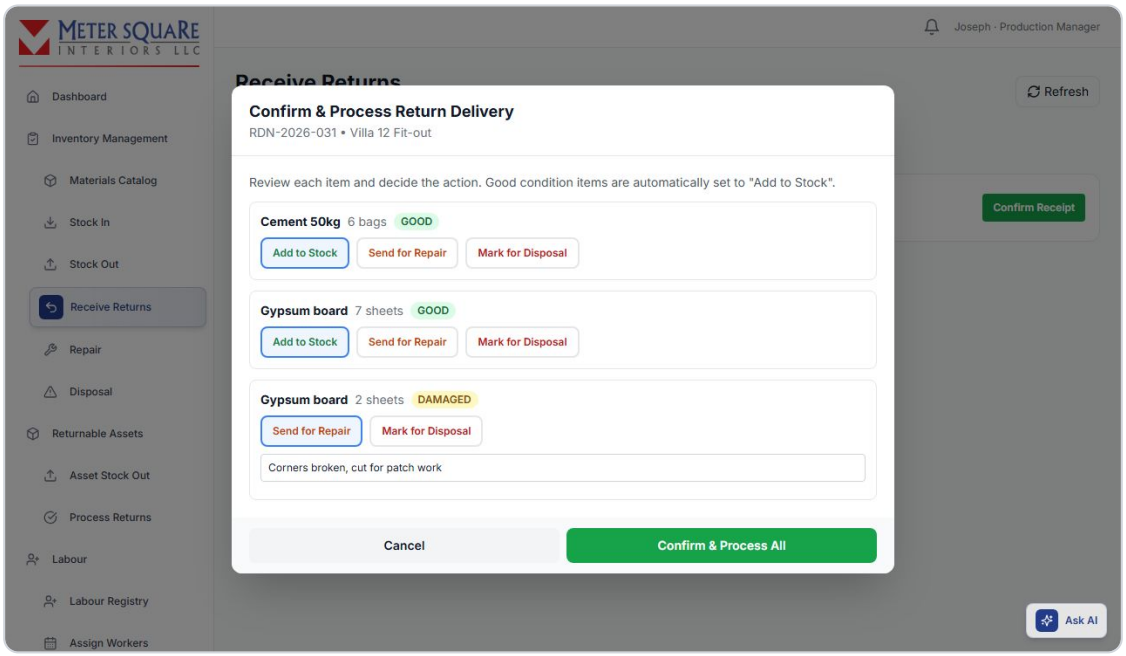


Confirm & Process Return Delivery

When every item is processed, the return is complete.

Repair (materials)

Open **Inventory Management** → **Repair**. The tabs are **Pending Repair** and **Completed**. Click **View** on an item.

- **Mark as Repaired** → **Add to Stock**: then **Confirm Repair**. The quantity moves from backup stock to main stock.
- **Cannot Repair - Request Disposal**: optionally add a **Reason for disposal (optional)**, then click **Request Disposal**. The request goes to the TD.

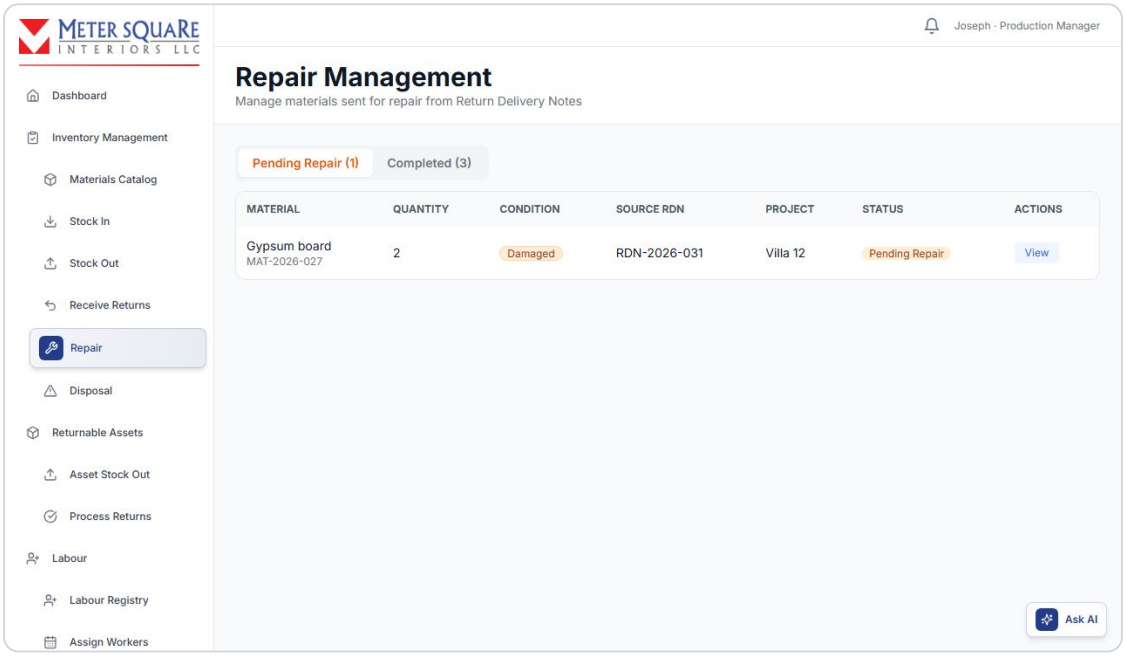

Repair Management

Disposal (materials)

Open **Inventory Management** → **Disposal** to follow disposal requests. This page is for viewing only.

- **Pending TD Approval**: waiting for the Technical Director.
- **TD Approved - Ready for Disposal**: approved. Dispose of the material physically.

The TD reviews each request:

- **Approve Disposal**: stock is reduced.
- **Reject & Add to Backup**: the TD must add review notes. The full quantity goes to backup stock, and the request shows **Backup Added**.

Returnable Assets

Returnable assets are tools and equipment that go to site and come back.

Asset Catalog

Open **Returnable Assets** → **Asset Catalog**. Each asset type shows its code, tracking type, and Available, Dispatched and Total quantities.

- **Quantity based** tracking counts the total number.

- **Individual** tracking records each item by serial number.

To dispose of an asset:

1. Click **Dispose**.
2. Enter the **Quantity to Dispose**.
3. Choose a reason: Damaged Beyond Repair, Obsolete / Outdated, End of Life, Lost / Missing, Safety Hazard or Other.
4. Add notes and click **Submit Request**.

The quantity is taken out of available stock straight away, and the request goes to the TD for approval.

How to add assets (Asset Stock In)

1. Open **Returnable Assets** → **Stock In** and click **Add Stock**.
2. Choose or type the **Asset Category**, and enter the **Quantity**. For a new category, choose the **Tracking Mode**: Quantity Based or Individual.
3. Optional: **Vendor**, **Invoice Number**, **Purchase Date**, **Unit Cost**, **Total Cost**, **Condition** (New, Second Hand, Refurbished or Repaired) and **Notes**.
4. Attach the **DN/Invoice/Receipt** document. This is required.
5. For individual tracking, enter each item's **Serial Number**.
6. Click **Create Stock In**.

The available quantity increases. The **Stock In History** table lists every entry.

Asset Dispatch (Stock Out)

Open **Returnable Assets** → **Stock Out**. Tabs: **Pending**, **Ready**, **Rejected**, **Draft ADN**, **Issued ADN**, **Delivered ADN**.


Asset requests come from Site Engineers after the Project Manager approves them.

How to handle an asset request:

1. In **Pending**, open **Details** to check the request.
2. Click **Approve** on the row. Stock is checked; if it is not enough you see "Insufficient stock". Or click **Reject** on the row and enter a reason.
3. The Site Engineer is notified.

How to create and dispatch an Asset Delivery Note (ADN):

1. In **Ready**, click **Create DN** on the request.
2. Check the project and site location. Choose **Attention To** (the Site Engineer).
3. Enter **Vehicle Number**, **Driver Name**, **Driver Contact** and the transport fee.
4. Select the items:
   - quantity-based assets with their quantity;
   - individual assets by serial number.
5. Add notes and click **Create Delivery Note**. The ADN is created as a draft and the request shows **Dispatched**.
6. In **Draft ADN**, click **Dispatch** on the ADN and confirm. There is no Issue step: the ADN goes from **Draft** straight to **In Transit**. Stock is deducted and the Site Engineer is notified. In-transit ADNs are listed under **Issued ADN**.
7. The Site Engineer receives the assets on site. The ADN becomes **Delivered** and the request **Completed**.

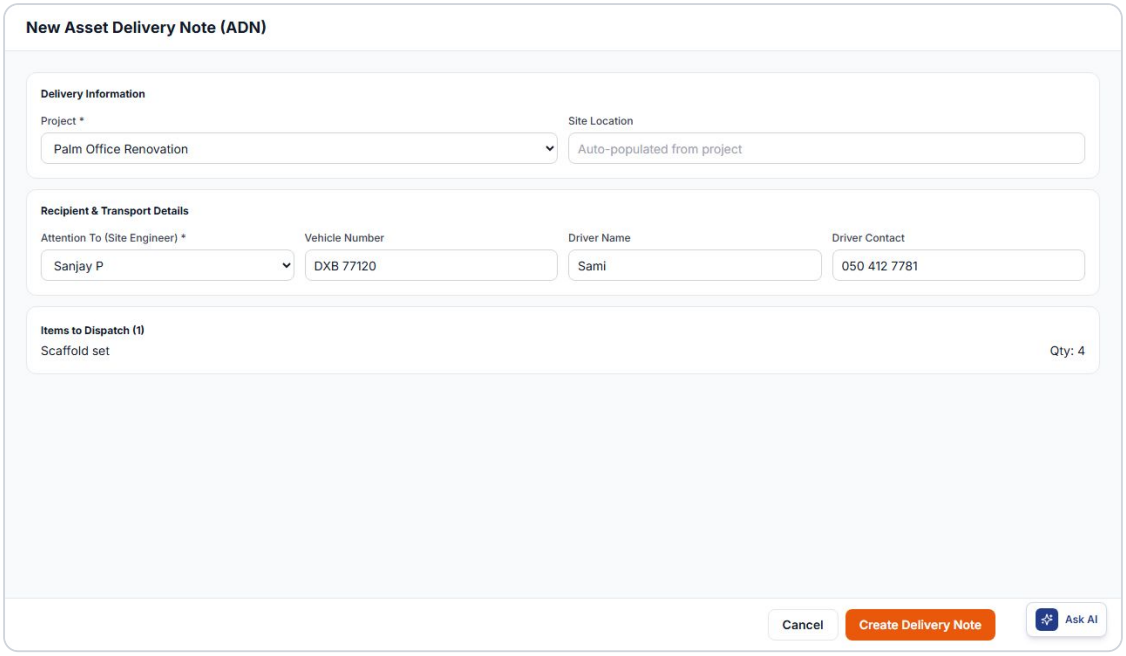


New Asset Delivery Note (ADN)

How to process returned assets

1. Open **Returnable Assets** → **Process Returns**. The tabs are **Pending** and **History**.
2. When a return is **In Transit**, click **Receive**.

3. Click **Process**. For each item set the **Verified Condition** (OK, Damaged, Needs Repair or Lost), add notes, and choose the **Action**:
    - **Return to Stock**: available quantity goes up.
    - **Send to Repair**: listed under Repair.
    - **Dispose** or **Write Off**: sent to the TD for approval.
4. Click **Process All Items**.

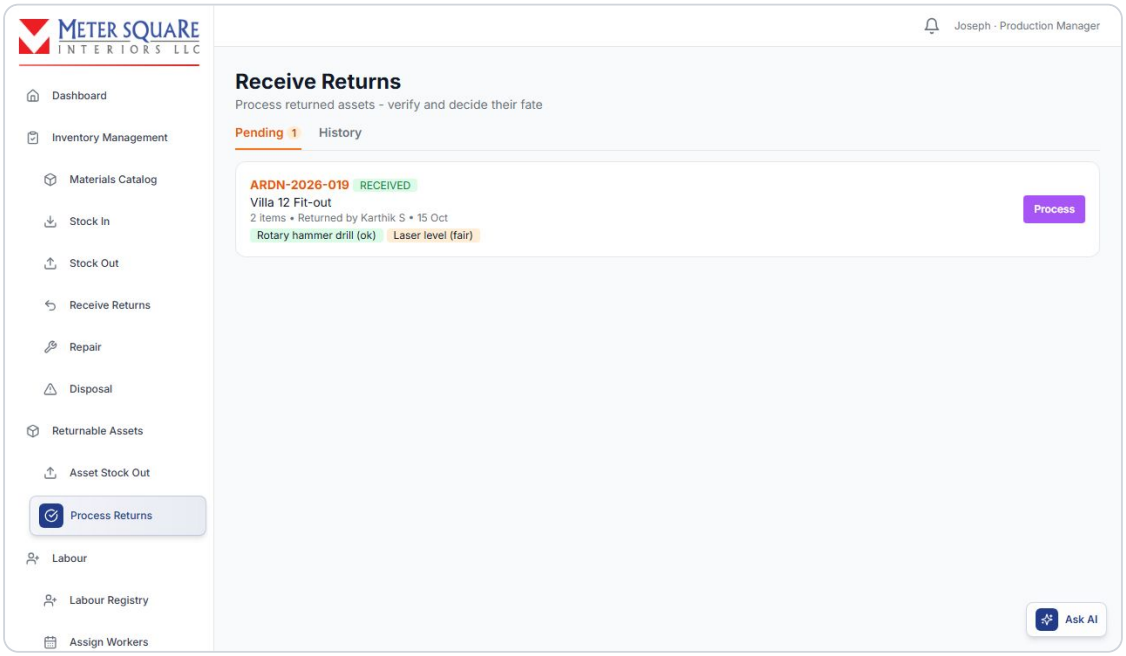

Receive Returns for assets

Asset Repair and Disposal


- **Repair** (Pending, History):
    - **Mark as Repaired** → **Confirm Repair** returns the asset to stock.
    - **Cannot Repair - Dispose** needs a reason and justification, with an optional photo. It is sent to the TD.
- **Disposal**: view-only. It shows **Pending TD Approval** and **TD Approved - Ready for Disposal**.
    - When the TD approves, the asset is removed from inventory.
    - When the TD rejects, it goes back to stock or to repair.

Labour Registry

Open **Labour** → **Labour Registry** to manage workers.

- Search, and filter by status (Active, Inactive, On Leave) and skill.

- Click **Add Worker** and fill in:
  - **Worker Code** (leave blank to generate one, for example WRK-006)
  - **Full Name**
  - **Phone** (used for WhatsApp)
  - **Hourly Rate (AED)**
  - **Skills**
  - **Worker Type** (Regular, Contract or Temporary)
  - **Status**
  - ID Number, Emergency Contact and Notes
- Use the row icons to view, edit or delete a worker. Deleting marks the worker as terminated.

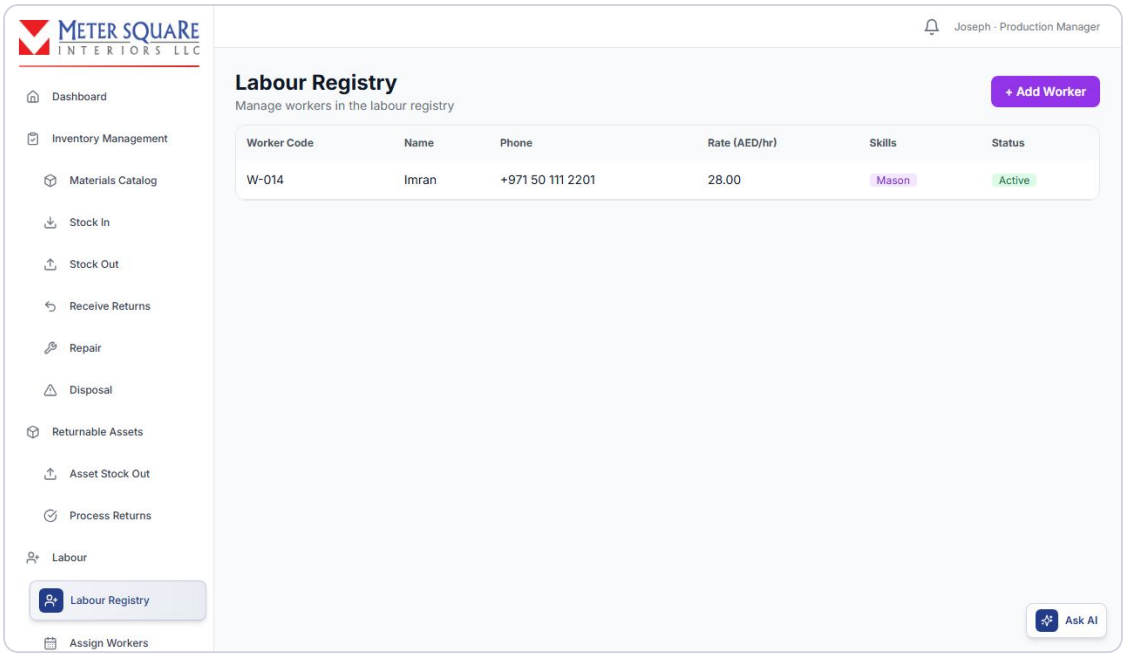

Labour Registry

Assign Workers


Open **Labour → Assign Workers**. The tabs are **Pending Assignment** and **Assigned**.

How to assign workers to a labour requisition

1. Click **Assign** on an approved requisition.
2. Select **exactly** the number of workers required.
   - Preferred workers are selected automatically.
   - Shortcut buttons: **Low Rate**, **High Rate**, **Single Skill**, **Multi Skill**.

- Workers already booked on another project are blocked.
- Use **Add New Worker** to add someone on the spot.

3. Click **Assign Selected**.
4. Enter the transport details: **Driver Name**, **Driver Contact**, **Vehicle Number** and the transport fee.
5. Check the workers to be notified, then click **Confirm & Send**.

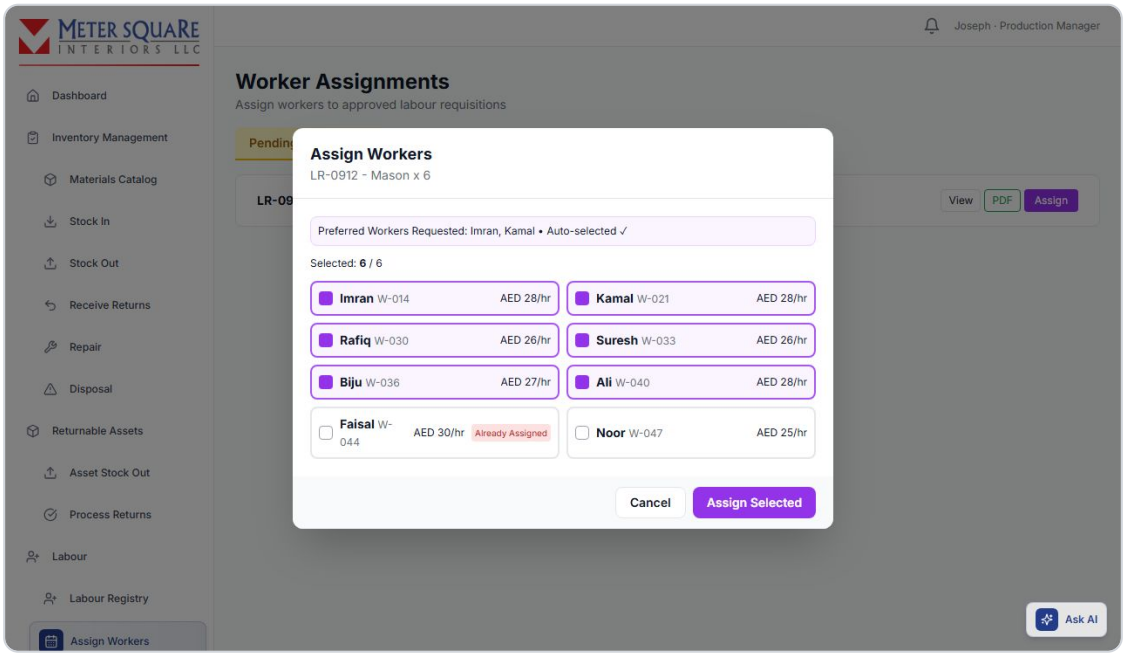

Assign Workers

Each worker receives a WhatsApp message, and the Site Engineer can then confirm their arrival. The transport fee is added to payroll cost.

Choose a date and click **Download Daily Schedule** for a PDF of all assigned workers. Use **PDF** on a row for that requisition's report.

Assets and Labour: End-to-End Flows

These processes involve several roles. This chapter shows who does what, in order. The detailed steps are in each role's chapter.

Asset requisition: from request to return

1	Site Engineer	Requests assets (Site Assets, Request Asset, Submit Request). The request is saved as a Draft
2	Site Engineer	Clicks Send for Approval on the request, then Send to PM
3	Project Manager	Approves in Asset Requisition Approvals (or rejects with a reason)
4	Production Manager	Approves after checking stock (Returnable Assets, Stock Out)
5	Production Manager	Creates the Asset Delivery Note (ADN) and dispatches it
6	Site Engineer	Receives the assets on site (Receive Selected or Receive All)
7	Site Engineer	Returns assets with a return note, split by condition (Good, Fair, Poor, Damaged): Issue, then Dispatch
8	Production Manager	Verifies each item and chooses Return to Stock, Send to Repair, Dispose or Write Off
9	Technical Director	Approves or rejects any Dispose or Write Off

Key points:

- **Submit Request** only saves a **Draft**. The PM does not see it until you click **Send for Approval** and confirm with **Send to PM**.
- Only drafts and requests rejected by the PM can be edited and sent again. After a PM rejection the button reads **Resend**.
- A rejection by the store (Production Manager) is final. Create a new request if the assets are still needed.

- Stock is checked when the Production Manager approves. It is deducted when the ADN is dispatched, or when the request is dispatched directly without an ADN.
- When returning, the Site Engineer splits the quantity by condition: **Good**, **Fair**, **Poor** or **Damaged**.
- The Production Manager verifies each item as **OK**, **Damaged**, **Needs Repair** or **Lost**, then chooses **Return to Stock**, **Send to Repair**, **Dispose** or **Write Off**.
- **Dispose** and **Write Off** go to the TD for approval. Stock is reduced only when the TD approves. If the TD rejects, the asset goes back to stock or to repair.

Labour: from requisition to payroll

1	**Production Manager**	Keeps the Labour Registry of workers up to date
2	**Site Engineer**	Creates a labour requisition and clicks Send to PM
3	**Project Manager**	Approves it (or rejects with a reason)
4	**Production Manager**	Assigns exactly the number of workers needed (Assign Workers)
5	**System**	Workers receive a WhatsApp message with the job details
6	**Site Engineer**	Marks arrivals (Arrived, Late Arrival, No Show) and clocks workers out
7	**Project Manager**	Reviews and locks the attendance (Attendance Lock)
8	**Admin**	Views and exports payroll for the period (Payroll Processing)

Key points:

- A Project Manager can also create a labour requisition and click **Send to Production** directly.
- Clocking a worker out creates their attendance record for the day.
- Only **locked** attendance reaches payroll.

- Overtime is time worked after the shift end time (or after 8 hours if no shift was set). It is paid at 1.5 times the hourly rate.
- The transport fee entered when workers are assigned is added to the project's labour cost.

Material returns from site

1 **Site Engineer**	Selects returnable materials and splits them by condition (Good, Damaged, Defective)
2 **Site Engineer**	Creates the Return Delivery Note (RDN), issues and dispatches it
3 **Production Manager**	Confirms receipt at the M2 Store
4 **Production Manager**	Good items go to stock, Damaged or Defective items go to repair or disposal
5 **Technical Director**	Approves or rejects disposals (a rejected disposal goes to backup stock)

Vendor delivery problems

1 **Production Manager**	Inspects the vendor delivery and rejects some or all materials with evidence
2 **Procurement**	Creates a return request: Refund, Replacement or New Vendor
3 **Technical Director**	Approves the return request
4 **Procurement**	Returns the material and confirms the refund, replacement, or new vendor purchase

Glossary and FAQ

Glossary

Term	Meaning
BOQ	Bill of Quantities: the detailed list of items, materials, labour and prices for a project
Sub-item / Scope	A part of a BOQ item with its own quantity, unit and rate
Preliminaries	General project conditions and costs (approvals, site setup and similar) selected in the BOQ
Internal BOQ	The full BOQ with costs, overheads and profit margins (for internal use)
Client BOQ	The BOQ with final prices only, as sent to the client
O&P	Overhead and Profit percentage
Revision (R1, R2…)	A changed version of a BOQ requested by the client
Internal revision	A BOQ corrected after the TD rejected it
CR / Material Purchase / Purchase Request	A request for extra materials on an approved project (shown as PO-… or EM-…)
PO-x.1, PO-x.2	Parts of one purchase split across different vendors
LPO	Local Purchase Order: the purchase order PDF sent to the vendor
VRR	Vendor Return Request: a request to return rejected materials to a vendor
M2 Store	The company warehouse. All purchased materials pass through it.
IMR	Internal Material Request: a request for materials from the M2 Store
DN / MDN	Material Delivery Note: the document for materials sent from the store to site
RDN	Return Delivery Note: the document for materials returned from site to the store
ADN	Asset Delivery Note: the document for assets sent to site
Current stock	Usable stock in the M2 Store

Term	Meaning
Backup stock	Damaged or partly usable stock, for example items waiting for repair
Returnable assets	Tools and equipment that go to site and come back
Fresh role	Temporary access to another role starting with no projects
Same as existing user	Temporary access with the same data as another holder of the role

Frequently asked questions

I cannot sign in. It says "Email not found".

Check that you selected **your own role** in **Select Your Role**. The message also appears when the role does not match, or when your account is inactive. If you were given a temporary role, you can choose that role too (except Site Engineer: sign in with your own role and switch).

I did not receive the OTP email.

Wait a minute and check your spam folder. After 30 seconds you can click **Resend OTP**. The code expires after 5 minutes.

My account is locked.

After 5 wrong codes, the account is locked for 30 minutes. Wait and try again, or ask your Admin.

Why did I get a notification but no email?

Emails for most workflow steps are sent only when you are **offline**. If you are online, you get the notification in the app. Set your status in the account menu.

Where do I see what I need to do?

Your **Dashboard** shows pending items for your role, and the bell icon shows notifications. Click a notification to go to the related page.

How do I switch to a role someone gave me?

Open the account menu at the bottom of the sidebar. Under **SWITCH ROLE**, click the role. See "Working in more than one role" in Getting Started.

Why can't I see the Role Access menu?

Only users whose own role is Admin or Technical Director can use it. Admin and TD both find **Role Access** as its own item in their sidebar.

- A TD working in a granted role does not see the menu item.
- A user working in a granted Admin role still sees **Role Access** in the menu. The page itself is available only in your own Admin or Technical Director role.

Switch back to your own role from the amber banner to use it again.

Why does a material request go to the Estimator?

The Estimator must price **new materials**. A request goes to the Estimator when:

- it has materials added with **Add New**, either **From Catalogue** or **Enter Manually**. Catalogue materials count as new because they are not in the BOQ.
- it has a BOQ material whose BOQ quantity is already used up or exceeded by earlier requests.
- the Project Manager chooses to send it to the Estimator.

Requests with only existing BOQ materials, within the BOQ quantity, go to a buyer.

One request holds either existing BOQ materials (**Select Material**) or new materials (**Add New**), not both. To request both kinds, create two requests.

Why is the Approve button disabled on a material request?

There is not enough stock in the M2 Store for that request. Stock in the vendor delivery first, or wait for the purchase.

Can materials be delivered directly from the vendor to site?

No. All purchased materials go to the M2 Store first, where the Production Manager inspects them and then dispatches them to site with a Delivery Note.

What happens if the vendor delivers wrong or damaged material?

The Production Manager rejects it at inspection with evidence. Procurement then creates a return request (Refund, Replacement or New Vendor), which the TD approves.

How do I return unused material from site?

The Site Engineer opens **Material Receipts** → the **Materials** tab → **Returnable Materials**. Click **Select Materials** on the project, split the quantities by condition, then click **Create RDN**. Issue and dispatch the RDN.

Why doesn't attendance show in payroll?

Only attendance that the Project Manager has **locked** appears in **Payroll Processing**. Ask the PM to lock it in **Labour** → **Attendance Lock**.

How do I report a problem with MeterSquare?

Open the account menu → **Support** → **New Ticket**, attach a screenshot, and submit.

Can Structo (Ask AI) change my data?

No. Structo, opened with the **Ask AI** button, only answers questions about how to use MeterSquare, from this guide. It cannot see or change projects, BOQs or any records.
